
PMP®敏捷部分测试题（一）

注意事项

1. 本套测试题共有 180 道单选题，测试时间为 3 个小时，**闭卷答题！**正确率要求答对 126 题（70%）或以上。
2. 本套测试题尽可能地覆盖 PMP 考试的题型，请学员们集中精力在 3 个小时内完成，达到全真的模拟效果
3. 模拟考试过程中，调整思维，揣摩考题的意图；考试结束后，认真总结。
4. 解题策略：TKSC 策略

T（topic）真正读懂题目

K（key）迅速抓住考点

S（source）准确找到出处

C（choice）果断做出选择

1. The velocity of a sprint is lower than expected. What should an agile team member do?

- A. Limit communication between the team members and the customer to prevent unnecessary anxiety.
- B. Manage communication to reset expectations with the appropriate team members and stakeholders.
- C. Manage communication between a few team members and the customer so that they may convey information to other team members.
- D. Facilitate one-on-one communication between team members to reduce conflict and inefficiencies.

1. Sprint 的速度低于预期，敏捷团队成员应该怎么做？

- A. 限制团队成员和客户之间的沟通，以防止不必要的焦虑。
- B. 管理沟通，以重置相应团队成员和干系人的期望。
- C. 管理几名团队成员和客户之间的沟通，让他们可以将信息传达给其他团队成员。
- D. 引导团队成员之间的一对一沟通，以减少冲突和低效率。

2. Senior executives wish to forecast the company's future growth based on a lifesaving product under development by an agile team. Executives want to demonstrate the product's features and functionality at the next shareholder meeting.

What should the agile practitioner do?

- A. Invite shareholders to the daily stand up meetings.
- B. Provide demonstrations for senior executives.
- C. Share, publish, and update a product roadmap and story map for shareholders.
- D. Invite senior executives to the daily stand up meetings.

2. 高层管理人员希望基于一个由敏捷团队正在开发的救生产品来预测公司的未来发展。高管们希望在下次股东大会上演示产品的特性和功能。敏捷管理专业人士应该怎么做？

- A. 邀请股东参加每日站立会议。
- B. 向高层管理人员提供演示。
- C. 为股东分享、发布和更新产品路线图和故事地图。
- D. 邀请高层管理人员参加每日站立会议。

3. Team members disagree about how to approach a user story, so it remains incomplete. The agile team lead learns about this issue during the stand up meeting. What should the agile team lead do?

- A. Have the manager determine the best approach to use for the user story.
- B. Ask the proper stakeholder to provide clarification to the team so the team can reach consensus.
- C. Use this opportunity to empower the team lead to choose the best approach.
- D. Request an informal report on the different approaches and then select the best one.

3. 团队成员对如何处理用户故事意见不一致，因此用户故事仍不完整。敏捷团队领导在站会上了解到这个问题。敏捷团队领导应该怎么做？

- A. 让经理确定用户故事的最佳使用方法。

-
- B. 要求合适的干系人向团队提供澄清，以让团队能够达成一致意见。
 - C. 利用这个机会让授权团队领导选择最好的方法。
 - D. 要求对不同方法请求非正式报告，然后选择最佳的方法。

4. An agile project team requires a new, custom tool for integration as a project component. The team hires a contractor to create the tool. How should the project team plan and monitor the contractor's work?

- A. By ensuring the contractor submits a project plan and status reports
- B. By using a sprint backlog and retrospective meetings
- C. By using the product backlog and daily stand up meetings
- D. By ensuring daily task plans are created and status updates are communicated clearly

4. 敏捷项目团队需要一个新的项目组件的集成工具。项目团队应如何计划和监督分包商的工作？

- A. 通过确保分包商提交项目计划和状态报告。
- B. 通过使用 sprint 待办事项和回顾会议。
- C. 通过使用产品待办事项列表和每日站会。
- D. 通过确保创建每日任务计划并明确沟通状态更新。

5. During a presentation, stakeholders want to know what product features will be delivered in the near future. In addition, one stakeholder wants to demonstrate that the project can adapt to scope changes. What information radiators should be used?

- A. Cumulative flow diagram and burn down chart
- B. Product roadmap and burn up chart
- C. Cumulative flow diagram and product roadmap
- D. Story map and burn up chart

5. 在演示过程中，项目干系人想知道在不久的将来将交付什么样的产品特性。此外，一名项目干系人希望证明项目可以适应范围变更。应使用什么信息发射源？

- A. 累计流量图和燃尽图。
- B. 产品路线图和燃起图。
- C. 累计流量图和产品路线图。
- D. 故事地图和燃起图。

6. In which situation would the development team need to review the definition of done with the product owner?

- A. The team fails to create artifacts for the sprint.
- B. The team fails to complete all user stories in the sprint cycle.
- C. The customer requests changes at the end of a sprint cycle.
- D. The customer requests early delivery of a product feature.

6. 在哪种情况下，开发团队需要与产品负责人一起审查已完成的定义？

- A. 团队无法为 sprint 创建工作件。
- B. 团队无法在 sprint 周期中完成所有用户故事。
- C. 客户在 sprint 周期结束时请求变更。
- D. 客户要求提前交付一个产品特性。

7. An organization is undergoing a transformation from waterfall to agile development. The organization plans to adopt a “hybrid agile” development process incrementally. A project manager is hired to lead the organizational transformation and product development. What should the project manager do next?

- A. Build a work authorization and work breakdown structure (WBS).
- B. Avoid micro-management and overhead.
- C. Engage with stakeholders and tailor the process.
- D. Form small working groups and silos.

7. 组织正在经历从瀑布模式到敏捷开发的转变。该组织计划逐步采取“混合敏捷”开发过程。项目经理受聘来领导组织转变和产品开发。项目经理下一步该怎么做？

- A. 建立工作授权和工作分解结构（WBS）。
- B. 避免微观管理和日常管理。
- C. 让干系人参与，并定制过程。
- D. 形成小工作组和孤岛。

8. An agile team is meeting its commitments but feels that velocity could be improved. How can the team members accomplish this?

- A. Pull simpler stories into the sprint.
- B. Reduce non-productive time.
- C. Move user stories to another sprint.
- D. Identify key processes to improve.

8. 敏捷团队履行其承诺，但感觉能够提高速度。团队成员如何能够实现这一点？

- A. 将较为简单的故事拉近 Sprint 中。
- B. 减少非生产性时间。
- C. 将用户故事移到另一个 Sprint。
- D. 识别关键过程以改进。

9. A business owner asks an agile practitioner to provide a central place where stakeholders can find information about a project’s progress. What should the agile practitioner recommend?

- A. Regular circulation of updated, detailed versions of the project plan
- B. Maintain an online team collaboration site and redirect the business owner to the same
- C. Regular one-on-one meetings with stakeholders
- D. Daily scrum meetings with stakeholders

9. 业务负责人要求敏捷管理专业人士提供一个中心位置，让项目干系人可以查找项目进展的相关信息。敏捷管理专业人士应提供什么建议？

- A. 定期循环更新项目计划的详细版本。
- B. 维护在线团队协作网站，并将业务负责人重新定向到相同的网站。
- C. 与项目干系人定期举行一对一会议。
- D. 与项目干系人举行每日 scrum 会议。

10. Members of an agile team identify that the daily stand up meeting is not adding value because the group is too large. During a retrospective, they raise some ideas

about breaking the project team into smaller groups. What should the scrum master do?

- A. Reduce the size of the team to make the stand up meeting more manageable.
- B. Seek direction from the project sponsor before taking action.
- C. Inform the team of the value of the stand up meeting.
- D. Allow the team to make the decision to reorganize.

10. 敏捷团队成员认为每日站会并不会增加价值，是因为小组规模太大。在回顾会议上，他们提出将现有的项目团队分解成更小的小组。Scrum 主管应该怎么做？

- A. 缩小团队规模，使站会更易于管理。
- B. 在采取行动之前寻求项目发起人的指示。
- C. 告知团队站会的价值。
- D. 允许团队做出重组的决定。

11. Which of the following should be used to facilitate continuous improvement for an agile project team during an iteration?

- A. Iteration retrospective
- B. Iteration planning
- C. Daily stand up meeting
- D. Continuous integration

11. 下列哪一项可用于促进敏捷项目团队在迭代期间的持续改进？

- A. 迭代回顾。
- B. 迭代计划。
- C. 每日站立会议。
- D. 持续集成。

12. A product owner is working on a project with two stakeholders who have opposing requirements. The product owner is unsure of which user stories to write and wants to involve an agile coach. What should the agile coach do first in this scenario?

- A. Oversee subject matter experts (SMEs) who will user stories
- B. Request the sponsor to facilitate a story-writing workshop
- C. Begin independently writing user stories using journey maps
- D. Organize a story-writing workshop with the team to define the requirements

12. 产品负责人正在从事一个项目，但其中两名项目干系人的需求相反。产品负责人不确定要编写哪些用户故事，并希望让一名敏捷教练参与。在这个情景中，敏捷教练首先应该怎么做？

- A. 监督将编写用户故事的主题专家（SME）。
- B. 请求项目发起人安排召开一次故事编写研讨会。
- C. 开始使用旅程图独立编写用户故事。
- D. 与团队安排一次故事编写研讨会，定义需求。

13. A team agrees during an iteration planning meeting that making certain changes to a feature will add product value. The changes, however, will affect the schedule because they require extra work. What should the agile team lead do next?

- A. Discuss impact of changes with the product owner and then proceed.

B. Include a many of the changes as possible while complying with the initial schedule.

C. Complete the product using the initial plan.

D. Form a re-estimation of the project.

13. 在一次迭代计划会议上，团队同意对某项特性进行某些变更将增加产品价值。然而，由于这些变更需要额外工作，将影响进度计划。敏捷团队领导下一步应该怎么做？

A. 在产品负责人讨论变更的影响，然后继续执行。

B. 包含尽可能多的变更，同时遵守初始进度计划。

C. 使用初始计划完成该产品。

D. 形成一份项目的重新估算。

14. An agile team's backlog contains a large numbers of work items targeted for a release. The product owner is concerned that the work items will not be delivered on time. What recommendation should the agile practitioner provide to the product owner?

A. Facilitate a meeting with stakeholders to determine the value-added items, and reprioritize the backlog.

B. Facilitate a meeting with the agile team to determine which work items require less implementation effort.

C. Ask the business sponsor for more agile-team resources.

D. Speak with the customer about changing the release date.

14. 一个敏捷团队的待办事项包含大量针对某个版本的工作项。产品负责人担心这些工作项无法按时交付。敏捷管理专业人士应向产品负责人提供什么建议？

A. 引导一次与项目干系人的会议，确定增值工作项，并对待办事项重新排列优先顺序。

B. 引导一次与敏捷团队的会议，确定哪些工作项需要较少的实施工作。

C. 向业务发起人请求获得更多敏捷团队资源。

D. 与客户讨论变更发布日期。

15. A company executive asks an agile practitioner for recommendations to ensure that stakeholders completely understand the product goals. What should the agile practitioner recommend?

A. Communicate the product business plan

B. Conduct a meeting with key stakeholders

C. Invite stakeholders to a sprint planning meeting

D. Develop a product vision

15. 一名公司高管要求敏捷管理专业人士提供建议确保项目干系人完全理解产品目标。敏捷管理专业人士应提供什么建议？

A. 沟通产品业务计划。

B. 与关键干系人一起召开会议。

C. 邀请项目干系人参加 sprint 规划会议。

D. 制定产品愿景。

16. Subject matter experts (SMEs) on an agile team are experiencing low motivation due to performing the same tasks repetitively. Which action should the agile practitioner take?

-
- A. Increase the number of resources on the team to assist the SMEs with the tasks.
 - B. Have team members conduct a value stream analysis of their activities.
 - C. Plan a team-building exercise to increase the team's morale.
 - D. Facilitate pair programming so that the SMEs develop new skills.

16. 由于一直重复执行相同的任务，一个敏捷团队的主题专家（SME）士气低落。敏捷管理专业人士应采取哪一项行动？

- A. 增加团队的资源数量，协助主题专家完成任务。
- B. 让团队成员执行其活动的价值流分析。
- C. 计划一次团队建设活动以提高团队的士气。
- D. 引导结对编程，让主题专家培养新的技能。

17. What should an agile practitioner do to maintain a visible, monitored, and prioritized list of risks and issues?

- A. Conduct team building exercises, risk reviews, and iteration retrospectives.
- B. Use information radiators, daily stand up meetings, and planning sessions.
- C. Ensure that the project has comprehensive documentation.
- D. Ensure that the risk and issues logs are maintained.

17. 敏捷管理专业人士应该怎么做以获得一份可视的、可监控的并具有优先顺序的风险和问题清单？

- A. 开展团队建设活动、风险评审和迭代回顾。
- B. 利用信息辐射体、每日站立会议和规划会议。
- C. 确保项目具有全面的文档。
- D. 确保具有风险和问题日志。

18. A customer has a new user interface (UI) technology. This technology, however, causes the implementation team's productivity to decrease. What should the agile team lead do to increase productivity?

- A. Request the customer to identify the risks associated with adopting new technology.
- B. Recommend halting the iteration since the team is underperforming.
- C. Schedule additional training for the team.
- D. Increase the number of specialists on the team.

18. 一名客户拥有新的用户界面（UI）技术。然而，这项技术导致实施团队的生产力下降。若要提高生产力，敏捷团队领导应该怎么做？

- A. 要求客户识别采用新技术带来的相关风险。
- B. 建议停止迭代，因为团队表现不佳。
- C. 为团队安排额外的培训。
- D. 增加团队中的专家数量。

19. A senior executive, who is also the escalation contact, joins an agile team during production go-live. Prior to the next sprint, the executive asks the team about features that should be included. What meeting should the executive have attended?

- A. Retrospective
- B. Daily scrum
- C. Sprint review


D. Sprint planning

19. 一名高管，也是上报升级的联系人，在生产启动期间加入一个敏捷团队。在下一个 sprint 之前，该高管向团队询问应包含的特性。该高管应已参加什么会议？

- A. 回顾会议。
- B. 每日 scrum 会议。
- C. Sprint 评审会议。
- D. Sprint 计划会议。

20. Based on this burn down chart, how should an agile project manager evaluate the iteration's current status?

- A. The team is progressing well, and there have been no roadblocks.
- B. The team made scope changes to get back on track.
- C. The team maintained effort and made no changes.
- D. The team needs assistance to meet the plan.

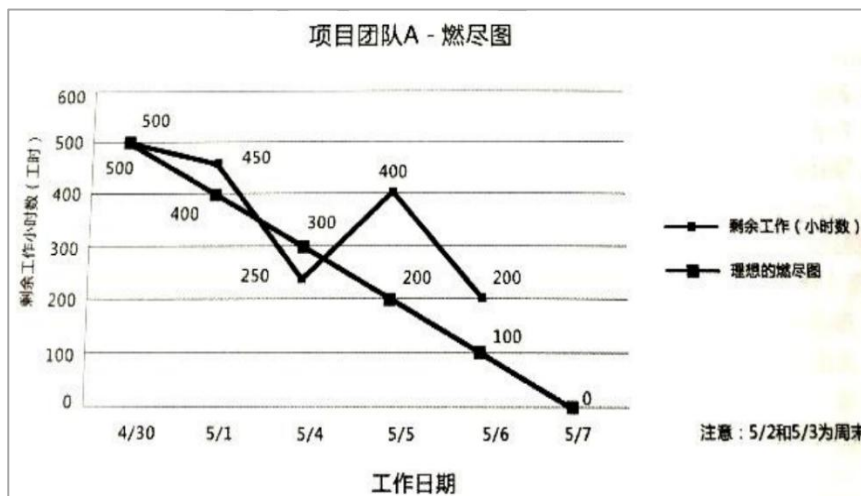

20. 基于此燃尽图，一个敏捷项目经理应如何评估迭代的现状？

- A. 团队进展顺利，没有任何障碍。
- B. 团队进行范围变更以恢复正轨。
- C. 团队保持努力，不作任何变更。
- D. 团队需要协作，满足计划。

21. A team member located outside of the country recommends a new, web-based conferencing application that will improve communication at no extra cost. The local team objects to the application and prefers to meet face-to-face. What should the agile practitioner do?

- A. Encourage the team to experiment with the new application and then re-evaluate it.
- B. Explain that the new application is not approved by all team members and discuss alternative solutions.
- C. Determine what application is best for the team.
- D. Ask the product owner to decide what application is best for the team.

21. 一名位于国外的团队成员推荐一种新的、基于网络的会议应用程序，将在不生产额外成本的情况下改善通信。但本地团队反对应用程序，并倾向于面对面会议。敏捷管理专业人士应该怎么做？

-
- A. 鼓励团队尝试新的应用程序，然后重新评估该程序。
 - B. 解释新的应用程序未被所有团队成员批准并讨论替代解决方案。
 - C. 确定什么应用程序最适合团队。
 - D. 要求产品负责人决定哪个应用程序最合适团队。

22. An agile team is taking longer cycles to develop features. Increased cycle time is leading to poorer quality. Which law should the team apply to improve quality?

- A. Lean lead time law
- B. Law of diminishing returns
- C. Little's law
- D. Parkinson's law

22. 敏捷团队正在花较长的周期来开发功能。增加周期时间导致质量较差。团队应当应用哪项法则改进质量？

- A. 精益交付时间法则。
- B. 收益递减定律。
- C. 利特尔法则。
- D. 帕金森定律。

23. An agile team suggests ideas for improving performance. but the agile team lead is aware of better method. What should the agile team lead do?

- A. Encourage the team to explore more ideas for improvement.
- B. Explain the better method to the team and have them use it.
- C. Display servant leadership by seeking guidance from the project sponsor.
- D. Compromise by using both the product team's idea and the better method.

23. 敏捷团队提出改进绩效的建议，但是敏捷团队领导了解到一个更好的方法。敏捷团队领导应该怎么做？

- A. 鼓励团队探讨更多改进建议。
- B. 向团队说明更好的方法，并让他们使用该方法。
- C. 通过向项目发起人寻求指导，展示服务型领导能力。
- D. 通过同时使用产品团队的建议和更好的方法来折中。

24. While working on a user story in a sprint, a team member comes up with an idea for adjusting an organizational process in order to maximize value delivery. What is the best time to propose this idea to the team?

- A. During the next sprint planning session
- B. During the next daily scrum
- C. During the project status meeting
- D. During the sprint retrospective

24. 在处理一个 sprint 的用户故事时，团队成员提出了调整组织过程实现价值交付最大化的想法。向团队提出这个想法的最佳时机是什么？

- A. 在下一次 sprint 规划会议上。
- B. 在下一次每日 scrum 期间。
- C. 在项目状态会上。
- D. 在 sprint 回顾会议上。

25. Business owners are trying to decide if agile methodologies should be adopted for their next project. What should the agile practitioner do?

- A. Inform them that agile methodologies are effective for all projects.
- B. Present them with core agile principles, linking business goals and customer needs.
- C. Ask them to review recommended agile books before making a decision.
- D. Demonstrate to them the increased revenue and reduced costs associated with agile projects.

25. 业务负责人正在尝试决定是否应该为他们的下一个项目采用敏捷方法。敏捷管理专业人士应该怎么做？

- A. 告知他们敏捷方法对所有项目都有效。
- B. 向他们提供核心敏捷原则，将业务目标和客户需求联系起来。
- C. 让他们在做出决定之前查看推荐的敏捷图书。
- D. 向他们展示敏捷项目可以增加收入并且减少成本。

26. A project is behind schedule based on actual versus planned velocity. Where should an agile practitioner look to remove the waste?

- A. Product roadmap
- B. Burn down chart
- C. Burn up chart
- D. Value stream map

26. 根据实际速度与计划速度的对比，项目落后于计划。敏捷管理专业人事应在哪里查看消除浪费的时间？

- A. 产品路线图。
- B. 燃尽图。
- C. 燃起图。
- D. 价值流图。

27. Trend analysis shows that velocity is significantly lower than predicted and the release will be completed a month behind schedule. The team recommends changing the end date to reflect this. What should the agile practitioner do?

- A. Announce that the team has not exceeded the predicted velocity, but that the end date will remain the same.
- B. Ask the scrum master to reduce additional features in the product backlog. Then re-plan subsequent iterations.
- C. Meet with the business owner to determine whether to reduce scope or add time.
- D. Ask the team to increase velocity to meet contractual obligations, and document this decision.

27. 趋势分析显示，速度显著低于预期，版本完成日期将落后于进度计划一个月。团队建议更改结束日期以反映这一点。敏捷管理专业人士应该怎么做？

- A. 宣布团队没有超过预测速度，但结束日期将保持不变。
- B. 要求 scrum 主管减少产品待办事项中的额外特性，然后重新计划后续迭代。
- C. 与业务负责人联系以确定是减少范围还是增加时间。
- D. 要求团队提高速度以满足合同中的义务，并记录此决定。

28. Due to lengthy technical explanations for implemented features, the last two demos took longer than scheduled. What should the agile practitioner do?

- A. Remind the team and the stakeholders that two hours is the maximum length for a review meeting.
- B. Shorten regular iteration durations, have more frequent review meetings, and discuss less new functionality per meeting.
- C. Coach the product owner and team to timebox future review meetings, and remind them of their purpose.
- D. Organize refreshments for the next review meeting, and plan to have an intermediate break.

28. 由于对已实施特性的技术说明时间较长，最后两个演示花费的时间比计划长。敏捷管理专业人士应该怎么做？

- A. 提醒团队项目关系人评审会议的最长时间为两小时。
- B. 缩短定期迭代持续时间，更频繁地召开评审会议，并且在每次会议上较少讨论新功能。
- C. 教导产品负责人和团队确定未来评审会议的时间盒，并提醒他们这些会议的目的。
- D. 组织下一次评审会议的茶歇，并计划中间休息时间。

29. An agile practitioner shows that recent research indicates that a new technology, which will be used in the project, may have some issues on larger projects. What should the agile practitioner do?

- A. Plan a spike for the new risk.
- B. Include the new risk in the risk register.
- C. Assess the impact and probability with the team, and inform the stakeholders.
- D. Discuss the possible risk-response activities with team and include them in the backlog.

29. 敏捷管理专业人士声明，最近的研究表明即将用于项目的一项新技术可能在大型项目中有一些问题。敏捷管理专业人士应该怎么做？

- A. 为新风险计划一次探测。
- B. 将新风险包含在风险登记册中。
- C. 与团队一起评估影响和概率，并通知项目干系人。
- D. 与团队一起讨论可能的风险应对活动，并将其包含在待办事项中。

30. What should a development team do when they identify significant technical debt during a sprint?

- A. Dedicate the next iteration entirely to technical debt cleanup.
- B. Ask the customer to include incremental technical debt cleanup in future iterations.
- C. Discuss the technical debt in the next retrospective meeting.
- D. Capture the technical debt in the product backlog.

30. 开发团队在一个 sprint 期间识别到重大技术债务时应该怎么做？

- A. 在下一个迭代专注与技术债务清理。
- B. 要求客户在未来的迭代中包含增量技术债务清理。
- C. 在下次回顾会议中讨论技术债务。
- D. 在产品待办事项中收集技术债务。

31. During a project's first iteration, a newly formed agile team encounters major process issue. A team member suggests holding a retrospective to address these issues. What should the agile team lead do?

- A. Explain that a retrospective can only be held at the end of an iteration.
- B. Stop the iteration midway and hold the retrospective.
- C. Explain that the team is experiencing the storming stage and encourage them to work through it.
- D. Seek external assistance to help the team with the process issues.

31. 在项目的第一次迭代期间，一支新组建的敏捷团队遇到主要过程问题。一名团队成员建议召开一次回顾会议，解决这些问题。敏捷团队领导应该怎么做？

- A. 解释说回顾会议只能在迭代结束时举行。
- B. 在中途停止迭代，并召开回顾会议。
- C. 解释说团队正在经历震荡阶段，并鼓励他们设法克服这个问题。
- D. 寻求外部协助，帮助团队解决过程问题。

32. How should a team respond to a junior team member who recommends using a different method to accomplish a team goal?

- A. Have the project lead work with the team member to decide if the method should be adopted.
- B. Form a task group of senior team members to evaluate the method and to determine if it should be adopted.
- C. Communicate the idea to management and request to adopt the new method.
- D. Work as a group to determine if the method should be adopted.

32. 一名初级团队成员建议使用不同的方法来完成团队目标，团队应如何答复？

- A. 让项目领导与该团队成员一起决定是否应采用该方法。
- B. 组建一个由高级团队成员组成的任务组来评估该方法并确定是否应采用。
- C. 将该建议传达给管理层，并要求采用新方法。
- D. 群体决策是否应该采用该方法。

33. What should an agile team do after finding a new, high severity risk with a story?

- A. Add a goal to the current iteration to fully mitigate or control the risk.
- B. Ensure the story containing the risk is added to the backlog and prioritized.
- C. Maintain team velocity by continuing with the current plan.
- D. Promptly update the risk register, and request that a risk specialist be hired.

33. 发现故事存在一个新的高度严重风险后，敏捷团队应该怎么做？

- A. 对当前迭代添加一个目标，完成减轻或控制该风险。
- B. 确保将包含该风险的故事添加进待办事项并确定优先顺序。
- C. 通过继续当前计划保持团队速度。
- D. 及时更新风险登记册，并要求聘请一名风险专家。

34. During a retrospective meeting, a team develops a small list of initiatives. All will have a positive impact and improve team performance. What should the agile coach do next?

- A. Ask the team to develop the list into a longer set of initiatives before in
- B. Help the team create a high-level proposal of the initiatives to present

-
- C. Positively acknowledge the list and encourage the team to implement
 - D. Ask the team to choose and implement the most complex initiative.

34. 在回顾会议期间，一个团队制定了一份小的举措清单，所有这些都将产生积极的影响，并提高团队绩效。敏捷教练下一步应该怎么做？

- A. 要求团队在实施所有计划之前，将该清单制定成更长的举措列表。
- B. 帮助团队创建这些举措的高层建议书，提交给关键干系人。
- C. 积极认可这份清单，并鼓励团队实施这些计划。
- D. 要求团队选择并实施最复杂的计划。

35. The product owner is continuously listening to one stakeholder significantly more than the other stakeholders. What should the agile practitioner do?

- A. Allow the stakeholder and product owner to resolve the issue on their own.
- B. Schedule a private meeting with the stakeholder to clarify their needs.
- C. Speak with the product owner's direct manager.
- D. Instruct the team to follow the product owner's priorities.

35. 产品负责人一直听取一个项目干系人的意见，远远超过其他项目干系人。敏捷管理专业人士应该怎么做？

- A. 允许这名干系人和产品负责人自己解决问题。
- B. 与这名干系人安排一次私人会议，以澄清他们的需求。
- C. 与产品负责人的主管经理沟通。
- D. 指导团队遵循产品负责人的优先级。

36. What is the role of the facilitator during a retrospective meeting?

- A. To distribute pertinent documents, set the tone, and state the agenda
- B. To provide constant direction so that disputes are avoided
- C. To ensure that stakeholders are immediately made aware of feedback
- D. To monitor participation levels, ending the meeting if there are insufficient interactions

36. 在回顾会议上协调员（引导者）的角色是什么？

- A. 分发相关文件、设定基调并说明会议议程。
- B. 提供一致的会议方向，避免争议。
- C. 确保项目干系人立即获知反馈。
- D. 监督参与程序，如果交互不足，则结束会议。

37. When trying to predict a release date, What information should an agile team obtain from a burn down chart?

- A. The total amount of resources used in the sprint
- B. The total amount of remaining work, and how the project team is performing to date
- C. The total work effort for each team member, and who is falling behind
- D. A comparison of the total estimate of completed work to the estimate at completion (EAC).

37. 在尝试预测一个发布日期时，敏捷团队应从燃尽图中获得哪些信息？

- A. sprint 中使用的资源总量。
- B. 剩余工作的总量，以及项目团队到目前为止的表现如何。

- C. 每个团队成员的总工作量，以及谁落后了。
- D. 已完成工作的总估算与完工估算的（EAC）对比。

38. The company hires a project manager to coordinate an agile project with a tight deadline. Both the project manager and the agile team are managed by a portfolio manager who tends to reassign developers to other urgent matters as needed. When approached by the project manager, the portfolio manager insists that they have the authority to move resources as needed.


- A. Elevate the issue to the issue log
- B. Update the risk register
- C. Escalate the issue to the portfolio manager's supervisor
- D. Request additional resources

38. 公司聘用一名项目经理来协调一个期限紧迫的敏捷项目，项目经理和敏捷团队都由一位项目组合经理管理，该项目组合经理倾向于根据需要将开发人员重新分配给其他紧急事项，当项目经理与其接洽时，项目组合经理坚持认为他们有权根据需要调动资源，项目经理应该怎么做？

- A、将此问题提升为问题日志中的问题
- B、更新风险登记册
- C、将此问题升级上报给项目组合经理的主管
- D、请求额外的资源

39. What does the chart show?

- A. The team needs to hurry up in order not to fail this iteration.
- B. The team has removed scope.
- C. The iteration will need to be scoped up.
- D. The team is attaining a healthy velocity with small variations.

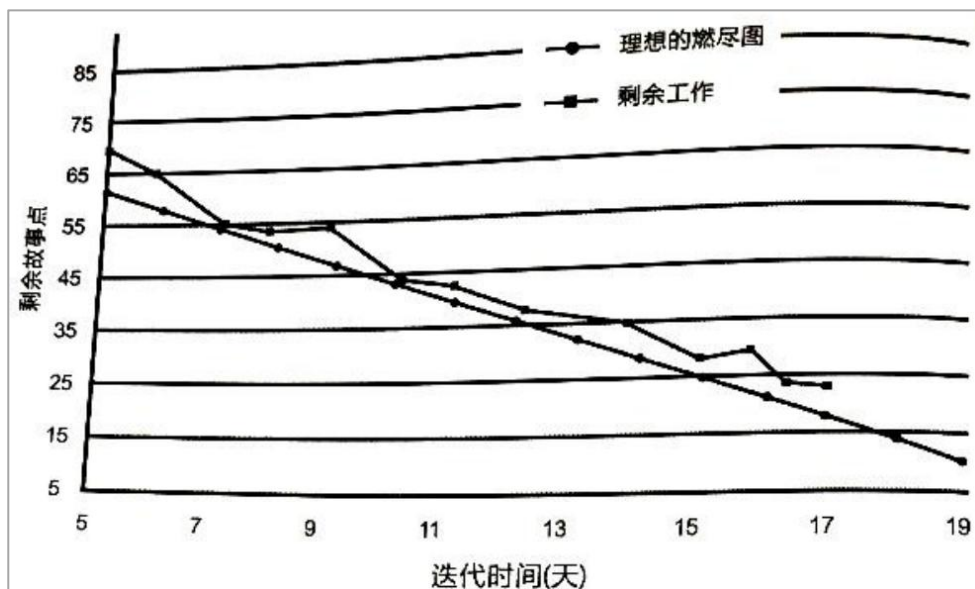

39. 这个图表说明什么？

- A. 团队需要加快速度，才能让这个迭代不失败。
- B. 团队已经删除范围。
- C. 迭代将需要增加范围。

D. 团队正在获得具有微小变化的健康速度。

40. Who should remove and document the impediments that emerge during a current sprint?

- A. Project manager
- B. Produce owner
- C. Agile team
- D. Scrum master

40. 在当前 sprint 中，谁应该移除和记录出现的障碍？

- A. 项目经理。
- B. 产品负责人。
- C. 敏捷团队。
- D. Scrum 主管。

41. An agile practitioner notices a new story on the product backlog that is vague and missing the acceptance criteria. At what point in the sprint cycle should the agile practitioner ask the product owner for more detail?

- A. During the backlog grooming meeting
- B. During the sprint retrospective
- C. During the daily scrum
- D. During the iteration review meeting

41. 敏捷管理专业人士需要注意到产品待办事项上一个新故事很模糊，缺少验收标准。敏捷管理专业人士应在 sprint 中的哪个时间点要求产品负责人提供更多详情？

- A. 在待办事项梳理会上。
- B. 在 sprint 回顾会议上
- C. 在每日 scrum 期间。
- D. 在迭代评审会上

42. Which method is critical when creating a minimum feasible product (MVP)?

- A. Smoke tests
- B. Demos
- C. Release by version
- D. Customer

42. 在创建最小可行产品（MVP）时，哪种方法至关重要？

- A. 冒烟测试。
- B. 演示。
- C. 按版本发布。
- D. 客户访谈。

43. An agile project team decides to adapt the testing process in use. In which session would this decision have arisen?

- A. Sprint retrospective
- B. Sprint review
- C. Release retrospective
- D. Sprint planning

43. 敏捷项目团队决定修改使用中的测试过程，这一决定在哪一次会议上产生的？

- A. sprint 回顾会议。
- B. sprint 审查会议。
- C. 发布回顾会议。
- D. sprint 计划会议。

44. After a recent company board meeting, stakeholders have changed their product vision and re-established project goals. What should the agile team lead do to communicate these changes to the team?

- A. Send an email to the team outlining the new product vision and goals.
- B. Start planning the next iteration based on the new product vision and goals.
- C. Update the release plan to reflect the new level of effort required to incorporate the new product vision and goals.
- D. Hold a project team meeting to provide transparent communication to ensure understanding of the new product vision and goals.

44. 在最近一次公司董事会之后，项目干系人改变了他们的产品愿景并重新确立项目目标，敏捷团队领导应该怎么将建议变更传达给团队？

- A. 向团队发送一封电子邮件，概述新产品愿景和目标。
- B. 根据新产品愿景和目标，开始规划下一次迭代。
- C. 更新发布计划，以纳入新产品愿景和目标所需的新投入水平。
- D. 召开项目团队会议，通过透明的沟通，确保了解新的产品愿景和目标。

45. During which meeting should an agile practitioner work with the team to share information about tasks, stories and commitments?

- A. Stakeholder priority
- B. Project status
- C. Sprint retrospective
- D. Stand up

45. 哪次会议期间，敏捷管理专业人士与团队合作，分享任务、故事和承诺相关的信息？

- A. 干系人优先级会议。
- B. 项目状态会议。
- C. sprint 回顾会议。
- D. 站会。

46. By whom should the success criteria be accepted?

- A. The agile project team
- B. The project management office (PMO)
- C. The product owner
- D. The agile project manager

46. 谁会接受成功标准？

- A. 敏捷项目团队。
- B. 项目管理办公室（PMO）。
- C. 产品负责人。
- D. 敏捷项目经理。

47. At what phase should an agile team establish sprint deliverables?

- A. Inception
- B. Planning
- C. Review
- D. Execution

47. 敏捷团队应该在什么阶段创建 sprint 可交付成果?

- A. 概念阶段。
- B. 规划阶段。
- C. 评审阶段。
- D. 执行阶段。

48. An agile team lead notices that a team member has decreasing performance levels and frequently arrives late to morning stand up meetings. Which solution should the agile team lead apply?

- A. Work closely with the team member to generate tangible ways to provide support.
- B. Facilitate proactive engagement and wait for the team member to request a meeting.
- C. Ask the team member to arrive to meetings on time.
- D. Discuss the issue at the retrospective with the team.

48. 敏捷团队领导注意到一名团队成员的绩效水平下降, 并且经常在早上的站会上迟到。敏捷团队领导应采取哪一种解决方案?

- A. 与该团队成员密切合作, 寻找具体的方式来提供支持。
- B. 引导主动参与并等待该团队成员发起一次会议。
- C. 要求该团队成员按时到达参加会议。
- D. 在回顾会议上与团队讨论这个问题。

49. When should a critical risk that is identified during a stand up meeting be discussed?

- A. Immediately at the same stand up meeting.
- B. During the retrospective meeting.
- C. At the bi-weekly risk assessment meeting
- D. After the stand up, during a separate meeting

49. 在一次站会上识别到的一项关键风险, 应在何时讨论?

- A. 在同一次站会上立即讨论。
- B. 在回顾会议上讨论。
- C. 在每两周举行的风险评估会议上讨论。
- D. 在站会后的一次单独会议上讨论。

50. During a retrospective, an agile team indicates that the iteration velocity forecast was unmet. While 19 points were planned, only 9 were completed. The team believe that 19 points are reasonable for the next iteration, but the agile practitioner disagrees. The shares that departmental meetings were a factor. What should the agile practitioner do?

- A. Tell the team that the next iteration's velocity estimate should be lowered.
- B. Ask the team to track non-project hours.
- C. Ask the team to work overtime to ensure that estimates are met.

D. Determine roadblocks that prevented the sprint success and mitigate them.

50. 在回顾会议上，一个敏捷团队表示无法满足迭代速度预测，虽然计划了 19 个点，但仅完成 9 个点。团队认为 19 个点对于下一个迭代是合理的，但是敏捷管理专业人士不同意，团队分享说部门会议是一个影响因素。敏捷管理专业人士应该怎么做？

- A. 告诉团队应降低下一次迭代的速度估算。
- B. 要求团队跟踪非项目时间。
- C. 要求团队加班工作，确保满足估算。
- D. 确定阻止 sprint 成功的障碍，并减轻这些障碍。

51. When should the agile practitioner add work to the backlog and ask the product owner to re-prioritize it?

- A. When sprint velocity is higher than expected
- B. When sprint velocity is lower than expected
- C. When acceptance criteria is missing information
- D. When the stakeholder requests additional features

51. 敏捷管理专业人士应在何时向待办事项列表添加工作并要求产品负责人重新确定其优先级？

- A. 当 sprint 速度高于预期时。
- B. 当 sprint 速度低于预期时。
- C. 当验收标准缺少信息时。
- D. 当干系人要求额外特性时。

52. During the stand up meeting, the team decides on a new way to approach a story and begins developing solutions. What should the agile practitioner do?

- A. Assign follow-up actions to team members.
- B. Ask the team if this is a time for action.
- C. End the conversation to keep sprint commitments.
- D. Remove the story from the sprint if it exceeds the estimate.

52. 在站会上，团队决定了一种处理故事的新方式，并开始制定解决方案，敏捷管理专业人士应该怎么做？

- A. 向团队成员分配后续行动。
- B. 询问团队是否有采取行动的时间。
- C. 结束对话，保持 sprint 承诺。
- D. 如果该故事超出估算，则将故事从 sprint 里删除。

53. During a sprint, the team encounters a problem that might prevent them from completing their sprint objectives. What should the team members do?

- A. Add the issue to the issue log and keep it within the team until the sprint outcome is certain.
- B. Abort the current sprint and create a new one to ensure the problematic story is excluded.
- C. Notify all stakeholders of the issue and discuss how to adjust the sprint backlog, if needed.
- D. Ask all team members to work as many extra hours as needed to meet the original sprints.

53. 在一次 sprint 期间，团队遇到一个问题，可能会阻止他们完成 sprint 目标。团队成员应该怎么办？

- A. 将该问题加到问题日志中，将其保留在团队内，直到 sprint 结果确定为止。
- B. 中止当前的 sprint，并创建一个新的 sprint，以确保排除有问题的故事。
- C. 如果需要的话，通知所有干系人该问题，并讨论如何调整 sprint 待办事项。
- D. 要求所有团队成员尽可能的加班，以满足原本 sprint 的承诺。

54. The first iteration of product development is complete. During the iteration review, a concern is raised that managing product quality will be difficult in the next iteration. What should the agile practitioner do to address this?

- A. Seek guidance from senior management.
- B. Hire outside experts to fix the quality issues.
- C. Incorporate refactoring into the development process.
- D. Ask the team to fix quality issues before implementing new functionality.

54. 产品开发的第一次迭代已经完成。在迭代评审期间，提出来的一个担心是：在下次迭代期间管理产品质量将很困难。若要处理这个问题，敏捷管理专业人士应该怎么做？

- A. 向高级管理层寻求指导。
- B. 聘用外部专家解决质量问题。
- C. 将重构纳入开发过程。
- D. 要求团队在实施新功能之前解决质量问题。

55. Two members of an agile team experience conflict due to a gap in technical skills and personality differences. You allow the team to self-adjust; however, the conflict continues and negatively impacts team morale and performance. What should the scrum master do next?

- A. Intervene to directly address the conflict.
- B. Discuss the conflict during the next retrospective.
- C. Ask the two members to resolve their conflict.
- D. Analysis the team to see if the two members are a good fit.

55. 由于技术能力差距和个性差异，一个敏捷团队的两名成员发生冲突，你允许团队自我调整；然而冲突继续并对团队士气和绩效产生负面影响。Scrum 主管下一步应该怎么做？

- A. 干预，直接解决冲突。
- B. 在下次回顾会议上讨论该冲突。
- C. 要求两名成员解决冲突。
- D. 分析团队，看看这两名成员是否配合良好。

56. A development team is investigating the root causes related to long delays between product compilation and release for validation testing. Which tool or technique is the team using?

- A. Fishbone diagram
- B. Kano Model
- C. Pareto analysis
- D. Return on Time invested (ROTI) chart

56. 产品完工以及发布验证测试之间长时间延期，开发团队正在调查根本原因，团队要使用哪种工具或技术？

-
- A. 鱼骨图。
 - B. 卡诺模型。
 - C. 帕累托分析。
 - D. 投入时间回报（ROTI）图。

57. An agile team has identified a non-functional requirement that is needed in the practitioner recommend?

- A. Revisit the original specification and write this requirement as a spike user story.
- B. Write a user story for the requirement and include it in release backlog.
- C. Document it as a change request and incorporate it in a later release.
- D. Add it as a risk and track it through the risk management process.

57. 敏捷团队已经识别出项目中需要的一个非功能性需求，团队不能确定如何继续。敏捷管理专业人士应提出什么建议？

- A. 重新审视原始规范，将该需求编写为一个探测用户故事。
- B. 为该需求编写一个用户故事，并将其包含进发布待办事项中。
- C. 将其记录为一项变更请求，并将其包含进后续版本中。
- D. 将其添加为一项风险，通过风险管理流程跟踪该风险。

58. What estimation technique is an agile team using if they are collectively estimating the relative size of 50 stories using story points?

- A. Planning poker
- B. Dot voting
- C. Affinity mapping
- D. Bucket system

58. 如果敏捷团队使用故事点集体估算 50 个故事的相对规模，敏捷团队使用的是哪一种估算技术？

- A. 计划扑克。
- B. 记点投票表决。
- C. 亲和图。
- D. 斗伦体系

59. A team focused on production details produces a high-quality product, but delivery is often delayed. What should the agile practitioner do?

- A. Encourage the team to increase velocity without compromising quality.
- B. Ask the product owner to delay the release schedule until velocity and quality match.
- C. Accept the trade-off between high quality and reduced velocity.
- D. Change the sprint cycle to accommodate delayed delivery.

59. 一个专注于生产细节的团队生产高品质的产品，但经常延迟交付。敏捷管理专业人士应该怎么做？

- A. 鼓励团队在不影响质量的情况下提高速度。
- B. 要求产品负责人延迟发布计划，直到速度和质量匹配为止。
- C. 接受高品质和低速度之间的权衡。
- D. 更改 sprint 周期以适应延迟交付。

60. A developer starts implementing a feature that the customer recently requested. However, the developer did not consult with the project team first. What should the team do?

- A. Ensure the developer understands that the feature must be prioritized by the product owner.
- B. Inform the customer that their request is not supported by agile principles.
- C. Support the developer's decision to proactively address the needs of the customer.
- D. Add the feature to the product backlog without further discussion.

60. 一名开发人员开始实施客户最近请求的一个功能，然而，该开发人员并未事前咨询项目团队，团队应该怎么做？

- A. 确保该开发人员理解该功能必须由产品负责人确定优先级。
- B. 通知客户他们的请求未获得敏捷原则的支持。
- C. 支持该开发人员的决定，主动解决客户的需求。
- D. 在产品待办事项中添加该特性，而不进行进一步讨论。

61. A company transitions to agile practices, and a co-located team adopts scrum methodology. The scrum master sets up daily scrum meetings and insists that all team members attend in person to implement face-to-face conversation. However, attendance is low. What should the scrum master do?

- A. Enforce a penalty for missing the meeting.
- B. Inform team members that they can use web cameras or video conferencing for the meeting.
- C. Allow team members to call into a conference line.
- D. Emphasizing the importance of this agile principle and require that everyone attend the meetings in person.

61. 一家公司过渡到敏捷实践，一个集中办公的团队采用 scrum 方法，scrum 主管安排召开每日 sprint 会议，并坚持让所有团队成员亲自参加面对面对话。但是，出勤率很低，scrum 主管应该怎么做？

- A. 对缺席会议执行处罚。
- B. 通知团队成员他们可以为会议使用网络摄像头或视频会议。
- C. 允许团队成员呼叫会议线路。
- D. 强调这一敏捷原则的重要性，并要求每个人亲自出席会议。

62. An agile team is developing a product to be integrated with a customer's system. The system is frequently changed and some releases fail the integration test. What should the agile practitioner do?

- A. Ask the customer to make less frequent changes to the system and re-test the failed releases in integration.
- B. Advise the team to do additional testing before each release.
- C. Delegate the problem to an integration subject matter expert (SME).
- D. Implement a feedback loop between the project team and the customer.

62. 敏捷团队正在开发一个即将与客户系统集成的产品。系统频繁更改，某些版本未能通过集成测试。敏捷管理专业人士应该怎么做？

- A. 要求客户不要那么频繁地更改系统，并在集成中重新测试失败的版本。

-
- B. 建议团队在每次发布版本前进行额外的测试。
 - C. 将问题分配给集成主题专家（SME）。
 - D. 在项目团队和客户之间实施反馈回路。

63. The iteration velocity for an agile team is showing sharp increases and decreases. The agile team lead needs to make the velocity more consistent. What should the agile team lead do?

- A. Meet with the team to identify underlying causes and implement adjustments to obtain a steady iteration velocity.
- B. Use the highest velocity from previous iterations as a baseline.
- C. Conduct a team meeting to encourage cooperation and achieve consistent velocity.
- D. Facilitate pair programming between team members to achieve desired iteration velocity.

63. 一个敏捷团队的迭代速度呈现急剧上升和下降的趋势。敏捷团队需要让迭代速度更加可持续。敏捷团队领导应该怎么做？

- A. 与团队开会识别潜在原因并实施调整，以获得稳定的迭代速度。
- B. 使用之前迭代的最高速度，并将其作为基准。
- C. 召开团队会议来鼓励合作，实现可持续的迭代速度。
- D. 引导团队成员之前结对编程，实现理想的迭代速度。

64. A new executive joins project and is unclear about the intent of some of the features. An agile practitioner that learns about this. What should the agile practitioner do?

- A. Schedule a meeting between the product owner and executive.
- B. Invite the executive to the release planning meeting.
- C. Invite the executive to the sprint demo.
- D. Invite the executive to a Kaizen event.

64. 一名新高管加入一个项目，不清楚一些特性的意图，该项目的敏捷管理专业人士了解到一点，敏捷管理专业人士应该怎么做？

- A. 安排一次产品负责人与高管的会议。
- B. 邀请该高管参加发布计划会议。
- C. 邀请该高管参加 sprint 演示。
- D. 邀请该高管参加改善活动。

65. On a web-based software project, the project business owner asks a team member about a new feature's status. The team member responds that the work is complete. The business owner is confused because, upon visiting the website, the new feature was not present. What would cause this misunderstanding?

- A. The team member felt pressured to overstate progress to satisfy the business owner.
- B. Development work on the feature was complete but the feature had not been released.
- C. Development work on the feature has not yet been approved by the stakeholders.
- D. The business owner failed to define the feature's acceptance criteria in the user story.

65. 在基于 web 的软件项目中，项目业务负责人向团队成员询问一个新特性的状态，团队成员回应说工作已完成，业务负责人赶到困惑，因为在访问网站时，新功能不存在。是什么原因导致这种误解？

- A. 团队成员感到压力而夸大项目进展，以便让业务负责人满意。
- B. 该特性的开发工作已完成，但该特性未发布。
- C. 该特性的开发工作未获得项目干系人的批准。
- D. 业务负责人未能在用户故事中定义该特性的验收标准。

66. An agile practitioner is concerned about a high-risk portion of a project. The agile practitioner wants to ensure that risk and value are both given priority in the solution. What should the agile practitioner do?

- A. Create four quadrants that show the risk-to-value relationship, and do the high-risk, high-value task first.
- B. Create four quadrants that show the risk-to-value relationship, and do the high-risk, low-value task second.
- C. Use an information radiator, and have the development team focus on the highest risk development matter.
- D. Use a fishbone diagram to see the relationship between schedule, cost, and functionality risks.

66. 敏捷管理专业人士对项目中的高风险部分感到担忧，敏捷管理专业人士希望确保风险和价值都在解决方案中设立优先级。敏捷管理专业人士应该怎么做？

- A. 创建四个象限，显示风险与价值的关系，首先执行高风险、高价值的任务。
- B. 创建四个象限，显示风险与价值的关系，首先执行高风险、低价值的任务。
- C. 使用信息发射源，并让开发团队专注于具有最高风险的开发事项。
- D. 使用鱼骨图查看进度计划、成本和功能性风险之间的关系。

67. To identify and respond to risks early in the project and at minimal cost, what is the most efficient action that the agile team can do?

- A. Limit sprint size.
- B. Refer the risk learned.
- C. Consult the risk register.
- D. Review the information radiator records.

67. 若要在项目早期以最低的成本识别并应对风险，敏捷团队可以采取的最有效行动是什么？

- A. 限制 sprint 规模。
- B. 参照已认识到的风险。
- C. 查询风险登记册。
- D. 查看信息发射源记录。

68. A team is estimating user stories for an upcoming iteration. Which team will they use to describe the duration of tasks for uninterrupted team focus?

- A. Ideal effort
- B. Velocity
- C. Stick
- D. Technical debt

68. 团队正在为一个即将到来的迭代进行用户故事估算，他们将使用哪个术语来描述团队不间断专注的任务时间？

- A. 理想工时。
- B. 速度。
- C. 浮动时间。
- D. 技术债务。

69. An agile team is struggling with a complex project in which requirements are changing and the customer's needs appear to be volatile. What should the team do to address this moving forward's?

- A. Consult with the product owner to prioritize the user stories.
- B. Raise an escalation to the project sponsor to address the customer's volatility.
- C. Use the change management process and record changes as they arise.
- D. Limit the iteration length and increase the review frequency with the customer.

69. 敏捷团队正在努力为一个复杂项目工作，该项目需求不断发生变化，客户需求似乎反复无常，若要解决这个问题继续该项目，团队应该怎么做？

- A. 查询产品负责人，为用户故事排列优先顺序。
- B. 将该问题升级给项目发起人，以解决客户的反复无常。
- C. 利用变更管理流程，并在发生变更时记录。
- D. 限制迭代长度，提高与客户一起审查的频率。

70. The following chart lists stories for a release of an agile project:

If the team completes story A, story B, and 50 percent of story C for the first iteration, what is the team's velocity?

- A. 9
- B. 10
- C. 12
- D. 15

70. 以下图表列出了某个敏捷项目版本的故事。如果团队在第一次迭代中完成故事 A、故事 B 以及 50% 的故事 C，团队的速度是多少？

故事	故事点
A	4
B	5
C	6
D	5
E	4
F	6
G	1

- A. 9
- B. 10
- C. 12
- D. 15

71. The development team expressed concerns regarding the number of emails and calls they are receiving from company executives about the recent launch of a product. What should the scrum master do?

- A. Inform the development team that they should ignore the phone calls and emails.
- B. Work with the product owner to re-direct the executives' inquiries.
- C. Ask the product owner to enter the requests into the product backlog as high priority.
- D. Ask the scrum master to enter the requests into product backlog as high priority.

71. 最近，开发团队对从公司高管处收到有关产品发布的电子邮件和电话数量表示担忧。Scrum 主管应该怎么做？

- A. 通知开发团队忽略电话和电子邮件。
- B. 与产品负责人一起处理高管的问询。
- C. 让产品负责人将这些请求作为高优先级录入产品待办事项中。
- D. 让 scrum 主管将这些请求作为高优先级录入产品待办事项中。

72. An agile team is showing signs of low morale. What should the agile project manager do?

- A. Ask the employees' direct managers to address the issue.
- B. Rely on the team to motivate themselves.
- C. Ask the product sponsor for direction.
- D. Collaborate with the team to address the issue.

72. 敏捷团队正显示出士气低落的迹象，敏捷项目经理应该怎么做？

- A. 让员工的直属经理来解决这个问题。
- B. 依靠团队来鼓励他们自己。
- C. 询问产品发起人的指示。
- D. 与团队协作来解决这一问题。

73. An agile team lead notices that the team is hesitant to voice their opinions. What should the agile team lead advise the team to facilitate communication?

- A. Be dedicated to the outcome.
- B. Follow a common strategy.
- C. Feel free to share ideas.
- D. Use a shared workspace.

73. 一名敏捷团队领导注意到团队不愿意表达他们的意见，为引导沟通，敏捷团队领导应该向团队提出什么建议？

- A. 专注于结果。
- B. 遵循一个共同策略。
- C. 自由分享想法。
- D. 使用共享工作区。

74. During an iteration, the product owner insists that a feature must have a response-time threshold. The team explain that this requirement presents technical challenges, but does not jeopardize the iteration's goal. What should the product owner do?

- A. Urge the team to work overtime to satisfy this requirement.

-
- B. Cancel the iteration if the team cannot satisfy this requirement.
 - C. Ask the team to prolong the iteration to satisfy this requirement.
 - D. Add a new user story to the backlog to satisfy this requirement.

74. 在一次迭代期间，产品负责人坚持认为某个特性必须具有相应时间阈值。团队解释说这个需求存在技术挑战。但不会危及迭代目标。产品负责人应该怎么做？

- A. 敦促团队加班工作，以满足这一需求。
- B. 如果团队不能这个需求则取消迭代。
- C. 要求团队延长迭代，以满足这一需求。
- D. 在待办事项中添加一个新的用户故事来满足这个需求。

75. The agile team completed the product development phase and verified that all tests have passed, but the customer reports dissatisfaction with quality and performance. What should the agile project team have done before product release to avoid this situation?

- A. Held a retrospective to validate project deliverables.
- B. Performed a review of all requirements.
- C. Obtained approval from the project sponsor.
- D. Captured feedback from stakeholders at scheduled demos.

75. 敏捷团队完成了产品开发阶段，并核实所有测试均已通过，但客户报告对质量和性能不满意，若要这种情况，敏捷项目团队应该在产品发布之前做什么？

- A. 召开一次回顾会议，核实项目可交付成果。
- B. 执行对所有需求的评审。
- C. 获得项目发起人的批准。
- D. 通过计划的演示，收集项目干系人反馈。

76. On what does the connect of building and delivering incrementally focus?

- A. Building the high-value item
- B. Building the item quickly
- C. Building the item correctly
- D. Building the correct item

76. 构建和交付增量关注的是什么概念？

- A. 构建最高价值的工作项。
- B. 快速构建工作项。
- C. 正确构建工作项。
- D. 构建正确的工作项。

77. A project is in the initial stage of planning, and a project team needs to create a reliable, realistic, plan, which agile practice helps the team achieve this goal?

- A. Adding a schedule buffer that accounts for changes to the product backlog.
- B. Adding a period of overtime to the schedule to set expectations of team members.
- C. Adding extra team members to the project.
- D. Adding extra points to all estimations.

77. 项目在初始计划阶段，项目团队需要创建一份可靠、现实的计划。下列哪一项敏捷实践可有助于实现这个目标？

- A. 为产品待办事项的变更设置进度计划的缓冲。

-
- B. 为进度计划增加加班时间，设置团队成员的期望。
 - C. 为项目添加额外的团队成员。
 - D. 对所有的估计增加额外的点数。

78. An agile project team in planning version two of a product but is simultaneously responsible for supporting and maintaining version one. How should the team balance the planning needs of version two with the support and maintenance needs of version one?

- A. Priorities the return on investment (ROI) of version two's development as higher than supporting and maintaining that of version one.
- B. Create an estimate that does not use ideal, as ideal days do not account for other commitments.
- C. Subtract support costs from capacity when establishing velocity.
- D. Focus only on creating new business value and transfer version one's maintenance and support to another team.

78. 敏捷项目团队正在规划某个产品的第二个版本，但同时还要负责第一个版本的支持和维护，团队应如何平衡第二版本的规划需求与第一个版本的支持和维护需求？

- A. 优先考虑第二个版本的开发是由于相较于第一个版本的支持和维护，因为第二个版本投资回报率（ROI）率较高。
- B. 创建一份不使用理想天数的估算，因为理想天数未考虑其他承诺。
- C. 确定速度时，从生产能力中减去支持成本。
- D. 只关注于创造新的商业价值，并向另一个团队移交第一个版本的支持和维护的工作。

79. Members of a scrum team have frequent misunderstanding with another team that uses Kanban. What should the two teams do?

- A. Document major decisions in order to facilitate retrospective review sessions.
- B. Identify architectural risks that result from cross-team misunderstandings.
- C. Enacting a common vocabulary that both teams will use for communication.
- D. Ask the division manager to require the use of a single agile methodology.

79. Scrum 团队的成员对使用看板的另一个团队不断有误解，两个团队该如何做？

- A. 记录主要决策，以便引导回顾评审会议。
- B. 识别造成两团队误解的架构风险。
- C. 制作一份两个团队可用来沟通的常见词汇表。
- D. 让部门经理要求使用一种敏捷方法。

80. Why should a project team reduce the work in progress (WIP)?

- A. WIP reduction drives higher quality.
- B. WIP indicates poor project planning.
- C. WIP represents team members' utilization.
- D. WIP shows that the project is behind schedule.

80. 为什么项目团队应该减少进行中的任务（WIP）？

- A. 减少 WIP 能获得更高的质量。
- B. WIP 说明项目规划不佳。
- C. WIP 代表团队成员的利用率。
- D. WIP 表示项目落户于进度。

81. A change in project management office (PMO) strategy advocates an agile framework for the project, but the executive team has reservations. What should the PMO do to ensure that the executive team will be aligned?

- A. Issue a memo of understanding that agile principles should be implemented for all new projects.
- B. Obtain executive team buy-in conducting a meeting to present the advantages of agile principles and processes.
- C. Implement agile principles and processes across functional business units to demonstrate advantages.
- D. Requires that all staff, management, and executives attend agile training and adhere to as principles.

81. 项目管理办公室（PMO）战略的变化为新的 IT 项目提出敏捷框架，但是管理团队有所保留，那应该拿什么来确保执行团队保持一致？

- A. 签发一份谅解备忘录，应为所有新项目实施敏捷原则。
- B. 通过召开会议来介绍敏捷原则和流程的优势，获得管理团队的支持。
- C. 跨职能业务部门实施敏捷原则和流程以展示优势。
- D. 要求所有员工，管理层和高管参加敏捷培训并遵守敏捷原则。

82. At the end of an iteration, velocity is higher than expected. If this trend continues, what is the most appropriate response?

- A. The team should increase the amount of backlog items included in the sprint.
- B. The scrum master should reduce the number of resources on the project team.
- C. The project management office (PMO) should move up the release date.
- D. The manager should ask the team members to work on other projects.

82. 在迭代结束时，速度高于预期。如果这种趋势继续下去，最适应的应对措施是什么？

- A. 团队应该增加 sprint 中包含的待办事项数量。
- B. Scrum 主管应减少项目团队资源数量。
- C. 项目管理办公室（PMO）应将发布日期向前推移。
- D. 经理应要求团队成员从事其他项目。

83. A team's customers is unresponsive to questions and often misses iteration reviews and demos. Despite this lack of engagement, the customer wants the product to be delivered on time to meet expectations. What should the agile practitioner do?

- A. Instructed the team to make educated decisions using expert judgment.
- B. Advices the customers that their active participation is critical to the success of the project.
- C. Engage a team of specialists to perform requirements gathering.
- D. Train the product owner to obtain the necessary customer feedback.

83. 团队客户不回应问题，且经常错过迭代评审和演示。尽管缺乏参与，但客户希望产品按时交付并满足期望。敏捷管理专业人士应该怎么做？

- A. 指示团队使用专家判断做出有根据的决策。

-
- B. 告知客户他们的积极参与对项目的成功至关重要。
 - C. 聘用一个专家团队，执行需求收集。
 - D. 培训产品负责人获得必要的客户反馈。

84. Prior to delivering a new product to market, a team needs all features and functions to achieve a 97 percent pass rate during customer acceptance testing. Which step should the team take to achieve this goal?

- A. Adhere to a plan-driven test process.
- B. Require four days for approving and debugging code.
- C. Implement a highly predictive testing process.
- D. Use test-driven development (TDD) practices.

84. 在将新产品推向市场之前，团队需要所有的特性和功能在客户验收测试期间获得 97% 的合格率，需要实现这个目标，团队应该采取哪个步骤？

- A. 遵守计划驱动测试过程。
- B. 批准和调试代码需要四天。
- C. 实施高预测性测试过程。
- D. 使用测试驱动的开发（TDD）实践。

85. A team member brings a problem to the team lead's attention. As an agile coach, what should the team need do?

- A. Allow the team to resolve it.
- B. Ask the functional manager for guidance.
- C. Reactive the problem and notify the team.
- D. Reactive the problem with the product owner and notify the team.

85. 一名团队成员提出一个问题，引起团队领导的注意。作为敏捷教练，该团队领导应该怎么做？

- A. 允许团队来解决这个问题。
- B. 寻求职能经理的指导。
- C. 解决这一问题，并通知团队。
- D. 与产品负责人一起解决这一问题，并通知团队。

86. An agile practitioner learns that a new stakeholder is unsure how to stay informed of the project status. What should the agile practitioner do?

- A. Inform the team that this stakeholder must be involved in every discussion.
- B. Invite the stakeholder to the daily stand up meeting.
- C. Add the stakeholder to the communications management plan.
- D. Ask the stakeholder to review the project status reports.

86. 敏捷管理专业人士得知，新的干系人不确定如何持续了解项目状态，敏捷管理专业人士应该做什么？

- A. 告诉团队该干系人必须参与每次讨论。
- B. 邀请该干系人参加每日站会。
- C. 将该干系人添加进沟通管理计划。
- D. 让该干系人查看项目状态报告。

87. An agile team has developed an idea for a new product. The user experience and marketing teams wish to quickly proceed with implementation. The sponsor has supplied the necessary funding, and the product vision and roadmap have been defined. What should the team do next?

- A. Begin backlog planning, work decomposition, and estimation.
- B. Ensure that the necessary skillsets and knowledge are available to meet the product's vision.
- C. Share the roadmap and vision with the relevant stakeholders, and involve them as necessary.
- D. Display the product roadmap in the work area, and distribute it virtually to stakeholders.

87. 敏捷团队已经想出一个新产品的创意，用户体验和营销团队希望快速实施。项目发起人提供必要的资金，并定义了产品愿景和路线图。团队下一步应该怎么做？

- A. 开始待办事项规划、工作分解和估算。
- B. 确保提供必要的技能和知识满足产品愿景。
- C. 与相关项目干系人分享路线图和愿景，并根据需要让他们参与。
- D. 在工作区中展示产品路线图，并通过虚拟方式分享给项目干系人。

88. A scrum team is developing complex customer products. The product owner for the team needs help prioritizing the backlog with a priority of customer preferences over compared features. Which method can the product owner use?

- A. Kano analysis
- B. Planning poker
- C. SMART goal setting
- D. Cost of delay

88. Scrum 团队正在开发复杂的客户产品。团队的产品负责人需要针对待办事项，按照客户的偏好优先级以及比较功能排列优先顺序。产品负责人可以使用哪种方法？

- A. 卡诺分析。
- B. 计划扑克。
- C. SMART 目标设定。
- D. 延迟成本。

89. In an agile environment, who is responsible for designing and updating the Kanban board and the project status and progress?

- A. The product manager
- B. The team lead or coach
- C. The team
- D. The stakeholder

89. 在敏捷环境中，谁应负责设计和更新看板的项目状态和进度？

- A. 产品负责人。
- B. 团队领导或导师。
- C. 团队。
- D. 项目干系人。

90. An agile project team is having difficulty agreeing on the next steps for an iteration. What should the team do to come on an agreement?

- A. Ask the costumer to make the decision.
- B. Ask the project manager to make the decision.
- C. Ask the product manager to use a consensus-driven approach to help the team reach agreement.
- D. Use a collaborative approach to reach an agreement.

90. 某敏捷项目团队难以对一次迭代中的后续工作达成一致，团队应该怎么做来达成一致意见？

- A. 让客户做出决定。
- B. 让项目经理做出决定。
- C. 让产品经理采用一致意见驱动的方法来帮助团队达成一致。
- D. 采用协作的方法达成一致。

91. A disagreement between two team members has negatively impacted team velocity on the team project. What should an agile team lead do?

- A. Encourage the team members to keep their disagreement private and ensure they keep their professionalism.
- B. Work within the project's self-organizing framework by allowing them to reach a solution.
- C. Join the discussion and make a decision for the team.
- D. Escalate the situation to upper management.

91. 两名团队成员之间的分歧对多个项目的团队速度产生了负面影响。敏捷团队领导应该怎么做？

- A. 鼓励团队成员私下保持意见分歧，并确保他们保持专业精神。
- B. 通过允许他们自己达成解决方案，在项目的自组织框架内工作。
- C. 加入讨论，并为团队做出决策。
- D. 将这种情况上报给上级管理层。

92. How are minimal marketable features defined?

- A. By writing user stories that can be marketed first
- B. By the smallest increment of the product that is approved
- C. By the smallest amount of functionality that adds value to the market
- D. By a product backlog that is prioritized to deliver the most important features

92. 如何定义最小可售特性？

- A. 通过编写可先在市场上销售的用户故事。
- B. 通过已获批准的最小产品增量。
- C. 通过为市场增加价值的最小功能数量。
- D. 通过优先考虑交付量最重要功能的产品待办事项。

93. A new agile team lead accepts an assignment to lead a well-established team. Many team members have worked together on this product for several years. During a meeting, the agile team lead notices that, while there is central control, the team members make decisions based on conterminous, use verbal communication, and call team leads "coaches". What type of behavior does this describe?

-
- A. Synchronous
 - B. Collaborative
 - C. Random
 - D. Hierarchical

93. 一名新的敏捷团队领导接受委任，管理一个成熟团队，多名团队成员已经在这个产品上合作多年。这一次会议期间，敏捷团队领导注意到，虽然有集中控制，团队成员基于共识做出决策，使用口头沟通。并称呼团队领导为“教练”。这概述的是哪种行为？

- A. 同步
- B. 协作
- C. 随机
- D. 层级

94. Which of the following is an aspect of communication that must be present to promote their cohesive?

- A. Team lead evaluation
- B. Fear-free atmosphere
- C. Individual acknowledgement
- D. Productivity tracking

94. 如果要提高团队凝聚力，在沟通方面，以下哪一项是必需的？

- A. 团队领导评价。
- B. 无恐惧气氛。
- C. 个人确认。
- D. 生产效率追踪。

95. A team needs to evaluate stories for a critical-to-satisfy end user. What method should the team amplify?

- A. Impact mapping
- B. Story mapping
- C. Personas
- D. Assign priority to stories

95. 在团队需要评估一个最终用户的用户故事，该用户的满意度至关重要。团队应该使用什么方法？

- A. 影响图
- B. 故事地图
- C. 人物创建/用户画像
- D. 为故事分配优先级

96. A project sponsor requests a brief overview of agile. What should the agile practitioner interpret about agile project execution?

- A. The project will follow the plan at all times.
- B. The project will focus on technical excellence and good design.
- C. The project will focus on predictability over adaptability.
- D. The project will have well-defined processes and less reliance on individuals.

96. 项目发起人要求提供敏捷的简要概述，敏捷管理专业人士应如何解释敏捷项目执行？

- A. 项目将始终遵循计划。

-
- B. 项目将关注技术卓越和良好设计。
 - C. 项目将关注可预测性胜过适应性。
 - D. 项目将具有定义良好的过程并减少对个人的依赖。

97. A new project manager is assigned to an agile project. In the first stand up meeting, the project manager notices that resources are anxious, withdrawn, and struggling to complete tasks. The resources are also distracted by frequent interruptions and requests from the functional manager. What type of organization is this?

- A. This is a flat structure organization and has long history of an informal work culture in place.
- B. This is a hierarchical organization in which work load and performance are evaluated by functional managers.
- C. This is a strong matrix organization in which project managers have little or no authority over resources.
- D. This is an agile organization in which functional managers are all strong and experienced leaders.

97. 一名新项目经理被分配到一个敏捷项目。在第一次站会上，项目经理注意到团队成员对完成任务感到焦虑、退缩和挣扎。成员们还因为职能经理的频繁中断和请求导致精力分散。这属于哪一种组织类型？

- A. 这属于一个扁平结构组织，实施非正式工作文化的历史悠久。
- B. 这是一个层级组织，由职能经理评估工作负荷和绩效。
- C. 这是一个强矩阵组织，项目经理对资源拥有很小甚至不拥有职权。
- D. 只是一个敏捷组织，职能经理全部是强有力且经验丰富的领导者。

98. An agile practitioner needs to ensure that their end product satisfies business requirements. How should the agile practitioner achieve this goal?

- A. By ensuring customers are at product review meetings
- B. By asking the team to submit regular reports to key stakeholders
- C. By obtaining agreement from the product owner on business requirements
- D. By inviting other product owners to product review meetings

98. 敏捷管理专业人士需要确保最终产品满足业务需求。敏捷管理专业人士应如何实现这个目标？

- A. 通过确保客户参加产品评审会议。
- B. 通过要求团队向关键项目干系人提交定期报告。
- C. 通过获得产品负责人对业务需求的同意。
- D. 通过邀请其他产品负责人参加产品评审会议。

99. An agile team needs to identify the possible causes of an issue they are experiencing in a current project. What should the agile team do?

- A. Develop a spike.
- B. Create an Ishikawa diagram.
- C. Perform a prior analysis.
- D. Complete a variance and trend analysis.

99. 敏捷团队需要识别当前项目中遇到问题的可能原因。敏捷团队应该怎么做？

-
- A. 开发一个探测。
 - B. 创建石川图
 - C. 执行事前分析。
 - D. 完成偏差和趋势分析。

100. A functional manager assigns a cross-functional team member several tasks, which prevents agile team member from completing stories. What should the agile practitioner do immediately?

- A. Talk with the functional manager about the situation.
- B. Coach the team member on agile practices for time management.
- C. Report the functional manager to the project sponsor.
- D. Request that the functional manager to attend agile training.

100. 职能经理向一名跨职能团队成员分配多项任务，这妨碍了敏捷团队成员完成故事。敏捷管理专业人士应立即怎么做？

- A. 与该职能经理讨论这种情况。
- B. 教导团队成员有关时间管理的敏捷实践。
- C. 向项目发起人举报该职能经理。
- D. 请求职能经理参加敏捷培训。

101. During a scrum retrospective, the team identifies a non-functional requirement that was omitted from the release. What should the team do?

- A. Re-plan subsequent iterations and re-prioritize the product backlog.
- B. Place the non-functional requirement in the next iteration.
- C. Put the requirement in the product backlog for a future release.
- D. Add time to the iteration to include the non-functional requirement.

101. 在一次 scrum 回顾会议上，团队识别到发布版本中遗漏了一项非功能性需求。团队应该怎么做？

- A. 重新计划后续迭代，并重新确定产品待办事项的优先顺序。
- B. 在下一次迭代中包含该非功能性需求。
- C. 将该需求放入未来版本的产品待办事项中。
- D. 为该迭代增加时间，包含该非功能性需求。

102. A web developer is struggling to satisfy a product owner's requirements. How can a daily stand up help the developer?

- A. The agile practitioner can provide direction to the web developer.
- B. The web developer can discuss possible solutions with the team.
- C. The web developer can raise the issue with the team to create visibility.
- D. The meeting can be used to discuss whether the requirement is a priority.

102. 网络开发人员正在竭力满足产品负责人的要求。每日站会将如何帮助开发人员？

- A. 敏捷管理专业人士可以为网络开发人员提供指导。
- B. 网络开发人员可以与团队讨论可能的解决方案。
- C. 网络开发人员可以向团队提出问题，以便让问题可见。
- D. 会议可用于讨论该需求是否属于优先事项。

103. An experienced team member notices that a new team member consistently misses iteration commitments. What should the experienced team member do?

- A. Ask the team member to assign the commitment to the agile practitioner.
- B. Ask the team member's manager to speak with them.
- C. Ask the scrum master to apply pressure on the team member.
- D. During the retrospective, coach the team on how to better estimate.

103. 一名经验丰富的团队成员注意到，一名新团队成员总是不能兑现迭代承诺。该经验丰富的团队成员应该怎么做？

- A. 要求该团队成员将该承诺分配给敏捷管理专业人士。
- B. 要求该团队成员的经理与其谈话。
- C. 要求 scrum 主管对该团队成员施加压力。
- D. 在回顾会议上，教导团队如何更好地估算。

104. An agile team provides feedback that user stories include insufficient details to understand the requirements. What should the agile practitioner do?

- A. Coach the product owner to update only the acceptance criteria.
- B. Instruct the agile team to fix the user stories during the next retrospective.
- C. Coach the team to have a conversation with the customer to resolve issues.
- D. Inform the product owner's manager that the work items provide insufficient detail.

104. 敏捷团队反馈用户故事包含信息不足，无法理解需求。敏捷管理专业人士该怎么做？

- A. 指导产品负责人仅更新验收标准。
- B. 指示敏捷团队在下次回顾会议中解决用户故事的问题。
- C. 指导团队与客户进行对话解决问题。
- D. 通知产品负责人的经理，工作项提供的信息不足。

105. What is one of first steps an agile project manager should take to ensure that a product meets business needs?

- A. Align stakeholder interests and expectations.
- B. Start planning the next iteration.
- C. Gather the developers to prioritize user stories.
- D. Develop a project plan with the development team.

105. 为确保产品符合业务需求，敏捷项目经理应采取的其中一个首要步骤是什么？

- A. 让干系人的利益和期望相符合。
- B. 开始规划下一次迭代。
- C. 集合开发人员，为用户故事排列优先顺序。
- D. 与开发团队一起制定项目计划。

106. During an agile project iteration, the project owner wants to know the turnaround time for addressing software quality issues. In addition to using a Kanban board, what should the agile practitioner do to communicate this?

- A. Regular defect status reports
- B. Discussions between the product owner and the team
- C. Cycle time
- D. Cumulative flow diagram

106. 在敏捷项目迭代期间，产品负责人想知道解决软件质量问题的周转时间。除了使用看板以外，敏捷管理专业人士应如何传达这个想法？

- A. 定期缺陷状态报告。
- B. 产品负责人和团队之间的讨论。
- C. 循环时间。
- D. 累积流量图。

107. A senior team member with siloed knowledge resigns, providing very little notice. As a result, the team experiences bottlenecks. What should the team lead have done to ensure that development was maintained in this scenario?

- A. Merged similar development teams to enhance information sharing.
- B. Had the senior team member document their daily processes.
- C. Cross-trained the team in supplemental skills.
- D. Hired temporary staff with the required skill set.

107. 一名拥有封闭知识的高级团队成员辞职，提供极少信息。结果，团队经历瓶颈。若要确保在该情景中继续保持开发，团队领导应该事先做什么？

- A. 合并类似的开发团队以加强信息共享。
- B. 让高级团队成员记录他们的日常流程。
- C. 交叉培训团队的补充技能。
- D. 聘请具有所需技能的临时工作人员。

108. In a conversation with the team, the project sponsor challenges the value of daily stand up meetings. What should the agile practitioner do with this information?

- A. Replace some of the stand up meetings with information radiators.
- B. Educate the project sponsor on the benefits of daily stand up meeting.
- C. Ask the stakeholder to replace stand up meetings with on-demand status meetings.
- D. Combine stand up meetings with other meetings to reduce meeting time.

108. 在与团队谈话过程中，项目发起人对每日站立会议的价值提出质疑。敏捷管理专业人士应如何处理？

- A. 采用信息发射源替换一些每日站立会议。
- B. 教导项目发起人每日站立会议的好处。
- C. 让干系人将每日站立会议替换成按需召开的状态会议。
- D. 将每日站立会议与其它会议相结合，减少会议时间。

109. What should be done to manage cross-functional teams that are not co-located?

- A. Focus on team successes, and promote healthy competition among the teams.
- B. Use video conferencing and other collaboration tools.
- C. Optimize project work by removing project dependencies and reducing processes.
- D. Simplify processes and review time.

109. 应该如何管理不在同一地点办公的跨职能团队？

- A. 专注于团队成功，并促进团队之间的健康竞争。
- B. 使用视频会议和其他协作工作。
- C. 通过删除项目依赖关系和减少流程来优化项目工作。
- D. 简化流程和缩短评审时间。

-
110. Which condition must be met for an item' s status to be considered “done” ?
- A. The team agrees with project sponsor that it is finished.
 - B. The product owner accepts it as finished.
 - C. The product owner and the customer approve the user stories.
 - D. The team and the customer accept the user stories.
110. 一个事项的状态被视为“已完成”，必须满足哪一项条件？
- A. 团队与项目发起人达成该事项已完成的一致意见。
 - B. 产品负责人接受该事项已完成。
 - C. 产品负责人和客户批准用户故事。
 - D. 团队和客户批准用户故事。
111. During an iteration retrospective, the product owner informs the project team that the solution did not fully meet business expectations. What should the team do to ensure that expectations are met to future releases?
- A. Work with the product owner to establish acceptance criteria.
 - B. Establish a chain of documentation for requests by the product owner.
 - C. Establish an escalation chain for product owner concerns.
 - D. Schedule more frequent meetings with the product owner.
111. 在一次迭代回顾会议上，产品负责人通知项目团队解决方案没有满足业务期望，为确保未来版本满足期望，团队应怎么做？
- A. 与产品负责人合作，确定验收标准。
 - B. 为产品负责人的请求创建一个文档链。
 - C. 为产品负责人的担忧创建一个问题上报链。
 - D. 更为频繁地安排召开与产品负责人的会议。
112. What contributes to positive agile-team motivation?
- A. Team size
 - B. Management tools
 - C. Personal recognition
 - D. Corporate reputation
112. 什么对敏捷团队的激励有正面作用？
- A. 团队规模。
 - B. 管理工具。
 - C. 个人认可。
 - D. 企业声誉。
113. A stakeholder has specific goals for a new agile project and the project team. Why is regular communication of stakeholder and team goals important?
- A. To limit external involvement in product development
 - B. To ensure goals are incentivized
 - C. To realign and reaffirm the team' s goal
 - D. To provide an opportunity for cross-training
113. 项目干系人对一个新敏捷项目和项目团队都拥有明确目标，为什么定期沟通干系人和团队的目标很重要？
- A. 为了限制外部介入产品开发。

-
- B. 为了确保目标受到激励。
 - C. 为了重新对齐和重申团队目标。
 - D. 为了提供交叉培训机会。

114. Discussions between team members before a retrospective indicate conflict. An agile practitioner wants to ensure that there is an open and safe environment during the meeting.

- A. Review with the team the established ground rules.
- B. Ask specific questions to identify the cause of conflicts.
- C. Encourage the team to continue working to remain on schedule for this iteration.
- D. Meet with project team members one-on-one prior to the meeting.

114. 在回顾会议之前团队成员之间的讨论表明存在冲突。敏捷管理专业人士希望确保会议期间存在开放和安全的环境。敏捷管理专业人士应该怎么做？

- A. 与团队评审既定的基本原则。
- B. 提出具体问题以确定冲突的原因。
- C. 鼓励团队继续工作，按进度计划完成此次迭代。
- D. 在会议之前与项目团队成员一对一会面。

115. A project team's initial estimate for a release is 300 story points, and the average estimated velocity for an iteration is 30 story points. After several iterations, the actual velocity is calculated as 15 story points, which double the project's estimated completion time. What should the project team do?

- A. Ask the product owner to increase team resources.
- B. Communicate the velocity and new release date to the product owner.
- C. Re-estimate by changing the unit of measure from story point to ideal days and inform the product owner.
- D. Re-estimate and inform the product owner that the project is more complicate than originally anticipated.

115. 项目团队对发布版本的初始估算是 300 个故事点，一次迭代的平均估计速度是 30 个故事点。经过几次迭代后，计算的 actual 速度只有 15 个故事点，让项目的预计完成时间翻倍。项目团队应该怎么做？

- A. 要求产品负责人增加团队资源。
- B. 与产品负责人沟通速度以及新的发布日期。
- C. 通过将测量单位从故事点更改为理想的天数重新估算，并通知产品负责人。
- D. 重新估算，并通知产品负责人项目比原先预期的更为复杂。

116. A key stakeholder is confused about the project's health. What could be done to prevent this in the future?

- A. Provide only verbal project reports.
- B. Discuss project health with stakeholders only at the planning meeting.
- C. Create a weekly report that follows the company's reporting standards.
- D. Visibly display progress metrics, and educate all key stakeholders on their meaning.

116. 关键干系人对项目的健康情况感到困惑。若要在将来防止这个问题，应该做什么？

- A. 仅提供口头项目报告。

-
- B. 仅在规划会上与项目干系人讨论项目健康情况。
 - C. 创建符合公司报告标准的每周报告。
 - D. 可视化显示进度测量指标，并告知所有关键项目干系人其意义。

117. Which of the following is a value statement in the Agile Manifesto?

- A. We believe in customers collaboration over responding to change.
- B. We believe in project management over individuals and interactions.
- C. We believe in process and tools over comprehensive documentation.
- D. We believe in working software over comprehensive documentation.

117. 下列哪一项属于敏捷宣言中对价值陈述？

- A. 我们认为与客户的协作高于响应变化。
- B. 我们认为项目管理高于个体和互动。
- C. 我们认为过程和工具高于完备的文档。
- D. 我们认为可工作的软件高于完整的文档。

118. A project owner has limited time to spend on the project and is unable to validate completed work. The agile team lead still needs to ensure that requirements are met. What should the agile team lead do?

- A. Ensure the product owner's commitment to the project by meeting with them directly.
- B. Confront the product owner's at the next stand up meeting.
- C. Distribute a memo on agile principles to the product owner and supervisor.
- D. Escalate the issue and request a new product owner.

118. 产品负责人在项目上花费的时间有限，无法核实已完成的工作，但敏捷团队领导仍需要确保所有需求均得到满足。敏捷团队领导应该怎么做？

- A. 确保产品负责人通过直接与他们开会参与项目。
- B. 在下一次站会中与产品负责人当面对质。
- C. 将符合敏捷原则的备忘录分发给产品负责人和主管。
- D. 将问题上报并请求一名新的产品负责人。

119. How is the time of the day for daily stand up meeting decided?

- A. By the agile team, as part of the team's discussion on ground rules.
- B. By the product owner, according to the agile framework selected.
- C. By the team lead, as part of the team's planning session.
- D. By the project management office, as per organizational standards.

119. 每日站会的举行时间是如何决定的？

- A. 由敏捷团队决定，作为团队讨论基本规则的组成部分。
- B. 由产品负责人按照所选定的敏捷框架决定。
- C. 由团队领导决定，作为团队规划会的组成部分。
- D. 由项目管理办公室根据组织标准决定。

120. Team members disagree about estimation methodologies during a planning session. What action should the agile practitioner take to correct this issue?

- A. Encourage the team to use problem solving techniques to find the root cause of the disagreement.

-
- B. Have the team discuss the disagreement further during the lessons learned meeting.
 - C. Facilitate the creation of a fishbone diagram to set participation guidelines.
 - D. Ask the team to resolve the issue at the retrospective.

120. 在规划会上，团队成员对估算方法有分歧，若要纠正这个问题，敏捷管理专业人士应采取什么行动？

- A. 鼓励团队使用问题解决技术找到分歧的根本原因。
- B. 让团队在经验教训会议上进一步讨论该分歧。
- C. 引导创建鱼骨图，设置参与指南。
- D. 要求团队在回顾会议上解决这个问题。

121. A product owner believes a user story is essential for an iteration, but a team subject matter expert (SME) disagrees. This conflict is affecting team morale. What should the agile coach do?

- A. Address the subject in the retrospective and ask the team to determine if the user story should be kept or modified.
- B. Ask the product owner for input but explain that the SME will make the final decision.
- C. Meet individually with the SME and the product owner to mitigate the disagreement.
- D. Ask the SME for input but explain that the product owner is responsible for defining backlog priorities.

121. 产品负责人认为某个用户故事对于迭代至关重要，但是一名团队的主题专家(SME)却不同意，该冲突影响到团队士气。敏捷教练应该怎么做？

- A. 在回顾会议中陈述该问题，并要求团队确定用户故事是否应该保留或修改。
- B. 询问产品负责人的意见，但解释说该主题专家将做出最终决定。
- C. 与该主题专家和产品负责人单独开会，以减轻分歧。
- D. 询问该主题专家的意见，但解释说产品负责人负责定义待办列表优先级。

122. An agile team, working on a product release one year into the future, has planned out all iterations in detail. What type of planning should have been done first?

- A. Incremental
- B. Adaptive
- C. Release
- D. Iterative

122. 一个敏捷团队正在为未来一年后发布的产品工作，已经详细规划了所有迭代。应该首先进行什么类型的规划？

- A. 增量
- B. 适应
- C. 发布
- D. 迭代

123. A team, new to agile practices and the project domain. Is using the scrum framework. However, the team feels that scrum ceremonies fail to add value. As a result, they decide to use the official review meeting as a knowledge-sharing platform for technical issues. What should the agile team lead do?

A. Explain that the scrum framework uses an inspect and adapt approach, and organize scrum training for the team.

B. Allow the team to use its preferred approach, and inform relevant stakeholders.

C. Replace the product owner with one who can better communicate the scrum framework and their domain knowledge.

D. Replace team members with developers knowledgeable about the project domain.

123. 一个没有敏捷实践和项目领域经验的团队，正在使用 scrum 框架。然而，团队认为 scrum 仪式不能带来价值。因此，他们决定使用官方评审会议作为技术问题的知识共享平台。敏捷团队领导应该怎么做？

A. 解释 scrum 框架使用的是一种检查和适应的方式，并为团队组织 scrum 培训。

B. 允许团队使用其首选方法，并通知相关干系人。

C. 将产品负责人替换为可以更好地传达 scrum 框架及其领域知识的人员。

D. 将团队成员替换为拥有项目领域相关知识的开发人员。

124. A product owner, working on a project to automate the processing of special claims, relies on a subject matter expert (SME) to explain the expected behavior of these claims. The SME is inexperienced with agile projects and documents the full life cycle of such claims up front. However, the product owner prefers to obtain feedback after every review to ensure that the special claims interfaces are as consistent as possible with other claims interfaces. What should the product owner do?

A. Use expert judgment to make decisions on behalf of the SME.

B. Invite the SME to the review meeting and demonstrate the benefits gained from attending this meeting.

C. Have the developers use the SME's full life cycle document as a reference.

D. Allow the SME to interact directly with the developers to reduce overhead.

124. 一名产品负责人正在为一个自动处理特殊索赔的项目工作，依靠主题专家(SME)来解释这些索赔的预期行为。该主题专家缺乏敏捷项目的经验，提前将此类索赔的全部生命周期记录在案。但是，产品负责人更喜欢在每次审查后获得反馈，以确保特殊索赔接口与其它索赔的接口尽可能保持一致，产品负责人应该怎么做？

A. 使用专家判断替代该主题专家做决定。

B. 邀请该主题专家参加评审会议，并表明参加会议将获得的好处。

C. 让开发人员使用该主题专家的全部生命周期文件作为参考。

D. 让该主题专家直接与开发人员互动，以减少管理费。

125. The Project Manager was managing a software redesign project executed by a cross-functional team. The company is undergoing an agile transformation and the Project Management Office (PMO) has issued updated policies and procedures that require current project iteration development to be integrated into the project management methodology. What should the project manager do if he wants to ensure that quality is considered for each iteration delivery?

A. Schedule all testing activities for the last iteration of the project so that the entire team can focus on the same goal

B. Assign testing and validation activities to team members with functional backgrounds

-
- C. Work with relevant parties and the project team to ensure that there is a clearly defined definition of "done" (DoD)
 - D. Assign dedicated software testers to ensure testing is performed throughout the project lifecycle

125. 项目经理正在管理一个由跨职能团队执行的软件重新设计项目。该公司正在进行敏捷转型，项目管理办公室(PMO)发布了更新后的政策和程序，要求当前项目迭代开发整合到项目管理方法中。若要确保每次迭代交付都考虑质量，项目经理应该怎么做？

- A. 安排该项目最后一次迭代的所有测试活动，以便整个团队可以关注同一目标
- B. 将测试和验证活动分配给具有功能背景的团队成員
- C. 与相关方以及和项目团队合作，以确保有明确定义的“已完成”定义(DoD)
- D. 分配专门的软件测试人员，以确保在整个项目生命周期中进行测试

126. A large company of more than 400 people changes from the Waterfall to the Agile framework. The company uses the approach of applying Scrum to all projects in the organization using an all-in scenario. The leaders are reluctant to fully commit to Scrum and there are no experienced Scrum Masters available within the organization yet. Six months later, Scrum has failed in the company. Many different applications of Scrum have been tried with varying degrees of success. The company gives up and returns to the Waterfall approach.

What is the most likely reason that the transition did not work?

- A. Scrum was not properly promoted as a best practice and the best way to solve the problems of the organization which created a big risk.
- B. The change to Agile was not disruptive enough to provoke a real change and there was not enough commitment to keeping the new process.
- C. The company was too large to transition easily. A successful pilot project should have been done first to be able to copy from.
- D. There was no public display of Agility and, therefore, customers kept asking for Waterfall projects. The company gave up too early.

126. 某个 400 多人的大公司从瀑布开发模式向敏捷框架转变。该公司采用全覆盖的方法将 Scrum 应用于组织中的所有项目。领导者不愿意完全投入 Scrum，而且组织内还没有经验丰富的 Scrum Master。6 个月后 Scrum 在公司宣告失败。公司已经尝试了许多不同的 Scrum 应用方式，取得了不同程度的成功。公司最终放弃并回归瀑布开发模式。哪一项是转型失败的最可能原因？

- A. 未能将 Scrum 作为解决组织中产生较高风险的问题的最佳实践和最佳方法宣传到位。
- B. 敏捷变革的颠覆性不足以引发真正的变革，同时，对坚持新流程的承诺不充分。
- C. 公司规模太大，无法轻松过渡。应首先完成一个成功的试点项目，然后才能进行复制。
- D. 没有公开展示敏捷性，因此，客户不断要求瀑布开发模式项目。公司过早放弃。

127. What can an agile coach do to ensure that Individuals and teams feel free to express themselves, and that confidentiality will be maintained?

- A. Meet with the team to explain their rights.
- B. Create a safe environment.
- C. Start a coaching conversation.
- D. Establish regular team building activities.

127. 敏捷教练可以怎么做来确保个人和团队能够自由表达自己，同时又保持机密性？

-
- A. 与团队开会，解释他们的权利。
 - B. 创建一个安全的环境。
 - C. 开始一次教练谈话。
 - D. 安排定期的团队建设活动。

128. After several iterations, an agile project manager notices that a similar problem occurs twice and affects the team's execution efficiency, what should the agile project manager do?

- A. Escalate the problem to the project manager
- B. Increase the work being performed to improve efficiency
- C. Ask team members to revisit the requirements
- D. Address the issue in an iteration review meeting

128. 在几次迭代后，一名敏捷项目管理者注意到类似问题连续两次发生，并影响团队的执行效率，敏捷项目管理者应该怎么做？

- A. 将问题上报给项目经理
- B. 增加正在执行的工作，提高效率
- C. 要求团队成员重新审阅需求
- D. 在迭代回顾会议上解决该问题

129. A Scrum Team suggests to have a project with 3 Sprints of 2 weeks, while the customer suggests 1 Sprint of 6 weeks.

What is the greatest advantage of having 3 Sprints of 2 weeks?

- A. The team can inspect and adapt twice.
- B. The customer has to invest less time.
- C. The team delivers more Story Points.
- D. There is no difference.

129. 某 Scrum 团队建议一个项目用 3 个 2 星期的冲刺完成，而客户建议用 1 个 6 星期的冲刺完成。用 3 个 2 星期的冲刺完成的最大优点是什么？

- A. 团队可以检查和调整两次。
- B. 客户减少时间投入。
- C. 团队交付更多的故事点。
- D. 二者其实没有区别。

130. An agile practitioner is working with a high-performing, cross-functional agile team whose members are dynamic and focused, and reliably deliver value. After the first major release, team members begin to lose interest, which affects team performance and the project. What should the agile practitioner do?

- A. Advise management to modify the recognition and rewards system to offer better compensation.
- B. Sponsor an off-site team building exercise to refresh and re-energize the team.
- C. Meet with team members to realign the project with team goals.
- D. Allow sufficient time between releases for team members to prioritize personal goals.

130. 一名敏捷管理专业人士正在与高绩效、跨职能的敏捷团队合作，其成员充满活力和专注力，能可靠地提供价值。在第一次重大发布后，团队成员开始失去兴趣，影响团队绩效和项目。敏捷管理专业人士应该怎么做？

- A. 建议管理层修改认可与奖励制度，提供更好的补偿。
- B. 发起一项场外团队建设活动，让团队恢复活力并重新激励团队。
- C. 与团队成员开会，重新调整项目的团队目标。
- D. 在两次发布之间让团队成员之间留出足够的时间来优先考虑个人目标。

131. An agile team delivers 20 points every iteration. Management asks the team to improve its productivity and deliver more points. What should the agile team do?

- A. Ensure that management understands agile practices.
- B. Work overtime to meet the request.
- C. Deliver more points by finding efficiencies.
- D. Increase estimates without doing additional work.

131. 敏捷团队在每次迭代都交付 20 个故事点。管理层要求团队提高生产力，交付更多故事点。敏捷团队应该怎么做？

- A. 确保管理层理解敏捷实践。
- B. 加班工作满足该请求。
- C. 提高效率以交付更多故事点。
- D. 在不进行额外工作的情况下，增加估算。

132. A company wants to move away from traditional practices to agile practices. What should an agile coach recommend to the company first?

- A. Assess the organization for possible transformation success factors.
- B. Consider cultural diversity as an asset to derive value.
- C. Promote continuous improvements, globally diverse teams, and lean startup practices.
- D. Change organizational structure, continuously adjust leadership roles, and adapt to market conditions.

132. 一家公司希望从传统实践转向敏捷实践。敏捷教练首先应向公司提供什么建议？

- A. 评估组织可能的转型成功因素。
- B. 将文化多样性视为产生价值的资产。
- C. 倡导持续改进、全球多样化团队和精益启动实践。
- D. 改变组织结构，不断调整领导角色，适应市场条件。

133. The project team is having difficulty delivering product increments, and the project manager schedules a retrospective meeting to identify errors. Who should attend the meeting?

- A. Members of the Steering Committee
- B. All members directly involved in the project production schedule
- C. Principal and project Manager of the Project Management Office (PMO)
- D. Team leader for each team involved in the project

133. 项目团队在交付产品增量时遇到困难，项目经理安排一次回顾总结会议以找出差错。谁应该参加这次会议？

- A. 指导委员会成员

-
- B. 所有直接参与项目生产进度工作的成员
 - C. 项目管理办公室 (PMO) 的负责人和项目经理
 - D. 参与该项目的每个团队的团队领导

134. A product owner requests that, due to their unavailability, a sprint review meeting be rescheduled. What should the scrum master do?

- A. Hold the meeting as planned since the sprint review must not be postponed.
- B. Reschedule the meeting so that the product owner can attend and provide feedback.
- C. Invite an available product owner from a different product group to attend.
- D. Ask the project sponsor to attend in lieu of the product owner.

134. 由于没空参加, 产品负责人请求重新安排 sprint 评审会议。scrum 主管应该怎么做?

- A. 由于 sprint 评审会不能推迟, 按计划举行会议。
- B. 重新安排会议, 让产品负责人可以参加并提供反馈。
- C. 从不同产品组中邀请一名有空的产品负责人参加会议。
- D. 要求项目发起人代替产品负责人参加。

135. During a project meeting, a member of the agile team shares useful expertise about a new technology for which the team has no previous knowledge. Most team members are enthusiastic but have some reservations about its value to the project. What should the project manager do?

- A. Continue the project using the originally planned technology
- B. Hire an external expert to assess the suitability of the new technology
- C. Implement the new technology in the next iteration to support continuous improvement.
- D. Ask the team to run an exploratory spike to assess the advantages of the new technology.

135. 在项目会议期间, 敏捷团队的一名成员分享了一项新技术的有用专业知识, 而团队以前对该新技术并不了解。大多数团队成员都很感兴趣, 但他们对该技术对于项目的价值有一些保留。敏捷项目经理应该怎么做?

- A. 使用原先规划的技术继续该项目
- B. 聘请外部专家评估新技术的适用性。
- C. 在下一次迭代中实施新技术, 支持持续改进。
- D. 让团队运行一个探索性的“刺探”, 评估新技术的优势。

136. A key resource is switching between projects to obtain more visibility and acclaim. However, project work has grown and become a burden. What should the agile team lead do?

- A. Allow the resource to continue switching between projects to deliver high customer value
- B. Ask management to ensure that the resource is available to only one project at a time.
- C. Add more resources to projects to ensure work sharing.
- D. Encourage the resource to undergo time management training.

136. 一名关键资源在项目之间轮换, 以获得更多的知名度和赞誉。但是, 项目工作越来越多, 已经成为一个负担。敏捷团队领导应该怎么做?

-
- A. 允许该资源继续在项目之间轮换以提供高客户价值。
 - B. 要求管理层确保该资源一次只能在一个项目中可用。
 - C. 为项目添加更多资源，以确保工作分享。
 - D. 鼓励资源进行时间管理培训。

137. At the end of an iteration, a team member tells the project manager that a planned task was not completed due to an unresolved issue that occurred a few days ago. What should the project manager do to avoid this situation in the future?

- A. Discuss the issue at the next iteration planning meeting
- B. Review the issue at the next iteration daily stand-up meeting
- C. Explain the issue in a presentation
- D. Discuss the issue at the retrospective meeting

137. 在一次迭代结束时，一位团队成员告诉项目经理，由于几天前出现了无法解决的问题，一个计划任务未完成。若要在将来避免这种情况，项目经理应该怎么做？

- A. 在下一次迭代规划会上讨论该问题
- B. 在下一次迭代每日站立会上审查该问题
- C. 在演示中说明该问题
- D. 在回顾总结会议上讨论该问题

138. What should a facilitator do when they want to contribute opinions during a retrospective?

- A. Request to speak at the beginning, before the other team members.
- B. Wait until the team has expressed their opinions before speaking.
- C. Nominate another team member to facilitate before speaking.
- D. Ask the product owner to facilitate instead.

138. 促进者在回顾会议上想要提出意见时应该怎么做？

- A. 在会议开始时在其他团队成员之前要求发言。
- B. 等到团队已经发表意见后再发言。
- C. 指定另一名团队成员辅助后再发言。
- D. 让产品负责人代替其推进。

139. A distributed team is developing a consumer-facing application, The product owner expects ease of use to be a key product differentiator. The user experience expert wants to conduct usability workshops with groups of beta users to obtain early feedback. However, the budget is insufficient to cover the cost of travel. What is the best course of action to ensure product success?

- A. Use the product owner's feedback as a proxy for user feedback.
- B. Conduct tests during a video conference using screen-sharing tools to obtain user feedback.
- C. Work with the product owner to reduce scope to free up the budget for travel.
- D. Motivate the team to work faster in order to free up the budget for travel.

139. 一个分布式团队正在开发面向消费者的应用程序。产品负责人希望易用性成为关键的产品差异点，用户体验专家希望与 Beta 用户群召开可用性研讨会，以获得早期反馈。但是，预算不足以支付旅行费用若要确保产品成功，采取的最佳行动是什么？

- A. 使用产品负责人的反馈作为用户反馈代表。

-
- B. 在视频会议期间使用屏幕共享工具进行测试，获得用户反馈。
 - C. 与产品负责人合作，减少范围，腾出旅行预算。
 - D. 激励团队更快地工作，以便腾出旅行预算。

140. Your organization wants you to setup a Scrum Team for the development of a new Customer Relationship Management System. You have to decide on the ideal team size for your Scrum project. What would be one advantage of choosing a small team?

- A. Harmful over-specialization is less likely to occur.
- B. Members with more diverse skills, experiences, and approaches are included.
- C. The loss of a key person is less likely to occur.
- D. There are more opportunities for individuals to specialize in a technology.

140. 你所在组织希望你成立一个 Scrum 团队，负责开发新的客户关系管理系统。你必须确定 Scrum 项目的理想团队规模。选择小型团队有哪些优点？

- A. 降低了有害过度专业化的可能性。
- B. 成员具备更多技能、经验和方法。
- C. 失去关键人物的可能性较低。
- D. 个人有更多机会专注于技术。

141. A senior executive joins an agile team during production go-live. Following the go-live, the executive wants to know what did and did not go well during the sprint. What meeting should the executive have attended?

- A. Sprint planning
- B. Daily scrum
- C. Sprint review
- D. Retrospective

141. 一名高管在生产上线期间加入敏捷团队。在上线之后，该高管希望知道 sprint 期间哪些进展顺利以及哪些进展不顺利。该高管应已参加什么会议？

- A. Sprint 计划会议
- B. 每日 scrum 会议
- C. Sprint 评审会议
- D. 回顾会议

142. A project team is frustrated by a project manager who makes unrealistic promises to the customer and stakeholders. What should the project manager do?

- A. Apologize to the team and perform Kaizen activities to demonstrate continuous improvement.
- B. Allow the team to determine what promises should be made to the customer and stakeholders,
- C. Ask the team to work overtime to keep the promises and offer a fun team-building event as a reward.
- D. Empathize with the team's frustration but stress that customer satisfaction must be the priority.

142. 项目经理对客户和项目干系人做出不切实际的承诺，这让项目团队感到沮丧。项目经理应该怎么做？

- A. 向团队道歉，并进行改善活动，以证明持续改进。

-
- B. 让团队确定应该向客户和项目干系人做出哪些承诺。
 - C. 要求团队加班工作来守承诺，并提供有趣的团队建设活动作为奖励。
 - D. 对团队的接折深表理解，但强调客户的满意度必须是重中之重。

143. A company hires an agile coach to help resolve issues with silos and attrition. What should the agile coach recommend?

- A. Create teams with focused subject matter experts (SMEs) and continuously harness their expertise.
 - B. Encourage learning for team growth rather than individual development.
 - C. Develop teams of generalized specialists and encourage individuals to learn new skills.
 - D. Provide equal training to all team members, regardless of their experience.
143. 一家公司聘请敏捷教练帮助解决孤岛和人员损耗问题。敏捷教练应提供什么建议？
- A. 创建由主题专家(SMEs)组成的团队，并不断利用其专业知识。
 - B. 鼓励学习团队成长而不是个人发展。
 - C. 培养由通才专家组成的团队，并鼓励个人学习新的技能。
 - D. 向所有团队成员提供平等的培训，无论他们的经验如何。

144. An engineering organization changes its project management methodology to Agile Scrum. what is the best way to achieve this change?

- A. Transfer the all practices of the benchmarking organization.
- B. Have team managers monitor their team's progress on a daily basis.
- C. Transition quickly and start using Scrum in all projects.
- D. A senior executive in charge of leading this transition.

144. 一个工程机构将其项目管理方法改为敏捷 Scrum。那么实现这种转变的最佳方式是？

- A. 移植标杆企业的完整做法。
- B. 让团队经理每天监控其团队进度。
- C. 快速过渡，开始在所有项目中使用 Scrum。
- D. 让一个高级主管负责领导这次转变。

145. Agile teams are developing products based on user stories provided by teams of business analysts. After the fourth sprint, the stakeholders held a presentation, three of the completed stories passed, and the remaining two stories failed to meet the stakeholders' expectations. What should the project manager do?

- A. Ask business analysts to develop new user stories
- B. Review user stories and issue change requests
- C. Confirm stakeholder expectations, then update and rewrite user stories
- D. Start a new project to incorporate the revised user story

145. 敏捷团队正在根据商业分析师团队提供的用户故事开发产品。在第四次冲刺之后，相关方举行了一次演示，其中三个已完成的故事获得通过，其余两个故事未能满足相关方的期望，项目经理应该怎么做？

- A. 要求商业分析师开发新的用户故事
- B. 审查用户故事并签发变更请求
- C. 确认相关方的期望，然后更新并重新编写用户故事
- D. 启动一个新项目，将修订后的用户故事纳入工作范围

146. The security department has released a new compliance policy that must be followed before the next release can go live. What should the agile practitioner do?

- A. Add a non-functional requirement to system wide specifications
- B. Identify the user stories affected by the new policy and create new backlog items
- C. Update the backlog with a task that adheres to the new policy.
- D. Log the non-functional requirement as a defect

146. 在下一个版本上线之前，必须遵守安全部门已经发布的新的合规政策。敏捷管理专业人士应该怎么做？

- A. 向系统范围的规范添加非功能性需求
- B. 识别受新政策影响的用户故事，并创建新的待办事项。
- C. 用遵守新政策的任务更新待办列表。
- D. 将该非功能性需求记录为一项缺陷。

147. A product development team, new to agile, comprises equal numbers of technical specialists and non-specialists. For one project iteration, most tasks require specialists. What should the agile project manager do?

- A. Identify training for non-specialist team members and reduce silos.
- B. Encourage team members to become generalized specialists to create high-performing teams and reduce silos.
- C. Allow team members to decide how to handle the tasks as a team.
- D. Ask a specialist to work with other team members to develop a team of generalized specialists.

147. 一个新的敏捷产品开发团队拥有同等数量的技术专家和非专家。对于一次项目迭代，大部分任务都需要专家。敏捷项目经理应该怎么做？

- A. 确定非专家团队培训并减少孤岛/竖井。
- B. 鼓励团队成员成为通才专家，创造高绩效团队，减少孤岛/竖井。
- C. 让团队成员决定如何作为团队处理任务。
- D. 请一名专家与其他团队成员合作开发培养一支通才专家团队。

148. What is the benefit of having a cross-functional team when estimating new tasks?

- A. Cross-functional teams are able to compensate for missing information.
- B. Cross-functional teams are better at Affinity Estimation than other Teams.
- C. Cross-functional teams use less averaging in Planning Poker sessions.
- D. Cross-functional teams members like each other to enhance collaborations.

148. 评估新任务时，跨职能团队有什么好处？

- A. 跨职能团队能够弥补缺失的信息。
- B. 跨职能团队在类比估算上优于其他团队。
- C. 跨职能团队减少在计划扑克会议中平均数的使用。
- D. 跨职能团队的成员一定会互相喜欢，以更有效合作

149. A team must choose a project's technology framework. The team has experience with a specific framework, but now, more-effective frameworks have emerged. Using

a new framework will require additional knowledge. What should the agile team lead do?

- A. Include the need for additional knowledge in the projects priorities, and assess it against the other priorities.
- B. Use the framework in which the team members already have capabilities.
- C. Arrange training for the team as it is an opportunity for the team to acquire additional knowledge.
- D. Request new resources that have experiences with the new framework.

149. 团队必须选择一个项目的技术框架。该团队拥有特定框架的经验，但已经出现了新的更有效的框架使用新的框架将需要额外知识。敏捷团队领导应该怎么做？

- A. 将额外知识的需求包含在项目优先事项中，并与其它优先事项一起评估。
- B. 使用团队成员已具备能力的框架。
- C. 为团队安排培训，因为这是团队获得额外知识的机会。
- D. 请求拥有新框架经验的新资源。

150. A scrum master observes that the serum team needs frequent clarification from the product owner. What should the scrum master do?

- A. Maintain a whiteboard to display communication gaps to quickly resolve issues.
- B. Propose that team and the product owner are seated in close proximity in an open and shared workplace.
- C. Educate the team about the value of communication in agile.
- D. Address the issue in the retrospective, and escalate it to the product owner.

150. scrum 主管注意到 scrum 团队经常需要产品负责人澄清。scrum 主管应该怎么做？

- A. 保留一块白板显示沟通落差，快速解决问题。
- B. 建议团队和产品负责人近距离地坐在一个开放和共享的工作场所中。
- C. 教导团队敏捷的沟通价值。
- D. 在回顾会议中陈述该问题，并将其上报给产品负责人。

151. At what phase would an agile team use collaboration tools to show progress during sprints?

- A. Inception
- B. Planning
- C. Review
- D. Execution

151. 敏捷团队将在什么阶段使用协作工具在 sprint 中显示进度情况？

- A. 概念阶段
- B. 规划阶段
- C. 评审阶段
- D. 执行阶段

152. An agile team has adopted the Kanban approach. Blockages in development are clearly marked with a pink note on the Kanban board. During what meeting should these blockages be discussed?

- A. Queue replenishment
- B. Daily stand up

-
- C. Release planning
 - D. Retrospective

152. 敏捷团队已经采用 Kanban 板方法。在 Kanban 板上用粉红色批注清楚地标记开发过程中的障碍，这些障碍，应该在什么会上进行讨论？

- A. 队列补充会议
- B. 每日站会
- C. 发布计划会议
- D. 回顾会议

153. A Scrum Master would like to facilitate the team by making a visual representation of the Sprint Backlog in the form of a task board.

Which columns are minimally required to be shown?

- A. To Do, In Process, Delivered
- B. To Do, In Process, Reviewing
- C. To Do, In Process, Done
- D. To Do, In Process, Testing

153. 某 Scrum Master 想要通过任务板的形式直观展示冲刺待办事项列表，来指导团队运作。至少需要展示哪些栏目？

- A. 待办、执行中、已交付
- B. 待办、执行中、评审中
- C. 待办、执行中、已完成
- D. 待办、执行中、测试中

154. A stakeholder complains that a team sends excessive emails for approvals. The team lead notices that the team and stakeholder have isolated working spaces and little chance to interact. To resolve this issue, the team lead suggests more frequent, in-person requirements reviews. What is the team lead recommending?

- A. Osmotic communication
- B. Collaboration
- C. Colocation
- D. Pair programming

154. 一名干系人抱怨团队发送过多的电子邮件进行审批。团队领导注意到团队与该干系人的工作空间相互隔绝，几乎没有机会互动。为了解决这个问题，团队领导建议进行更频繁的面对面需求评审。团队领导建议的是什么？

- A. 渗透沟通
- B. 协作
- C. 集中办公
- D. 结对编程

155. Your company is changing to Agile Scrum working. You have been working as a project manager, but will now take on the role of Scrum Master. You will work with new co-workers in your team. What is the most successful strategy for the transition to Agile Scrum?

- A. Customize Scrum to fit with formerly used ways of working, so that the transition is made gradually.

-
- B. Do not learn too much about Agile or Scrum and keep away from other Scrum Masters until you find your way.
 - C. Let the Development Team decide the way of working, so that you do not introduce harmful behavior.
 - D. Strictly keep to the rules of Scrum, until there is more experience with Scrum and Agile working.

155. 你的公司正在向敏捷 Scrum 工作方式转变。你一直担任项目经理，但现在将承担 Scrum Master 的角色。你将与团队中的新同事共事。哪一项是向敏捷 Scrum 过渡的最成功策略？

- A. 自定义 Scrum 以适应原来的工作方式，以便逐步过渡。
- B. 在找到自己的方式之前，不要对敏捷或 Scrum 学习太多，并远离其他 Scrum Master。
- C. 让开发团队决定工作方式，这样你就不会引进有害团队的行为。
- D. 严格遵守 Scrum 规则，直到积累了更多的 Scrum 和 Agile 工作经验。

156. A scrum team meets with stakeholders to present sprint results and to demonstrate the developed product's working functionality. What does this describe?

- A. Sprint planning
- B. Sprint review
- C. Retrospective
- D. Stand up

156. Scrum 团队与干系人开会，提交 sprint 结果并展示已开发产品的有效功能。这描述的是什么会议？

- A. Sprint 计划会议
- B. Sprint 评审会议
- C. 回顾会议
- D. 站会

157. A team is reviewing the retrospective from the previous iteration. What will influence and be incorporated into the next iteration's backlog?

- A. Items on the task or kanban board that have not been started and all tasks identified in the retrospective
- B. Extra processes identified in the retrospective and defects from previous iterations
- C. Planned velocity and partially completed work from previous iterations
- D. Actual velocity averaged from previous iterations and high-priority tasks identified in the retrospective

157. 团队正在审查上一次迭代的回顾结果。哪些会影响并被纳入下次迭代的待办列表？

- A. 任务板或 Kanban 板上尚未开始的事项以及在回顾中识别到的所有任务
- B. 在回顾中识别到的额外过程和之前迭代的缺陷
- C. 之前多次迭代的计划速度和部分完成的工作
- D. 之前多次迭代的实际平均速度以及在回顾中识别到的高优先级任务

158. A team is required to deliver a critical user story to fix an issue. After starting work, a team member identifies that a dependency on another vendor has a wait time of two weeks. This wait time will impact the delivery of the current sprint's user story. What should the team member do?

-
- A. Immediately begin working with the team to identify options to accelerate and improve the process to deliver the user story on time.
 - B. During the retrospective, work with the team to identify options to accelerate and improve the process to deliver the user story in the next sprint.
 - C. Alert the vendor's account manager so that they can prepare for the next meeting
 - D. Follow the process and discuss the fixes with the vendor's account manager during the next meeting.

158. 团队需要交付一个关键的用户故事来解决一个问题。开始工作后，一名团队成员识别到对另一个供应商的依赖关系有两个星期的等待时间。这个等待时间将影响当前 sprint 的用户故事交付。该团队成员应该怎么做？

- A. 立即开始与团队合作，确定方案，加快速度并改进流程，按时交付用户故事
- B. 在回顾会议上与团队合作，确定方案，加快速度并改进流程，在下一次 sprint 交付用户故事。
- C. 提醒该供应商的客户经理，让他们可以准备下一次会议。
- D. 遵循流程，并在下一次会议上与供应商的客户经理讨论解决方案。

159. A team is building a product in three-week iterations. During the last retrospect, it was identified that there was a 20 percent increase from previous iterations in the number of reported defects and change requests. Since this is causing the product's value to decrease, what should the team do?

- A. Run a sprint to clear all reported defects before taking new stories.
- B. Change the control mechanism so that items are better tested before delivery.
- C. Increase the opportunities to confirm common understanding with the client.
- D. Reevaluate the duration of the cycles, as faster cycles may allow for earlier detection of defects.

159. 团队正在为期三周的迭代中构建一个产品。在上一次回顾会议中，已识别到报告的缺陷和变更请求数量比之前的迭代增加了 20%。由此导致产品价值下降，团队应该怎么做？

- A. 运行一次 sprint，清除所有报告的缺陷，然后再进行新的故事。
- B. 更改控制机制，让产品在交付前更好地进行测试。
- C. 增加与客户确认共识的机会。
- D. 重新评估周期的持续时间，因为更快的周期可能允许较早的缺陷检测。

160. Agile team members regularly update their work items and visualize them through information radiators. The scrum master reviews the project's status with stakeholders using release burn down charts as visual indicators. After several iterations, more information and clarity causes the overall project estimation to change. How can the scrum master express this change for stakeholders during the review meeting?

- A. Display approval notifications from the change control board (CCB).
- B. Annotate release burn down charts with the changes in the top right corner.
- C. Use release burn up charts rather than release burn down charts.
- D. Ask a specialized team member to speak about the changes.

160. 敏捷团队成员定期更新自己的工作项，并通过信息发射源将其可视化。Scrum 主管使用发布燃尽图作为视觉指标，与干系人一起评估项目的状态。经过几次迭代，更多信息和澄清引起整个项目估算发生变更。评审会议期间 Scrum 主管如何向干系人表达这一变更？

-
- A. 展示变更控制委员会 (CCB) 的批准通知。
 - B. 在发布燃尽图右上角注释变更。
 - C. 使用发布燃起图，而不是发布燃尽图。
 - D. 让一名专业团队成员谈谈这些变更。

161. During a project's last iteration, an agile team struggled with a feature's delivery due to the lack of a required skill. The project has already incurred a five-day delay. A further delay of at least 10 days is anticipated. What should the agile team lead have done to avoid this situation?

- A. Ensured that the team was comprised of cross-functional, generalized specialists
- B. Provided just-in-time training of the required skill to specific team members
- C. Assigned the feature to another agile team that had members with the required skills
- D. Lowered the feature's priority until a team member acquired the skill to build it

161. 在项目的最后一次迭代期间，由于缺乏必要的技能，敏捷团队在交付某项功能过程中陷入困境。项目已经延期五天了。但预计还要至少延期 10 天。敏捷团队领导事先应该怎么做来避免这种情况？

- A. 确保团队由跨职能的通用的专才专家组成
- B. 为特定团队成员提供所需技能的适时培训
- C. 将该功能分配给具有所需技能成员的另一个敏捷团队
- D. 降低该功能的优先级，直到一名团队成员掌握构建该功能的技能为止

162. Users report a major issue that needs to be fixed. This fix will require expensive changes to the product's architecture. What should the team do?

- A. Raise it as an issue, discuss it with the product owner, and take appropriate action.
- B. Make incremental changes to the architecture and keep stakeholders informed.
- C. Remove user access to the feature until it is fixed.
- D. Allow the issue to exist while the team makes an incremental fix for the long term.

162. 用户报告一个重大问题，需要修复。这项修复将需要对产品架构进行昂贵的变更。团队应该怎么做？

- A. 将其作为问题提出，与产品负责人讨论，并采取适当的行动。
- B. 对架构进行增量变更，并通知干系人
- C. 删除用户对该功能的访问权限，直到修复为止。
- D. 允许问题存在，同时团队长期进行增量修复。

163. A customer complains about the response time of an application under development. The team suspects that this is due to the poor performance of database queries, but the required skill set to fix the issue is lacking. What should the agile team do to overcome this problem.

- A. Designate one team member to take ownership of and resolve all database-related problems.

B. Perform a root cause analysis and, if required, ask a subject matter expert (SME) to fix the issue.

C. Hire an expert in database performance to resolve the issue in one sprint.

D. Make the last sprint of the development cycle a performance sprint and fix the issue during that sprint.

163. 客户抱怨一个正在开发中的应用程序响应时间。团队怀疑这是由于数据库查询的性能不佳，但缺少解决该问题所需的技能。若要克服这个问题，敏捷团队应该怎么做？

A. 指定一名团队成员负责并解决所有与数据库有关的问题。

B. 执行根本原因分析，且如果需要，请一名主题专家(SME)解决该问题。

C. 请一名数据库性能方面的专家，在一次 sprint 中解决问题。

D. 让开发周期的最后一次 sprint 成为一次性能 sprint，并在该 sprint 期间解决问题。

164. When working on a new product, what should an agile team do to ensure alignment with external stakeholders?

A. Ask the product owner for a detailed product-specification document.

B. Review the project vision statement.

C. Hold a kick-off meeting to assign roles.

D. Work with the scrum master to ensure that agile principles are followed.

164. 在为新产品工作时，敏捷团队应该如何确保与外部干系人保持一致？

A. 要求产品负责人提供详细的产品规范文件

B. 查看项目愿景说明书。

C. 召开项目启动大会分配角色。

D. 与 scrum 主管合作，确保遵循敏捷原则。

165. A project is being executed by a virtual team spread across multiple geographic locations. What will help the team work together?

A. Ensuring for the project's duration that all team members are not co-located

B. Using collaboration tools to enable closer communication

C. Executing one sprint in one geographic location and the other sprints remotely

D. Executing the first half of the sprints in one geographic location and the last half remotely

165. 一个项目正在由分布在多个地理位置的虚拟团队执行。哪项将有助于团队合作？

A. 确保项目持续时间内，所有团队成员没有集中办公

B. 使用协作工具实现更密切的沟通

C. 在一个地理位置执行一个 sprint，在远程执行另一个 sprint

D. 在一个地理位置执行一半 sprint，在远程执行另一半 sprint

166. What is one critical aspect of a daily stand up?

A. Coordinating

B. Reestimating

C. Planning future sprints

D. Communicating lessons learned

166. 每日站会的一个关键方面是什么？

A. 协调

B. 重新估算

-
- C. 规划未来 sprint
 - D. 沟通经验教训

167. Who is responsible for assigning tasks to a team member?

- A. Product owner
- B. Scrum Master
- C. Development team
- D. A team member

167. 谁负责为某个团队成员分配任务？

- A. 产品负责人
- B. Scrum Master
- C. 开发团队
- D. 某个团队成员

168. A now agile project manager accepts a position with a team in a start-up environment. During a company meeting, the project manager notices that decision-making occurs informally from the bottom up, and creative invention is prioritized. What type of organizational paradigm does this describe?

- A. Synchronous
- B. Collaborative
- C. Hierarchical
- D. Random

168. 新敏捷项目经理在团队处于启动环境时接受职位。在公司会议期间，项目经理注意到决策是非正式地自下而上发生，且优先考虑创意发明。这描述的是哪种组织范式类型？

- A. 同步
- B. 协作
- C. 等级
- D. 随机

169. Suppose you track the progress of a sprint through a burnout chart. You add a line to the chart to indicate the planned progress and find that the actual progress line is above the planned line. What does this mean?

- A. You are ahead of schedule.
- B. You need to redraw in order to overlap.
- C. You did not plan well
- D. You are behind schedule.

169. 假设你通过燃尽图追踪冲刺进度。你在图中添加一条线表示计划的进度，发现实际进度线在计划线的上方。这说明什么？

- A. 你的进度超前了。
- B. 你需要重新绘制以便重合。
- C. 你没有进行很好的规划
- D. 你落后于进度

170. An agile team member is trying to understand the status of the iteration on which the team is currently working. What information radiator will help?

-
- A. Iteration backlog
 - B. Sprint plan
 - C. Iteration burn down chart
 - D. Release plan

170. 一名敏捷团队成员正在尝试了解团队目前进行的迭代的状态。哪一项信息发射源将提供帮助？

- A. 迭代待办列表
- B. Sprint 计划
- C. 迭代燃尽
- D. 发布计划

171. While conducting a series of design-idea workshops, a product delivery team identifies a new area of its business that will be impacted by their product's introduction. What should the agile coach do to ensure that this organizational impact is addressed?

- A. Meet with the team, client, and stakeholders to discuss new requirements and priorities.
- B. Incorporate any identified needs at the bottom of the product backlog.
- C. Ask the sponsor whether the project scope should be modified.
- D. Discuss changing the priorities with the product owner.

171. 在开展一系列设计创意研讨会时，产品交付团队识别出将受到产品引入影响的业务新领域。若要确保解决这种组织影响，敏捷教练应该怎么做？

- A. 与团队、客户和干系人开会，讨论新的需求和优先级。
- B. 将识别到的任何需求纳入产品待办列表底部。
- C. 询问发起人是否应修改项目范围。
- D. 与产品负责人一起讨论变更优先级。

172. You want to convince customers of the benefits of Agile. What is the main benefit of Agile for the customer?

- A. Agile will definitely help to complete customer projects sooner.
- B. Agile enables the client to get a better management on day-to-day activities.
- C. Agile helps the team incorporate changes into the project at no additional cost
- D. Agile ensures that the client can get value early in the project

172. 你希望说服客户相信敏捷的好处。对客户而言，敏捷的主要好处是什么？

- A. 敏捷一定更早的完成客户项目。
- B. 敏捷能够让客户更好地掌握日常活动。
- C. 敏捷有助于团队在不花费额外成本的情况下将变更纳入项目中
- D. 敏捷确保客户能够在项目早期就获得价值

173. A product owner indicates that a competitor has released a new product version with features that are not part of the current backlog. The product owner suggests revisiting the product backlog, which could lead to a significant change in the plan and disrupt the team. What should the team do?

- A. Hold a team meeting and accept this suggestion only if the team agrees
- B. Create a buffer in the estimates to accommodate any changes.

C. Add the new features to the product backlog, then reprioritize the backlog and continue development based on the new priorities.

D. Add the new features to the backlog and work on them after all high-priority items have been completed.

173. 产品负责人表示竞争对手已经发布了一款新产品版本，拥有不属于当前待办列表组成部分的功能。产品负责人建议重新审视产品待办列表，这可能导致计划发生重大变化并扰乱团队。团队应该怎么做？

A. 召开一次团队会议，并只有在团队一致同意的情况下接受这一建议。

B. 在估算中创建一个缓冲以适应任何变更。

C. 将新功能添加到产品待办列表中，然后重新确定待办列表的优先级，并根据新的优先级继续开发。

D. 将新功能添加到待办列表中，并在所有高优先级事项均完成后再对其进行处理。

174. Reduced velocity in a project's fifth sprint has resulted in the team failing to deliver its sprint goal. Management wants the team to address this. What should the agile project manager do?

A. Delay the start of sprint six, arrange team-building exercises, and provide performance guidelines for the next sprint.

B. Add expert resources to increase productivity in the next sprint.

C. Engage an external consultant to evaluate team members, productivity.

D. Allow the team to self organize and facilitate a discussion during the retrospective.

174. 项目第五次 sprint 的速度降低导致团队未能交付其 sprint 目标。管理层希望团队解决这个问题。敏捷项目经理应该怎么做？

A. 延迟开始第六次 sprint，安排团队建设活动，并为下一次 sprint 提供绩效指南。

B. 增加专家资源，提高下一次 sprint 的生产力。

C. 聘请外部顾问来评估团队成员的生产力。

D. 让团队自我组织，并在回顾会议上推进讨论。

175. A senior team member often solves issues without informing the team. What should the agile coach do?

A. Congratulate the senior team member for promoting value delivery and saving time.

B. Work with the project manager to find a solution.

C. Discuss the issue with senior management at the next retrospective.

D. Explain to the senior team member that all issues should be visible and jointly solved by the team

175. 高级团队成员经常在不通知团队的情况下解决问题。敏捷教练应该怎么做？

A. 祝贺该高级团队成员促进价值交付和节省时间。

B. 与项目经理合作找出解决方案。

C. 在下次回顾会议中与高级管理层讨论该问题。

D. 向该高级团队成员解释，所有问题都应由团队明确并共同解决。

176. A traditional project manager assumes an agile project in an organization trying to adapt agile practices. What should the project manager do to achieve success?

A. Assist team members with their assigned work.

-
- B. Help tackle issues facing the customer.
 - C. Ensure that all team members have the appropriate resources.
 - D. Evenly delegate work assignments to maintain team balance.

176. 一位传统项目经理在一个尝试采用敏捷实践的组织中负责管理一个敏捷项目。若要获得成功，项目经理应该怎么做？

- A. 协助团队成员完成分配给他们的工作。
- B. 帮助解决客户面对的问题。
- C. 确保所有团队成员都有适当的资源。
- D. 平均分配工作任务来维持团队平衡。

177. An agile team consistently delivers planned user stories in each iterative cycle. Later, the end customer expresses concern about the final deliverables. How would frequent reviews help this situation?

- A. By helping the team strategically plan and achieve their goals
- B. By helping the team obtain final sign-offs from stakeholders
- C. By showcasing the team's achievements to stakeholders
- D. By allowing the team to get frequent feedback and make improvements

177. 敏捷团队在每个迭代周期中持续交付计划的用户故事。后来，终端客户对最终可交付成果表示担忧。频繁的评审会将如何有助于这种情况？

- A. 通过帮助团队策略性地计划和实现目标
- B. 通过帮助团队获得干系人的最终签署同意
- C. 通过向干系人展示团队的成就
- D. 通过让团队获得频繁的反馈并改进

178. An agile team is developing a valuable software feature. During a daily stand up, a project manager invites the team to a demo of a competitor's software with a similar feature. What should the agile team lead do?

- A. Send the team to the demo to obtain more insight on how the feature can be better developed to generate increased ROI.
- B. Send the product owner to the demo to obtain more knowledge about market trends, and allow the team to continue focusing on planned work.
- C. Send one developer to the demo so that the other developers can focus on planned work.
- D. Send a team tester to the demo so that the developers can planned Work.

178. 敏捷团队正在开发一个有价值的软件功能。在每日站会上，项目经理邀请团队参加具有类似功能的竞争对手软件演示。敏捷团队领导应该怎么做？

- A. 派团队参加演示，以获得有关如何更好地开发功能以产生更高投资回报率的更多见解。
- B. 派产品负责人参加演示，以获得有关市场趋势的更多知识，并让团队继续专注于计划的工作。
- C. 派一名开发人员参加演示，让其他开发人员可以专注于计划的工作。
- D. 派一名团队测试人员参加演示，开发人员可以专注于计划的工作。

179. A team regularly hits external dependencies that prevent them from completing stories by the end of a sprint. The team needs to know what to expect in future sprints. How far ahead should the team look at their backlog?

-
- A. As many sprints as external dependencies affect.
 - B. Since agile encourages adaptive planning, one sprint is sufficient.
 - C. Since agile teams execute and learn, tasks should be adapted accordingly.
 - D. Just enough to maintain the backlog grooming process.

179. 一个团队经常抨击外部依赖关系妨碍他们在 sprint 结束之前完成故事。团队需要知道未来的 sprints 预期。团队在看待办列表时应该向前看多远？

- A. 受外部依赖关系影响的尽可能多的 sprint。
- B. 由于敏捷鼓励适应性规划，一个 sprint 就足够了。
- C. 由于敏捷团队的执行和学习，任务应进行相应调整。
- D. 仅足以保持待办列表梳理过程即可。

180. An agile team approaches the third sprint of a project that has been following two-week sprints. During the previous two sprints, the team was unable to complete the majority of user stories to which they had committed. The product owner suggests that sprint lengths be changed to four weeks. What should the agile team do?

- A. Accept the product owner's recommendation based on their knowledge of the product vision.
- B. Work with the product owner to revise user stories to fit a two-week sprint.
- C. Refer to the project management organizations (PMO) knowledge repository on changing sprint length.
- D. In the retrospective, identify the root cause of the incomplete user stories before deciding on next steps.

180. 敏捷团队临近进行一个项目的第三次 sprint，该项目已经采用了两周 sprint 的形式。在前两次 sprint 期间，团队无法完成他们所承诺的大部分用户故事。产品负责人建议将 sprint 长度更改为四周。敏捷团队应该怎么做？

- A. 根据他们对产品愿景的了解，接受产品负责人的建议。
- B. 与产品负责人合作，修改用户故事以适应为期两周的 sprint。
- C. 参考项目管理组织（PMO）知识库中变更 sprint 长度的相关内容。
- D. 在回顾会议中，确定未完成用户故事的根本原因，然后再决定下一步。
