
PMP®敏捷部分测试题（二）

PMP 敏捷部分测试题（二）

1. 本套测试题共有 180 道单选题，测试时间为 3 个小时， **闭卷答题！** 正确率要求答对 126 题（70%）或以上。
2. 本套测试题尽可能地覆盖 PMP 考试的题型，请学员们集中精力在 3 个小时内完成，达到全真的模拟效果
3. 模拟考试过程中，调整思维，揣摩考题的意图；考试结束后，认真总结。
4. 解题策略：TKSC 策略
T（topic）真正读懂题目
K（key）迅速抓住考点
S（source）准确找到出处
C（choice）果断做出选择

1. An experienced team member fails to attend daily stand ups which causes them to fall behind on review activities. What should the agile practitioner do?

- A. Ask management for a resolution.
- B. Remind the team member about the ground rules.
- C. Inform the product owner.
- D. Request that the team member be replaced.

1. 一名经验丰富的团队成员没有参与每日站会，导致他们落后于审查活动。敏捷管理专业人士应该怎么做？

- A. 要求管理层解决。
- B. 提醒该团队成员基本规则。
- C. 通知产品负责人。
- D. 要求替换该团队成员。

2. A cross-functional team is working on a complex project with frequently changing requirements. What methodology should the team use to enhance the process?

- A. Scrum
- B. Kanban
- C. Extreme programming (XP)
- D. Feature-driven development (FDD)

2. 一个跨职能团队正在开展一个复杂项目，该项目的需求不断发生变化。团队应使用什么方法来改进这个过程？

- A. Scrum
- B. 看板
- C. 极限编程（XP）
- D. 功能驱动开发（FDD）

3. A globally distributed agile team is scheduled to launch a product next year. The sponsor's key objective is to sell a certain number of products globally, another department sets a goal to drive innovation. The agile team realizes that if the innovation goal is realized, product performance will decrease and affect the sponsor's key objective.

What should the agile team do to align the department's goal with the sponsor's key objective?

- A. Inform senior stakeholders of the department's goal and align everyone to the key objective.
- B. Inform the sponsor and relevant stakeholders of the misalignment, and commit to only fulfilling the key objective.
- C. Ask the department to withhold sharing any created innovations.
- D. Ask the sponsor and relevant stakeholders to determine the department goal's feasibility in connection with the key objective.

3. 一支全球分布式敏捷团队计划明年推出一款产品。项目发起人的主要目标是在全球销售一定数量的产品；另一个部门设定了推动创新的目标。敏捷团队意识到，如果实现创新目标，产品性能将会下降，并影响到项目发起人的关键目标。

若要让该部门的目标与项目发起人的关键目标保持一致，敏捷团队应该怎么做？

- A. 向高级项目干系人通报该部门的目标，让每个人都与关键目标保持一致。

-
- B. 通知项目发起人和相关项目干系人不一致之处，并承诺只履行关键目标。
 - C. 要求改部门暂停分享任何新的创新。
 - D. 要求项目发起人和相关干系人确定部门目标与关键目标相关性的可行性。

4. The executive sponsor who authorized the project informs the product owner that they want to review the project when it nears completion. What should the product owner do?

- A. Run the project by making decisions on behalf of the executive sponsor.
 - B. Insist on regular reviews with the sponsor and provide them with frequent updates.
 - C. Invite the sponsor to all review meetings.
 - D. Send regular updates to the sponsor.
4. 批准项目的执行发起人通知产品负责人，他们希望在项目快完成时审查项目。产品负责人应该怎么做？
- A. 通过代表执行发起人作出决定来执行项目。
 - B. 坚持与发起人进行定期审查，并频繁地为他们提供更新。
 - C. 邀请发起人参加所有评审会议。
 - D. 向发起人定期改善更新。

5. During a review meeting an agile team establishes that a release backlog cannot be completed within the mandated timeframe. What should the team do?

- A. Review the scope with the product owner.
- B. Email the product owner with a revised completion date.
- C. Reprioritize the product backlog and remove its least valuable stories.
- D. Meet with the product owner to discuss the scope and schedule.

5. 在审查会议期间，敏捷团队确定在规定的时间内不能完成某个版本的代办列表。团队应该怎么做？

- A. 与产品负责人一起审查范围。
- B. 向产品负责人改善一封修正过的完成日期的电子邮件。
- C. 对产品代办列表重新排列优先顺序，并删除最没有价值的故事。
- D. 与产品负责人开会讨论范围和进度计划。

6. Some executive sponsors disagree with certain product features, as they hamper their business agenda and are contradictory. What should the product owner do?

- A. Organize a demo for all executive sponsors to explain the features.
- B. Hold a one-on-one meeting with each executive sponsor.
- C. Arrange a meeting with all executive sponsors to resolve the conflict.
- D. Allow the executive sponsors to independently resolve the conflict.

6. 一些执行发起人不同意某些产品功能，因为它们阻碍了发起人的业务进程并且与其矛盾。产品负责人应该怎么做？

- A. 为所有执行发起人组织一次演示，说明这些功能。
- B. 与每名执行发起人召开一对一的会议。
- C. 安排与所有执行发起人召开一次会议来解决冲突。
- D. 让执行发起人独立解决冲突。

7. An external stakeholder likes to track the number of defects found. Although all defects have been fixed, they want to know why more defects were introduced during the last few sprints.

What should the team do?

- A. Stop sharing this information with that stakeholder.
- B. Share only high-severity defects that significantly impact product quality with that stakeholder.
- C. Conduct team-building activities to increase motivation and improve quality.
- D. Ask that stakeholder to obtain clarification from the product owner.

7. 一名外部干系人希望跟踪已发现的缺陷数量。虽然所有缺陷均已修复，但他们想知道为什么在最后几个 sprint 中生产更多缺陷。

- A. 停止与该干系人分享这些信息。
- B. 仅向该干系人分享显著影响产品质量的高严重性缺陷。
- C. 开展团队建设活动，增加激励，提高质量。
- D. 请该干系人从产品负责人处获得澄清。

8. Members of a scrum team have frequent misunderstandings with another team that uses Kanban. What should the two teams do?

- A. Document major decisions in order to facilitate retrospective review sessions.
- B. Identify architectural risks that result from cross-team misunderstandings.
- C. Establish a common vocabulary that both teams will use for communication.
- D. Ask the division manager to require the use of a single agile methodology.

8. Scrum 团队的成员对使用看板的另一个团队不断有误解。两个团队应该怎么做？

- A. 记录主要决策，以便引导回顾评审会议。
- B. 识别造成跨国团队误解的架构风险。
- C. 制作一份两个团队可用来沟通的常见词汇表。
- D. 让部门经理要求使用一种敏捷方法。

9. A project manager is concerned that the team's expectations are misaligned with some stakeholders, and that user stories were written only from a generic user's perspective. This may lead the team to miss stories for non-generic users.

What agile tools can help the team address these issues?

- A. Wireframes
- B. Story maps
- C. Process flows
- D. Personas

9. 项目经理担心团队的期望与一些干系人不一致，且用户故事只是从一般用户的角度来编写。这可能导致团队遗漏非一般用户的故事。哪些敏捷工具可以帮助团队解决这些问题？

- A. 线框图
- B. 故事地图
- C. 过程流图
- D. 人物角色

10. What should an agile practitioner do if team members express that they feel overworked and stressed?

-
- A. Discuss the potential root causes and analyze what needs to change.
 - B. Work with the product owner to identify additional resources.
 - C. Address the issue if it negatively affects velocity but add it to the backlog.
 - D. Ask the product owner to push back the delivery date.
10. 如果团队成员表示他们感到过度劳累和压力，敏捷管理专业人士应该怎么做？
- A. 讨论潜在的根本原因，并分析什么需要改变。
 - B. 与产品负责人合作，识别其他资源。
 - C. 陈述对速度有负面影响的问题，但将其添加到待办列表中。
 - D. 请产品负责人将交付日期向后退。

11. A team completes two sprints containing customer-valued functionality. For estimation purposes, the agile practitioner needs to identify information about an unknown aspect of a user story. What should the agile team use?

- A. Risk-based burn up chart
- B. Risk-adjusted backlog
- C. Risk-based spike
- D. Risk burn down graph

11. 团队完成了两个包含客户价值功能的 sprint。为了估算，敏捷管理专业人士需要识别关于用户故事未知方面的信息。敏捷团队应使用什么？

- A. 基于风险的燃起图
- B. 已调整风险的待办列表
- C. 基于风险的刺探
- D. 风险燃尽图

12. A new agile team member experiences difficulty with transferring development work to the operations team for test deployment. What should the agile practitioner recommend to the member?

- A. Working with other team members to learn and understand the transfer process
- B. Using a solution previously implemented by the team
- C. Meeting with involved stakeholders to identify a solution
- D. Updating the risk register to include the transfer process

12. 在要将开发工作转移给运营团队进行测试部署时，一名新的敏捷团队成员遇到困难，敏捷管理专业人士应向该团队成员提供什么建议？

- A. 与其他团队成员一起学习并了解转移过程。
- B. 使用团队之前实施的解决方案。
- C. 与相关干系人会面以找出解决方案。
- D. 更新风险登记册以包含该转移过程。

13. An agile practitioner notices a new story on the product backlog that is vague and missing the acceptance criteria. At what point in the sprint cycle should the agile practitioner ask the product owner for more detail?

- A. During the backlog grooming meeting
- B. During the sprint retrospective
- C. During the daily scrum
- D. During the iteration review meeting

13. 敏捷管理专业人士注意到产品待办事项上一个新故事很模糊，缺少验收标准。敏捷管理专业人士应在 sprint 周期中的哪个时间点要求产品负责人提供更多详情？

- A. 在待办事项梳理会上。
- B. 在 sprint 回顾会议上。
- C. 在每日 scrum 期间。
- D. 在迭代评审会上。

14. During a daily stand up, a team member mentions that the product owner has been missing appointments. What should the agile project manager do?

- A. Speak with the team member to confirm that the product owner's availability is not affecting progress and add the issue to the risk board.
- B. Ask other team members if they have experienced the same issue then discuss options to resolve it.
- C. Invite the product owner to the next stand up and ensure that all communications are up to date.
- D. Speak with the product owner about their availability and request that more of their time be dedicated to the team.

14. 在每日站会上，一名团队成员提到产品负责人总是失约。敏捷项目经理应该怎么做？

- A. 与该成员交谈，确认产品负责人的可用性不会影响进度，并将该问题添加到风险板上。
- B. 询问其他团队成员他们是否遇到同样问题，然后讨论方案来解决该问题。
- C. 邀请产品负责人参加下一次站会，确保所有沟通都是最新的。
- D. 与产品负责人谈谈他们的可用性，并要求他们在团队上投入更多时间。

15. An agile project resource splits work time between teams A and B. Members from team A complain that the resource is not engaging and creates multiple challenges due to unavailability. What should team A do?

- A. Encourage the resource to be transparent and discuss the issue during the next retrospective.
- B. Understand that the resource is split between two projects and independently work out any issues that arise.
- C. Escalate the issue to the resource's manager to resolve the lack of communication.
- D. Work with team B to split up the resource's hours to accommodate both teams.

15. 一名敏捷项目资源在团队 A 和 B 之间分配工作时间。团队 A 的成员抱怨该资源参与性不够，并由于其不可用造成多重挑战。团队 A 应该怎么做？

- A. 激励该资源透明化，并在下一次回顾会议中讨论这个问题。
- B. 理解该资源在两个项目之间分配时间，并独立解决出现的任何的问题。
- C. 将该问题升级上报给该资源的经理，解决缺乏沟通的问题。
- D. 与团队 B 合作分配该资源的时间，以适应两个团队的需求。

16. A product owner has limited time to spend on the project and is unable to validate completed work. The team lead still needs to ensure that requirements are met. What should the team lead do?

- A. Ensure the product owner's commitment to the project by meeting with them directly.
- B. Confront the product owner at the next stand up meeting.
- C. Distribute a memo on agile principles to the product owner and supervisor.

D. Escalate the issue and request a new product owner.

16. 产品负责人在项目上花费的时间有限，无法核实已完成的工作。但敏捷团队领导仍需要确保所有需求得到满足。敏捷团队领导应该怎么做？

- A. 确保产品负责人通过直接与他们开会参与项目。
- B. 在下次站会中与产品负责人当面对质。
- C. 将符合敏捷原则的备忘录分发给产品负责人和主管。
- D. 将问题上报并请求一名新的产品负责人。

17. Coding for a project has finished, however, the team failed to detect a number of defects. In the future, what should the agile team do to avoid this?

- A. Determine the acceptance criteria of the coding and/or testing before the sprint begins.
- B. Ensure that developers create more-detailed code by shortening the iteration lengths.
- C. Use a requirements traceability matrix to provide transparency back to specifications.
- D. Add resources to the testing team to ensure that ideal test cases are developed.

17. 一个项目的编码已经完成，然而，团队未能检测到一些缺陷。今后，敏捷团队应该怎么做才能避免这种情况？

- A. 在 sprint 开始前确定编码和/或测试的验收标准。
- B. 确保开发人员通过缩短迭代时间长度来创造更详细的代码。
- C. 使用需求跟踪矩阵，提供返回技术规格的透明性。
- D. 测试团队增加资源，确保开发理想的测试用例。

18. After several iterations, an agile practitioner notices that a technology issue continually impacts team productivity. What should the practitioner do?

- A. Brainstorm solutions during the iteration retrospective.
- B. Suggest changes to the technology governance process.
- C. Share previous lessons learned to improve efficiency.
- D. Escalate the issue to the product owner for support.

18. 在多次迭代后，一名敏捷项目管理师注意到一个技术问题持续影响团队的执行效率。敏捷项目管理师应怎么做？

- A. 在迭代回顾会议上头脑风暴解决方案。
- B. 建议对技术管理过程进行变更。
- C. 分享之前的经验教训，改进效率。
- D. 将问题升级上报给产品负责人，获得支持。

19. The agile team completed the product development phase and verified that all tests have passed, but that customer reports dissatisfaction with quality and performance. What should the agile project team have done before product release to avoid this situation?

- A. Held a retrospective to validate project deliverables
- B. Performed a review of all requirements
- C. Obtained approval from the project sponsor
- D. Captured feedback from stakeholders at scheduled demos

19. 敏捷团队完成了产品开发阶段，并核实所有测试均已通过，但客户报告对质量和性能不满意，若要避免这种情况，敏捷项目团队应该在产品发布之前做什么？

- A. 召开一次回顾会议，核实项目可交付成果。
- B. 执行对所有需求的评审。
- C. 获得项目发起人的批准。
- D. 在计划的演示中，收集项目干系人反馈。

20. Due to lengthy technical explanations for implemented features, the last two demos took longer than scheduled. What should the agile practitioner do?

- A. Remind the team and the stakeholders that two hours is the maximum length for a review meeting.
- B. Shorten regular iteration durations, have more frequent review meetings, and discuss less new functionality per meeting.
- C. Coach the product owner and team to timebox future review meetings, and remind them of their purpose.
- D. Organize refreshments for the next review meeting, and plan to have an intermediate break.

20. 由于对已实施特性的技术说明时间较长，最后两个演示花费的时间比计划长，敏捷管理专业人士应该怎么做？

- A. 提醒团队项目关系人评审会议的最长时间为两小时。
- B. 缩短定期迭代持续时间，更频繁地召开评审会议，并且在每次会议上较少讨论新功能。
- C. 教导产品负责人和团队确定未来评审会议的时间盒，并提醒他们这些会议的目的。
- D. 组织下一次评审会议的茶歇，并计划中间休息时间。

21. An experienced team member notices that a new team member consistently misses iteration commitment. What should the experienced team member do?

- A. Ask the team member to assign the commitment to the agile practitioner.
- B. Ask the team member's manager to speak with them.
- C. Ask the scrum master to apply pressure on the team member.
- D. During the retrospective, coach the team on how to better estimate.

21. 一名经验丰富的团队成员注意到，一名新团队成员总是不能兑现承诺，该经验丰富的团队成员应该做什么？

- A. 要求该团队成员将该承诺分配给敏捷管理专业人士。
- B. 要求该团队成员的经理与其谈话。
- C. 要求 scrum 主管对该团队成员施加压力。
- D. 在回顾会议上，教导团队如何更好地估算。

22. An agile team is developing product to be integrated with a customer's system. The system is frequently changed and some releases fail the integration test. What should the agile practitioner do?

- A. Ask the customer to make less frequent changes to the system and re-test the failed release in integration.
- B. Advise the team to do additional testing before each release.
- C. Delegate the problem to an integration subject matter expert (SME).
- D. Implement a feedback loop between the project team and the customer.

22. 敏捷团队正在开发一个即将与客户系统集成在产品。系统频繁更改，某些版本未能通过集成测试。敏捷管理专业人士应该怎么做？

- A. 要求客户不要那么频繁地更改系统，并在集成中重新测试失败的原因。
- B. 建议团队在每次发布版本前进行额外的测试。
- C. 将问题分配给集成主题专家（SME）。
- D. 在项目团队和客户之间实施反馈回路。

23. An agile team lead notices that the team is hesitant to voice their opinions. What should the agile team lead advise the team to facilitate communication?

- A. The dedicated to the outcome.
- B. Follow a common strategy.
- C. Feel free to share ideas.
- D. Use a shared workspace.

23. 一名敏捷团队领导注意到团队不愿意表达他们的意见，为引导沟通，敏捷团队领导应该向团队提出什么建议？

- A. 专注于结果。
- B. 遵循共同的策略。
- C. 自由分享想法。
- D. 使用共享工作区。

24. An organization rewards team members by inviting them to a lunch-and-learn track where employees introduce new technologies. An agile team member, more interested in contributing to the lunch-and-learn than working on a project's deliverables, is not adhering to due dates. What should the team lead do?

- A. Work with the team member to schedule a few hours per week for researching new technologies.
- B. At the next meeting, address the issue, and discuss how to conduct research as a team.
- C. Ask the team member to conduct research on new technologies outside of project hours.
- D. Allow the team member to continue researching new technologies, and ask other team members

to help with the incomplete deliverables.

24. 一家组织通过邀请团队成员参加午餐学习活动来奖励团队成员，在该活动上员工将会介绍新技术，一名敏捷团队成员对参与午餐学习活动比从事项目可交付成果工作更感兴趣，因而没有遵守截止日期。团队领导应该怎么做？

- A. 与该团队成员一起，每周安排几小时来研究新技术。
- B. 在下一次会议上陈述这个问题，并讨论如何作为一个团队进行研究。
- C. 要去该团队成员在项目时间之外进行新技术的研究。
- D. 允许该团队成员继续研究新技术，并让其他团队成员帮助其完成未完成的交付成果。

25. An agile project involving multiple stakeholders provides solutions to numerous customers. The agile team is responsible for responding to urgent production issues within a very aggressive timeframe. Lately, production issues have been a common occurrence, and customers require immediate fixes.

What should the agile team do to prevent a recurrence of this situation?

-
- A. For every new customer commitment, add 20 percent to the schedule as contingency time.
 - B. Regularly meet with stakeholders to review ongoing projects and critical defects, and devise plans to mitigate potential risks impeding delivery.
 - C. Advise stakeholders to review expectations with their customers to reflect attainable deliverables.
 - D. Add an action item to the backlog to assess the root cause for the production issues, and address the threats to other deliverables.

25. 涉及多个项目干系人的敏捷项目为众多客户提供解决方案。敏捷团队负责在非常紧迫的时间里对紧急生产问题做出响应。最近，生产问题经常发生，客户要求立即修复。

若要防止再次发生这种情况，敏捷团队应该怎么做？

- A. 对每个新的客户承诺，都增加 20%的进度计划时间作为应急时间。
- B. 定期情形项目干系人开会审查正在进行的项目和关键缺陷，并制定计划，以减轻阻碍交付的潜在风险。
- C. 建议项目干系人与客户一起审查期望，以反映可实现的可交付成果。
- D. 将一个行动项添加到待办列表中，评估生产问题的原因，并陈述其他可交付成果的威胁。

26. Two agile team members experience personal conflicts that will impact team performance. What should the agile team do?

- A. Allow the team members to resolve their differences independently.
- B. Request the transfer of one team member so that team decisions remain neutral.
- C. Discuss it in the retrospective and resolve the conflicts as a team.
- D. Ask the team members to remain professional by putting aside their personal conflicts.

26. 两名敏捷团队成员之间发生个人冲突，将会影响团队绩效，敏捷团队应该怎么做？

- A. 让这两名团队成员独立解决差异。
- B. 请求调走其中一名团队成员，以便团队决策保持中立。
- C. 在回顾会议上讨论该问题，并作为一个团队解决该冲突。
- D. 要求两名团队成员保持专业，抛开个人冲突。

27. A project owner is struggling to write a user story for a complex feature. What should the agile practitioner do to address this?

- A. Work with the product owner to divide the story and focus on its most valuable parts.
- B. Increase the length of the iteration to ensure that all requirements are met.
- C. Trade the story for a different one from the product backlog.
- D. Review the content of the story with the product owner at the next retrospective.

27. 产品负责人正在努力为一个复杂功能编写用户故事，若要处理这个问题，敏捷管理专业人士应该怎么做？

- A. 与产品负责人合作，分解故事并专注于其最有价值的部分。
- B. 增加迭代的时间长度，确保满足所有需求。
- C. 将该故事与产品代办列表中的不同故事交换。
- D. 在下次回顾会议上，与产品负责人一起评审故事内容。

28. A seven-member agile team's composition varies considerably in age, gender, culture, personality type, and professional background. When planning a team-building event, what type of interpersonal skills should the team lead use?

- A. Networking
- B. Emotional intelligence
- C. Communication
- D. Leadership

28. 有七名成员组成的敏捷团队在年龄、性别、文化、个性类型和职业背景方面差异很大，在规划一次团队建设活动时，团队领导应使用什么类型的人际关系技巧？

- A. 社交
- B. 情商
- C. 沟通
- D. 领导力

29. An agile team is working on a complex problem that requires knowledge about an unfamiliar technology. During a daily stand up, a tester volunteers to learn this technology to develop a solution to this complex problem.

What should the agile team leader do?

- A. Appreciate that the team is self-organizing and encourage other developers to help the tester as needed.
- B. Coach the tester to focus on quality improvement activities while team developers learn the unfamiliar technology.
- C. Since the tester will be working on a solution, ensure that the team provides relatively higher estimates by adding a buffer time.
- D. Allow the tester to develop a solution, note it in the risk register, and monitor the risk throughout its life cycle.

29. 敏捷团队正在为一个复杂问题工作，需要一项不熟悉的技术的相关知识，在每日站会上，一名测试人员志愿学习这项技术，以制定出解决这个复杂问题的解决方案。敏捷团队领导应该怎么做？

- A. 赞赏团队的自我组织能力，并鼓励其他开发人员根据需要帮助该测试人员。
- B. 领导该测试人员专注于质量改进活动，而让团队开发人员学习不熟悉的技术。
- C. 由于该测试人员将努力寻找解决方案，因此通过增加缓冲时间来确保团队提供相对较高的估算。
- D. 允许该测试人员制定解决方案，在风险登记册中记录，并在整个生命周期内监控该风险。

30. Two agile team members have differing opinions about a user story. Since neither member is willing to change their position, what should the agile coach do?

- A. Encourage to independently resolve their differences, but provide them with guidance if needed.
- B. Intervene and escalate the issue if it remains unresolved.
- C. Discuss the differences in a team meeting.
- D. Ask a trusted team member to help resolve the issue.

30. 两名敏捷团队成员对用户故事有不同的看法。由于两名成员都不愿改变自己的立场。敏捷教练应该怎么做？

- A. 鼓励他们独立解决分歧，但如有需要，可向他们提供指导。

-
- B. 干预，如果问题仍未得到解决，将该问题升级上报。
 - C. 在团队会议上讨论该分歧。
 - D. 请一名值得依赖的团队成員来帮助解决该问题。

31. A product team has three weeks to create a functioning prototype for a client demonstration. The team has already developed a large number of stories.

What should the team do next?

- A. Identify the minimum releasable features needed and prioritize them for delivery.
- B. Create a high-level schedule and submit a more realistic time frame for customer review.
- C. Estimate story sizes and deliver those that are able to be delivered in the available timeframe.
- D. Increase team size to maximize the chances of on-time delivery.

31. 产品团队有三周时间为客户演示创建一个功能原型，团队已经开发了大量故事。团队下一步应该怎么做？

- A. 识别所需的最低可发布功能，并为其排列优先顺序。
- B. 创建高层级进度计划，并提交更为实际的时间表供客户评审。
- C. 估算故事规模，并交付能够在可用时间范围内可交付的内容。
- D. 增加团队规模，最大限度地提高按时交付的概率。

32. During a daily stand up, a team member reports that the provided technical solution for a performance fix fails to work as expected. The technical architect then begins a discussion of the implemented solution. What should the agile practitioner do?

- A. Ask the product owner to remove this story from the sprint.
- B. Ask the architect to take the discussion offline and identify a solution.
- C. Continue the discussion with the architect until another solution is identified.
- D. Ask the customer to revisit the performance threshold.

32. 在每日站会上，一名团队成员报告说，为性能修复提供的技术解决方案无法按期工作，技术架构师随后开始讨论实施的解决方案。

敏捷管理专业人士应该怎么做？

- A. 要求产品负责人将该故事从 sprint 中删除。
- B. 要求架构师离线讨论，并找出解决方案。
- C. 继续与架构师讨论，直到找到另一个解决方案。
- D. 要求客户重新审视性能临界值。

33. An agile project in a large organization has multiple stakeholders with various needs. How should the team ensure that all stakeholders' needs are met?

- A. Determine which stakeholders are most influential and deliver based on their needs.
- B. Ensure that stakeholders are engaged and attend the review meetings.
- C. Begin with the delivery of features that stakeholders will like the most.
- D. Ask the product owner to prioritize the product backlog according to stakeholders' needs.

33. 一个大型组织的敏捷项目拥有多名干系人，每名干系人都有不同需求，团队应如何确保所有干系人的需求都得到满足？

- A. 确定哪些干系人最有影响力，并根据他们的需求交付项目。

-
- B. 确保干系人参与并参加评审会议。
 - C. 从交付干系人最喜欢的功能开始。
 - D. 要求产品负责人根据干系人的需求对产品待办列表进行优先级排序。

34. A project is nearing completion when the team identifies product quality issues. What should the team have done to avoid this?

- A. Engaged stakeholders in frequent product quality reviews
- B. Defined criteria for quality assurance (QA) during retrospectives.
- C. Increased the number of quality testers during the previous iteration.
- D. Documented all product quality issues in the risk register.

34. 团队识别到产品质量问题时项目已接近完成。若要避免这种情况，团队应该事先做什么？

- A. 让干系人参与频繁的产品质量评审。
- B. 在回顾会议上定义质量保证（QA）标准。
- C. 在上一次迭代中增加质量测试人员的数量。
- D. 在风险登记册中记录所有产品质量问题。

35. A scrum master, who has been working on a product for a number of years, is considered an expert. The product owner has been unable to prioritize the product backlog because of competing stakeholder demands. This impacts the team's ability to proceed. What should the scrum master do?

- A. Reprioritize the backlog and ensure that all decisions are promptly communicated to the product owner.
- B. Note this as an impediment, but continue working on other technical tasks.
- C. Note this as an impediment and work with the product owner to prioritize a subset of competing demands.
- D. Seek the opinions of all team members to collectively reprioritize the product backlog.

35. 已经为一个产品工作多年的 scrum 主管被认为是一名专家。由于竞争干系人的需求，产品负责人无法确定产品待办列表的优先顺序。这会影响团队继续执行的能力。

scrum 主管应该怎么做？

- A. 重新确定待办列表的优先顺序，并确保将所有决策及时传达给产品负责人。
- B. 将其记录为一项障碍，但继续从事其他技术任务。
- C. 将其记录为一项障碍，并与产品负责人合作，确定竞争需求子集的优先顺序。
- D. 征求所有团队成员的意见，共同重新确定产品待办列表的优先顺序。

36. A team of six agile generalists was on track to complete a project in four iterations. Due to changing priorities, management decided to reassign one team member to a different project. Prior to this change, the team's average velocity was 60 points per iteration. How will this change affect the project?

- A. Team morale and project velocity will be impacted.
- B. The team will have to self-organize to maintain the velocity and schedule.
- C. The team may require one or more iterations to regroup before project completion.
- D. The team will want to stop the project.

36. 有六名敏捷通才组成的团队正按进度在四次迭代中完成一个项目。由于优先级的变化。管理层决定将一名团队成员重新分配到另一个项目。在这个变化之前，团队每次迭代的平均速度是 60 点。这个变化将对项目造成什么影响？

- A. 团队士气和项目速度受到影响。
- B. 团队将必须自行组织，以保持速度和进度计划。
- C. 项目完成之前，团队可能需要一次或多次迭代来重组。
- D. 团队将希望停止该项目。

37. A team's morale is low because an issue that caused a delay in a previous release has resurfaced during the current release. The team already identified a corrective action during a retrospective.

What should the team do now?

- A. Create an action plan for issues identified during the retrospective.
- B. Wait until the next retrospective to conduct an in-depth discussion of the issue.
- C. Gain visibility by escalating this issue to the executive team.
- D. Develop a lessons learned list for discussion during the next retrospective.

37. 由于在之前发布中导致延迟的问题在当前发布中重新出现，造成团队士气低落，在回顾会议上，团队已经确定了纠正措施。团队现在应该怎么做？

- A. 为在回顾会议中识别的问题创建一份行动计划。
- B. 等到下一次回顾会议，对这个问题展开深入讨论。
- C. 通过将问题升级上报给高层团队来获得可见性。
- D. 制定一份经验教训列表，在下一次回顾会议讨论。

38. A development team is working on a distributed project across continents. What is a common problem associated with this?

- A. Developers in different locations make incompatible decisions.
- B. Developers working remotely misunderstand the business or domain.
- C. Developers in similar locations will typically agree with the customer.
- D. Developers from antagonistic "us versus them" relationships among individuals in different locations.

38. 一个开发团队正在为一个跨洲的分布式项目工作。与此相关的常见问题是什么？

- A. 不同地点的开发人员做出不相容的决定。
- B. 远程工作的开发人员误解业务或领域。
- C. 在类似地点的开发人员通常会与客户一致。
- D. 在不同地点的开发人员之间形成对抗性的“我们与他们”的关系。

39. During a daily stand up, a team member complains that another team member continually procrastinates reviewing work. What should the agile coach do?

- A. Ask another team member to review the work.
- B. Escalate the issue to the team members' functional managers.
- C. Meet individually with each team member.
- D. Encourage the team members to personally resolve the issue.

39. 在每日站会上，一名团队成员抱怨说，另一名团队队员不断拖延审查工作。敏捷教练应该怎么做？

- A. 让另一名团队成员审查工作。

-
- B. 将该问题上报给该团队成员的职能经理。
 - C. 与每名团队成员单独会面。
 - D. 鼓励该团队成员亲自解决这个问题。

40. An agile team must deliver a very sophisticated and critical software system. The team is geographically distributed and communication flows primarily through emails and the occasional telephone call. To improve team productivity and remove communication barriers, what should the agile practitioner do?

- A. Ask each team member to travel for an on-site assignment for at least for one iteration.
- B. Co-locate team members based on customer proximity.
- C. Encourage personal bonding among dispersed team members and use video conferencing and virtual boards.
- D. Ask the scrum master to act as an interface among the dispersed team members.

40. 敏捷团队必须支付非常复杂和关键的软件系统。团队分布在不同地理位置，主要通过电子邮件和偶尔的电话进行沟通。为提高团队生产力和消除沟通障碍，敏捷管理专业人士应该？

- A. 要求每名团队成员到达现场执行现场任务，至少进行一次迭代。
- B. 根据客户的距离，让团队成员集中办公。
- C. 鼓励分散的团队成员之间的个人联系，并使用视频会议和虚拟看板。
- D. 请 scrum 主管充当分散团队成员之间的接口。

41. An agile coach notices that team velocity is affected because a product owner writes priority defined requirements. What should the agile coach do?

- A. Work with the product owner and the team to clearly define user stories.
- B. Request that the product owner take training to clearly define user stories.
- C. Guide the team to take responsibility and obtain all clarification.
- D. Empower the team by asking a team member to provide clarification.

41. 敏捷教练注意到，因为产品负责人编写的需求定义不明确，团队速度受到影响，敏捷教练应该怎么做？

- A. 与产品负责人和团队合作，明确定义用户故事。
- B. 要求产品负责人参加培训，明确定义用户故事。
- C. 指导团队承担责任并获得所有澄清。
- D. 通过要求团队成员提供澄清来授权团队。

42. An agile team identifies a new risk that will impact a project's next two iterations. What should the team do?

- A. Ask the product owner to resolve the risk.
- B. Discuss risk resolution in the backlog grooming and planning sessions.
- C. Log it in the risk register as low priority.
- D. Log it in the risk register, then resolve it in the next iteration.

42. 敏捷团队识别到一个新风险，将影响一个项目的下两次迭代。团队应该怎么做？

- A. 要求产品负责人解决该风险。
- B. 在待办列表梳理和规划会议中讨论风险解决方案。
- C. 在风险登记册中将其作为低优先级风险记录。
- D. 记录在风险登记册中。然而在下次迭代中解决该风险。

43. A project is behind schedule based on actual versus planned velocity. Where should an agile practitioner look to remove the waste?

- A. Product roadmap
- B. Burn down chart
- C. Burn up chart
- D. Value stream map

43. 根据实际速度与计划速度的对比，项目落后于计划。敏捷管理专业人事应在哪里查看消除浪费的时间？

- A. 产品路线图
- B. 燃尽图
- C. 燃起图
- D. 价值流程图

44. During a team review meeting, the project sponsor complains about several implemented features that do not fit requirements. The sponsor wants these features to be modified immediately. What should the agile coach do?

- A. Ask the product owner to create new stories and prioritize them to be accomplished in the next sprint.
- B. Plan and start the next sprint with newly identified priorities.
- C. Explain to the sponsor the importance of following the product owner's direction.
- D. Work with the sponsor and product owner to determine why the sponsor's requests were not acted upon.

44. 在团队审查会议期间，项目发起人抱怨几个已实施的功能与需求不符。项目发起人希望立即修改这些功能。敏捷教练应该怎么做？

- A. 要求产品负责人创建新的故事，并将其优先考虑在下一个 sprint 中完成。
- B. 用新识别的优先级，计划并开始下一个 sprint。
- C. 向项目发起人说明遵循产品负责人方向的重要性。
- D. 与项目发起人和产品负责人一起确定未执行发起人请求的原因。

45. To foster self-organizing in an agile team, what should a servant leader do during a team meeting.?

- A. Ask questions using the Delphi technique.
- B. Display a burn down chart so that progress can be measured.
- C. Be a silent observer but log observations in the retrospective.
- D. Ask intelligent questions and establish a nurturing environment.

45. 为了培养敏捷团队的自我组织能力，仆人式领导在团队会议中应该做什么？

- A. 使用德尔菲技术询问问题。
- B. 显示一个燃尽图，以便可以测量进展情况。
- C. 作一个沉默的观察者，但在回顾会议中记录观察。
- D. 提聪明的问题，建立一个培养环境。

46. An agile team member expresses an interest in developing financial skills. However, the team's setup requires more technical knowledge than financial skills. What should the agile team lead do?

-
- A. Suggest that the team member instead receive technical training.
 - B. Request financial-skills training for all team members.
 - C. Convince the team member that more experience is required.
 - D. Support the team member's request for financial-skills training.

46. 一名敏捷团队成员表达了对培养财务技能的兴趣。然而，相较于财务技能，建立团队需要更多的技术知识。敏捷团队主管应该怎么做？

- A. 建议该团队成员接受技术培训。
- B. 要求所有团队成员接受财务技能培训。
- C. 说明该团队成员需要更多的经验。
- D. 支持该团队成员的财务技能培训请求。

47. An agile team, experienced in working together, delivers the required user stories in each iteration. Team members are highly specialized individuals with extensive knowledge in their fields, and believe it is unnecessary to share their knowledge when a project is going well. What should the agile team lead do?

- A. Help maintain a positive morale by supporting the team's decision.
- B. Explain to the team that sharing knowledge is important and will help to develop a team of generalized specialists.
- C. Ensure successful knowledge transfer by requiring the team to coach junior agile practitioners.
- D. Ask the team to look for new domains in which to gain expertise, independent of the project's needs.

47. 一个共同合作经验丰富的敏捷团队在每次迭代中交付所需的用户故事。团队成员都是在各自领域拥有广泛知识的高度专业人士，认为在项目进展顺利时，不必分享他们的知识。敏捷团队主管应该怎么做？

- A. 通过支持团队的决定，保持积极的士气。
- B. 向团队解决分享知识很重要，有助于建立一支通才专家团队。
- C. 通过要求团队指导初级敏捷管理专业人士，确保成功转移知识。
- D. 要求团队寻找独立于项目需求的新领域，以获得专业知识。

48. When prioritizing user stories for a new agile project, on what should the product owner focus?

- A. Stories with non-functional requirements
- B. Stories eliminating technical debt
- C. Stories balancing both technical requirements and value to business.
- D. Stories balancing both high business value and most resources needed

48. 在为新敏捷项目确定用户故事优先顺序时，产品负责人应重点关注什么？

- A. 具有非功能性需求的故事。
- B. 消除技术债务的故事。
- C. 平衡技术需求和商业价值的故事。
- D. 平衡高商业价值和需要大部分的资源的故事。

49. A team software developers uses a workflow management tool to progress through the development process. At the last two stand ups, three team members complained that completed that user stories failed to be peer reviewed, which has delayed work.

Although agreement was reached on who would be responsible for completing each peer review, the work remains undone.

How should the agile team lead help the team overcome this issue?

A. During the retrospective, have the team gather data to identify events leading to process bottlenecks, agree on the validity of identified patterns, and analyze the value stream to identify improvements for process flow.

B. Ask the team to discontinue the use of the workflow management tool to manually identify the of the issue.

C. Have the team discontinue work on user stories and begin work on the next-highest-priority items for delivery.

D. During the retrospective, have the team gather data to identify events leading to process bottlenecks, agree on the validity of identified patterns, and reach that use of the workflow management tool should be discontinued because it impedes the process.

49. 一个软件开发团队使用 workflow 管理工具来通过开发过程获得进展，在前两次站会上，一名队员抱怨说，完成的用户故事未能通过同行评审。这已经拖延了工作，虽然对谁将负责完成每次同行评审达成了协议，但这项工作仍未完成。团队领导应如何帮助团队克服这个问题？

A. 在回顾会议期间，让团队收集数据以识别导致流程遇到瓶颈的事件，同意已识别模式的有效性，并分析价值流以识别过程流图的改造。

B. 要求团队停止使用 workflow 管理工具，手动识别问题的根源。

C. 让团队停止在用户故事上的工作，并开始下一个要交付的最高优先级事项工作。

D. 在回顾会议期间，让团队收集数据以识别导致流程遇到瓶颈的时间，同意已识别模式的有效性。并对应停止使用 workflow 管理工具达成一致意见，因为其阻碍了过程进展。

50. During a retrospective, an agile team indicates that the iteration velocity forecast was unmet. While 19 points were planned, only 9 were completed. The team believe that 19 points are reasonable for the next iteration, but the agile practitioner disagrees. The shares that departmental meetings were a factor. What should the agile practitioner do?

A. Tell the team that the next iteration's velocity estimate should be lowered.

B. Ask the team to track non-project hours.

C. Ask the team to work overtime to ensure that estimates are met.

D. Determine roadblocks that prevented the sprint success and mitigate them.

50. 在回顾会议上，一个敏捷团队表示无法满足迭代速度预测，虽然计划了 19 个点，但仅完成 9 个点。团队认为 19 个点对于下一个迭代是合理的，但是敏捷管理专业人士不同意，团队分享说部门会议是一个影响因素。敏捷管理专业人士应该怎么做？

A. 告诉团队应降低下一次迭代的速度估算。

B. 要求团队跟踪非项目时间。

C. 要求团队加班工作，确保满足估算。

D. 确定阻止 sprint 成功的障碍，并减轻这些障碍。

51. A project owner with an overall product vision requests, a detailed project plan. On what should the agile project team spend time planning?

A. Immediate tasks with absolute certainty, end tasks that must be completed for product success.

B. The end-to-end project with a consistent level of certainty.

-
- C. The end-to-end project with an acceptable, low level of certainty.
 - D. Immediate tasks with a higher level of certainty, and upcoming tasks with decreasingly less certainty.

51. 具有整体产品愿景的产品负责人要求提供详细项目计划，敏捷团队应该花时间规划什么？

- A. 具有绝对确定性的立即任务。以及为产品成功而必须完成的结束任务。
- B. 具有一致确定性的结束到结束项目。
- C. 具有可接受、低确定性的结束到结束项目。
- D. 具有较高确定性的立即任务。以及具有较低确定性的即将到来任务。

52. An agile practitioner observes that the team is unable to meet sprint goals, which causes them to commit to fewer features and stories. This ultimately affects the team's morale. What should the agile practitioner do to address the issue and obtain the maximum number of possible ideas?

- A. Use the 5 Whys technique.
- B. Conduct a force field analysis with the scrum master and product owner.
- C. Require team members to participate in an online, anonymous survey.
- D. Brainstorm at the sprint retrospective.

52. 敏捷管理专业人士观察到，团队无法达到 sprint 目标，从而导致他们承诺的功能和故事减少，这最终影响了团队的士气。若要解决这个问题，并获得尽可能多的可能想法，敏捷管理专业人士应该怎么做？

- A. 使用五个为什么技术。
- B. 与 scrum 主管和产品负责人进行力场分析。
- C. 要求团队成员参与一项在线匿名调查。
- D. 在 sprint 回顾会议上进行头脑风暴。

53. A project stakeholder asks if a particular feature will be included in the next release. What should the agile project manager do?

- A. Raise the question with the team, product owner, and stakeholders to assess the feasibility of including the feature.
- B. Inform the stakeholder that the feature will be completed in the next sprint.
- C. Restructure the project team to maximize velocity and increase the probability of delivering the feature.
- D. Let the stakeholder know the feature's priority and state a confidence level based on team velocity.

53. 项目干系人询问某个特定功能是否将包含进下个发布版本中。敏捷项目经理该怎么做？

- A. 向团队、产品负责人和项目干系人提出这个问题，评估包含该功能的可行性。
- B. 通知项目干系人，该功能将在下一次 sprint 中完成。
- C. 重组项目团队结构，尽可能提高速度，并提高交付该功能的概率。
- D. 让干系人指导该功能的优先顺序，并根据团队速度陈述信心等级。

54. An agile team member experiencing personal issues takes frequent leaves of absence. Which hinders project progress. What should the agile team lead do?

- A. Raise this risk at the next team meeting to gather input from other team members.
- B. Ask the functional manager to take action.

-
- C. Personally work with that team member to identify a solution.
- D. Assign work to other team members until that resource returns to work.
54. 一名敏捷团队成员由于遇到个人问题而频繁请假。阻碍了项目进展。敏捷团队领导应该？
- A. 在下次团队会议上提出这个风险，收集其他团队成员的意见。
- B. 要求职能经理采取行动。
- C. 亲自与该团队成员合作，找到解决方案。
- D. 将工作分配给其他团队成员，直到该资源恢复工作为止。
55. Although an agile team lead has been overseeing all delivery processes, velocity has decreased. While user stories and work allocation have been appropriate the team lead identifies that a key developer has spent more time reducing technical debt than on implementing user stories. Burn down charts and information radiators have not reflected this.
- What should the agile team lead do?
- A. Conduct stakeholder interviews to explain the reason for decreased velocity.
- B. Discuss the reasons for decreased velocity and increased technical debt during the next retrospective.
- C. Ask the developer to work on the user stories.
- D. Ensure that there are dedicated user stories to address technical debt.
55. 虽然敏捷团队主管一直在监督所有交付过程，但速度已经下降。虽然用户故事和工作分配是适当的。但团队主管发现，一名关键开发人员花费更多的时间来减少技术债务而不是实施用户故事。燃尽图和信息发射源并未反映出这一点。
- 敏捷团队主管应该怎么做？
- A. 联系干系人解释速度下降的原因。
- B. 在下次回顾会议上讨论速度降低和技术债务增加的原因。
- C. 要求该开发人员从事用户故事方面的工作。
- D. 确保有专门的用户故事来解决技术债务。
56. A product development company is working on a consumer product. A key stakeholder was unavailable to provide feedback during a sprint's execution.
- When should the team gather feedback from this stakeholder?
- A. When the product is deployed into production
- B. During the sprint retrospective
- C. As early as possible
- D. During the next sprint planning meeting
56. 一家产品开发公司正在从事一种消费品的工作。在 sprint 执行期间，一名关键干系人无法提供反馈。团队应在什么时候收集这名干系人的反馈？
- A. 在部署产品投入生产时
- B. 在 sprint 回顾会议上
- C. 尽早
- D. 在下次 sprint 规划会议上
57. What should a team use when communicating progress based on velocity?
- A. The highest velocity in the last few sprints
- B. The lowest velocity in the last few sprints

-
- C. The mean velocity in the last few sprints
 - D. The best velocity the team has achieved to date

57. 根据速度沟通进度时，团队应该使用什么？

- A. 最后几个 sprint 中最高的速度。
- B. 最后几个 sprint 中最低的速度。
- C. 最后几个 sprint 的平价速度。
- D. 团队迄今取得的最佳速度。

58. While helping with a planning session, an agile facilitator learns that the team has agreed on six hours of daily effort. However, the facilitator engages the team to spend more than eight hours daily to work on tasks and other organizational-level meetings. The scrum master is concerned because they want the team to focus on committed effort. What should the scrum master do to address this?

- A. Tell the team to account for both meetings and individual tasks as part of planning.
- B. Apprise the facilitator of the team's agreement and have them limit the team's effort to the same.
- C. Escalate the issue to the project sponsor.
- D. Tell the team to work on individual tasks and decline other meetings.

58. 在帮助规划会议期间，敏捷促进者得知团队同意每天六小时的工作。但是，该促进者让团队每天花费超过八个小时的时间来完成工作任务和参加其他组织层级会议。Scrum 主管非常担心，因为他们希望团队能专注于承诺的工作。若要解决这一问题，scrum 主管该怎么做？

- A. 告诉团队将会议和个人任务纳入规划的一部分。
- B. 将团队的协议通知该促进者，并让促进者将团队的工作限制在协议范围内。
- C. 将该问题升级上报给项目发起人。
- D. 告诉团队做个人的任务，拒绝其他会议。

59. An agile team maintains a risk register. However, for the last two iterations, an identified and detailed business risk has failed to be addressed by the responsible stakeholder. The risk could become a blocker to further progress. What should the agile team do?

- A. Wait for the responsible stakeholder to address the risk.
- B. Stop iteration development and risk register updates until the responsible stakeholder provides a resolution.
- C. Obtain prompt resolution by reminding the responsible stakeholder about the qualitative and quantitative impacts of the risk.
- D. Update the risk register with a resolution due date and stop iteration development until a resolution is provided.

59. 敏捷团队保留一份风险登记册。然而，在最后两次迭代中，负责干系人却未能解决一个已识别的详细业务风险。该风险可能成为进一步向前进展的阻碍。敏捷团队应该怎么做？

- A. 等待负责干系人解决该风险。
- B. 停止迭代开发和风险登记册更新。直到负责干系人提供解决方案为止。
- C. 通过提醒负责干系人风险的定性和定量影响，及时获得解决。
- D. 更新风险登记册，注明解决的截止日期，并在提供解决方案之前，停止迭代开发。

60. An agile team has a pre-developed plan to work on three-week Sprints on a regular cadence. The stakeholders are invited to review progress after every two sprints. How should the product owner ensure that the team is delivering value to the customer?

A. Have the team continue to work according to the pre-developed plan.

B. Ensure that artifacts produced to deliver features remain valuable for the next iteration.

C. Ask the customer to continuously prioritize and validate backlog.

D. Ask the customer to regularly create and validate backlog items.

60. 敏捷团队有一个预先制定的计划，以固定节奏为一个为期三周的 sprint 工作，每两 Sprint 后，邀请干系人审查进展情况。产品负责人应如何确保团队为客户提供价值？

A. 让团队继续按照预先制定的计划工作。

B. 确保为交付功能而生产的工作对下一次迭代仍有价值。

C. 要求客户继续确定优先顺序并确认待办列表。

D. 要求客户定期创建并确认待办列表事项。

61. During the fifth sprint review, the team obtains the product owner's sign-off on all features. However, the product owner notices that two features developed and accepted during the second the sprint no longer work correctly. As new features are developed, the discovery of failures in previously developed features has become frequent. What should be done to control this?

A. The scrum master should reprimand the team.

B. During the next sprint, the team should fix all issues before beginning any new features.

C. An automation test should be included as part of the definition of done so that new features are continuously tested.

D. During the retrospective, the team should identify the developer responsible for causing these failures.

61. 在第五次 sprint 审查期间，团队获得产品负责人对所有功能的签署同意。但是，产品负责人注意到在第二次 sprint 期间开发和验收的两个功能不再正常工作。随着新功能的开发，在之前开发的功能中，故障出现的越来越频繁。若要控制这个问题，事先应该怎么做？

A. scrum 主管应该谴责团队。

B. 在下一次 sprint 期间，团队应该在开始任何新功能之前解决所有问题。

C. 应包含自动化测试。作为已完成定义的一部分，以便能够不断测试新功能。

D. 在回顾会议上。团队应找出为导致这些故障负责的开发人员。

62. Which condition must be met for an item's status to be considered "done"?

A. The team agrees with project sponsor that it is finished.

B. The product owner accepts it as finished.

C. The product owner and the customer approve the user stories.

D. The team and the customer accept the user stories.

62. 一个事项的状态被视为“已完成”，必须满足哪一项条件？

A. 团队与项目发起人达成该事项已完成的一致意见。

B. 产品负责人接受该事项已完成。

C. 产品负责人和客户批准用户故事。

D. 团队和客户批准用户故事。

63. After completing their tasks, an agile practitioner proposes adding a story to the current iteration. There are still committed stories in the sprint are incomplete. What should the agile practitioner do?

- A. Ask the product owner for a new story, outside of the sprint, on which to work.
- B. Complete the stories independently since the team composition was low quality.
- C. Wait until the retrospective to request team approval to work on a new story.
- D. Offer team support and help complete other stories in the sprint.

63. 完成任务后，敏捷管理人士建议在当前迭代中添加一个故事。在 sprint 中仍存在未完成的承诺的故事。敏捷管理专业人士应该怎么做？

- A. 在正在从事的 sprint 之外，要求产品负责人提供一个新故事。
- B. 独立完成故事。因为团队组成质量低。
- C. 等到回顾会议，要求团队批准开展新的故事。
- D. 提供团队支持，帮助完成 sprint 中的其他故事。

64. A customer rejects a product because they believe requirements were missed. What should the project team do to increase the likelihood that future work will be accepted?

- A. Conduct periodic product demos and progress reviews with the customer.
- B. Review the scope to include new customer requirements.
- C. Communicate goals more clearly in cross-team meetings.
- D. Conduct a product demo with the product owner for sign off.

64. 由于客户认为需求遗漏了，客户拒收产品。若要提高未来工作被接受的可能性，项目团队应该怎么做？

- A. 与客户一起定期进行产品演示和进度审查。
- B. 修改范围，包含客户的新需求。
- C. 在跨团队会议中更明确地沟通目标。
- D. 与产品负责人一起进行产品演示以获得签署同意。

65. A product manager asks the project lead to update the product backlog. These updates includes the addition of new requirements and a representative of existing ones. The product manager that a new requirement be implemented as soon as possible.

- A. Allow all changes, including the addition of new requirements and the reprioritization of existing ones.
- B. Reject all new requirements, but allow the reprioritization of existing ones.
- C. Maintain the priorities of existing requirements, but allow new requirements to be added.
- D. Reject all changes until the product owner a release replanning session.

65. 产品经理要求项目主管更新产品待办列表。这些更新包括添加新需求以及对现有需求重新排列优先顺序，产品经理坚持要求尽快实施新需求。项目主管应该怎么做？

- A. 这些更新包括添加新需求以及对现有需求重新排列优先顺序。
- B. 拒绝所有新需求，但允许重新确定现有需求的优先顺序。
- C. 现有需求的优先级，但允许添加新需求。
- D. 拒绝所有变更，直到产品负责人推进一次重新规划发布会议。

66. An agile team is working in two, week-long sprints. During the sprint, what should the team do when developing features?

- A. Demo the product at the end of the iteration to obtain product owner acceptance.
- B. Continually request product owner feedback on the features being worked.
- C. Ask the product owner to answer all stakeholder questions.
- D. Schedule a demo for the product owner once a feature has been unit-end functionally tested.

66. 敏捷团队正在为期两周的 sprint 工作,在 sprint 期间,团队在开发功能时应该怎么做?

- A. 在迭代结束时演示产品,以获得产品负责人的验收。
- B. 不断要求产品负责人对正在从事的功能提供反馈。
- C. 要求产品负责人回答所有项目干系人的问题。
- D. 一旦功能完成单元测试和功能测试,安排一次针对产品负责人的演示。

67. An agile team lead would like to begin a new project with a visioning workshop. Some team members are local, while some work remotely. There are multiple architectural spikes that need to be completed before development starts. What should the agile team lead do to successfully begin the project?

- A. Invite the product owner and all team members to participate in the visioning workshop, and then complete the architectural spikes.
- B. Invite expert team members to participate in the visioning workshop and ask junior members to complete the architectural spikes.
- C. Ask the product owner and local team members to participate in the visioning workshop and have remote team members complete the architectural spikes.
- D. Ask the product owner to create the vision and ask the entire team to complete the architectural spikes.

67. 敏捷团队领导希望通过一次愿景研讨会开始一个新项目。一些团队成员是本地的,另外一些团队成员在远程工作。开始开发之前,需要完成多次架构刺探。

- A. 邀请产品负责人和所有团队成员参加愿景研讨会,然后完成架构刺探。
- B. 邀请专家团队参加愿景研讨会,并要求初级成员完成架构刺探。
- C. 邀请产品负责人和本地团队成员参加愿景研讨会,让远程团队成员完成架构刺探。
- D. 要求产品负责人创建愿景,并要求整个团队完成架构刺探。

68. A stakeholder complains that a team sends excessive emails for approvals. The team lead notices that the team and stakeholder have isolated working spaces and little chance to interact. To resolve this issue, the team lead suggests more frequent, In-Person requirements reviews. What is the team lead recommending?

- A. Osmotic communication
- B. Collaboration
- C. Colocation
- D. Pair programming

68. 一个干系人抱怨团队发送过多的电子邮件进行审批。团队领导注意到团队与该干系人的工作相互隔绝,几乎没有机会互动。为了解决这个问题。团队领导建议进行更频繁的面对面需求评审。团队领导建议的是什么?

- A. 渗透沟通
- B. 协作

-
- C. 集中办公
 - D. 结对编程

69. An agile team is working on a project with both internal and external stakeholders. Midway through the project, a new requirement is identified that will delay delivery by two months. What should the team do?

- A. Deliver the planned items first, then work on the new requirement.
- B. Work with the product owner to reprioritize the backlog.
- C. Add the new requirement to an upcoming release.
- D. Inform the stakeholders and work backward from the new delivery date.

69. 敏捷团队正在从事一个项目。该项目具有内部和外部干系人，在项目中期，识别到一个将延迟交付两个月的新需求。团队应该怎么做？

- A. 首先交付已计划的事项，然后处理新需求。
- B. 与产品负责人一起，更新确定待办列表的优先顺序。
- C. 将新需求添加到即将发布的版本中。
- D. 通知干系人，并从新的交付日期倒排进行工作。

70. An agile team member is very quiet, seldom contributes in meetings, and rarely provides feedback during retrospectives. What should the agile practitioner do to encourage this member to be more vocal?

- A. Solicit the team member's opinion during the retrospectives.
- B. Meet individually with the member to determine their comfort level with providing feedback.
- C. Conduct team-building exercises.
- D. Speak to the team member's functional manager to obtain feedback on communication style.

70. 一名敏捷团队成员很安静，很少在会议上发言，且很少在回顾会议上提出反馈。敏捷管理专业人士应如何鼓励该团队成员更积极参与？

- A. 在回顾会议上征求该团队成员的意见。
- B. 与该团队成员单独开会，以确定其提供反馈的舒适程度。
- C. 开展团队建设活动。
- D. 与该团队成员的职能部经理沟通，获得其对沟通风格的反馈。

71. A team's current iteration is compromised because the product owner added new requirements. What initial action should the agile practitioner take?

- A. Work with the product owner and team to reprioritize the backlog.
- B. Lengthen the time spent for prioritizing and planning iterations.
- C. Meet with the product owner to coach them on agile principles.
- D. Formally request that the product owner be removed from this project.

71. 由于产品负责人添加了新的需求，损害了团队当前的迭代。敏捷管理专业人士应采取什么初步行动？

- A. 与产品负责人和团队合作，重新确定待办列表的优先顺序。
- B. 延长在排列优先顺序和规划迭代方面所花的时间。
- C. 与产品负责人开会，教导他们敏捷原则。
- D. 正式请求将产品负责人从项目中开除。

72. A stakeholder has been unavailable, which causes an agile team to become concerned that requirements will be unmet and the project will be behind schedule. What should the team lead do?

- A. Meet with the stakeholder to update the requirements document and submit change requests.
- B. Review and update the communications management plan.
- C. Ensure that the stakeholder requests and approves all changes.
- D. Set up a Kanban board.

72. 一名干系人不可用，这导致敏捷团队担心需求将得不到满足。且项目将落后于进度计划。团队领导应该怎么做？

- A. 与干系人开会，更新需求文件并提交更改请求。
- B. 审查并更新沟通管理计划。
- C. 确保干系人请求并批准所有变更。
- D. 设置一个 kanban 板。

73. An agile team is preparing to work on an epic story that may require the integration of a new technology. As the next iteration is planned, what should the agile practitioner do?

- A. Engage in exploratory research to better understand the risk of using the new technology.
- B. Add the story to the risk register.
- C. Raise this as an issue in the daily stand up.
- D. Change the story to avoid the integration of new technology.

73. 敏捷团队正在为一个史诗故事的工作做准备，该故事可能要求集成一项新技术。由于下一个迭代已经计划完毕，敏捷管理专业人士应该怎么做？

- A. 参与考察研究，更好地了解使用这项新技术的风险。
- B. 将该故事添加进风险登记册。
- C. 在每日站会上将其作为一个问题提出。
- D. 更改该故事，避免集成新技术。

74. An agile team is working on delivering a high-profile solution for a customer. However, the product owner is experiencing difficulty obtaining information from the customer on requirements for their evolving needs. What should the agile team do?

- A. Conduct a joint design session with the product owner and the customer to obtain all requirements.
- B. Adopt a validated learning approach to frequently review and validate small increments with the customer.
- C. Run a spike iteration to analyze the customer's needs and propose a hypothetical solution.
- D. Suggest that the product owner receive requirement-gathering training.

74. 敏捷团队正在为客户交付一个备受瞩目的解决方案。但是，由于客户的需求不断变化，产品负责人难以从客户那里获得需求相关信息。敏捷团队应该怎么做？

- A. 与产品负责人和客户召开联合设计会议以获得所有需求。

-
- B. 采用经过验证的学习方法，与客户一起经常审查和核实小幅增量。
 - C. 运行一次刺探迭代来分析客户的需求，并提出一个假设解决方案。
 - D. 建设产品负责人接受需求收集培训。

75. A project is proceeding according to its planned velocity, but the scope continues to increase and jeopardizes the project's deadline. The agile team insists that since the velocity is good, there is no problem. What should the agile coach do?

- A. Determine the cause of the scope increase and prohibit any further ones.
- B. Ask the product owner to evaluate the scope increase and determine next actions.
- C. Ensure that the product owner keeps the scope visible to the stakeholders.
- D. Discuss the scope increase at the next retrospective to ensure team understanding of its impact.

75. 一个项目正在按计划的速度进行，但范围继续增加，危及到项目的截至期限。敏捷团队坚持认为，由于速度良好，不会有问题。敏捷团队教练应该怎么做？

- A. 确定范围增加的原因。并禁止范围进一步增加。
- B. 要求产品负责人评估范围增加并确定下一步行动。
- C. 确保产品负责人保持范围对项目干系人可见。
- D. 在下次回顾会议上讨论范围增加，以确保团队了解其影响。

76. A senior team member with the siloed knowledge resigns, providing very little notice. As a result, the team experiences bottlenecks. What should the team lead have done to ensure that development was maintained in this scenario?

- A. Merged similar development teams to enhance information sharing.
- B. Had the senior team member document their daily processes.
- C. Cross-trained the team in supplemental skills.
- D. Hired temporary staff with the required skill set.

76. 一名拥有封闭知识的高级团队成员辞职，提供极少信息。结果，团队经历瓶颈。若要确保在该情景中继续保持开发，团队领导应该事先做什么？

- A. 合作类似的开发团队以加强信息共享。
- B. 让高级团队成员记录他们的日常流程。
- C. 交叉培训团队的补充技能。
- D. 聘请具有所需技能的临时工作人员。

77. Based on the chart, if a team's velocity is 11, how many iterations will be needed to complete all stories?

- A. 3
- B. 4
- C. 5
- D. 7

77. 根据图表，如果团队的速度为 11，需要多少次迭代来完成所有故事？

故事	故事点
A	4
B	5
C	6
D	5

E	4
F	6
G	1

- A. 3
- B. 4
- C. 5
- D. 7

78. An agile team is working on a large project with a short deadline. Two team members ask to less a new technology that could enhance team efficiency during the project. The product owner is apposed to this because if could delay project progress. What should the agile coach do?

- A. Allow the two team members to experiment withe the new technology and run a technical spit.
- B. Ask the product owner to prioritize the work, then decide if the new technology should be pursued.
- C. Have the team determine if the new technology will provide value, then establish a suitable timebox for testing.
- D. Present the new technology to the relevant functional manager to ensure that all company standards work appropriately.

78. 敏捷团队正在从事一个期限很短的大型项目工作。两名团队成员要求学习一种可以提高项目期间且效率的新技术。由于这可能延迟项目进度。产品负责人反对。敏捷教练该怎么做？

- A. 允许这两名团队成员尝试新技术，并运动技术刺探。
- B. 请产品负责人确定工作的优先顺序，然后决定是否应该追求新技术。
- C. 让团队确定新技术是否提供价值，然后建立适当的测试时间盒。
- D. 向相关职能经理介绍新技术，确保所有公司标准正常动作。

79. How can a product owner quickly determine the status of a team' s commitments for a current sprint?

- A. Review the percent complete for upcoming tasks and deliverables.
- B. View a demo of upcoming deliverables.
- C. Review the burn down and burn up charts.
- D. Attend the daily stand ups.

79. 产品负责人如何快速确定当前 sprint 的团队承诺状态？

- A. 查看即将到来任务和可交付成果的完成百分比。
- B. 查看即将交付的可交付成果演示。
- C. 查看燃尽图和燃烧图。
- D. 参加每日站会。

80. Team A has a critical dependency on team B. Team A learn s that the deliverable to meet that dependency will be delayed by team B, which will negatively impact the delivery.

What should be done to resolve this dependency?

- A. Foster closer collaboration between the teams.
- B. Ask the project sponsor to facilitate and resolve the issue.

-
- C. Escalate it to the agile project manager.
- D. Emphasize areas of agreement among the teams and ignore areas of disagreement.
80. 团队 A 对团队 B 存在关键依赖关系。团队 A 得知，团队 B 将延迟满足该依赖关系交付成果，这将对交付产生负面影响。若要解决这个依赖关系，事先应该怎么做？
- A. 促进团队之间的密切合作。
- B. 请项目发起人推进并解决该问题。
- C. 将该问题上报给敏捷项目经理。
- D. 强调团队之间具有一致意见的领域，忽视具有不同意见的领域。
81. A Web developer is struggling to satisfy a product owner's requirements. How can a daily stand up help the developer?
- A. The agile practitioner can provide direction to the web developer.
- B. The web developer can discuss possible solutions with the team.
- C. The web developer can raise the issue with the team to create visibility.
- D. The meeting can be used to discuss whether the requirement is a priority.
81. 网络开发人员正在竭力满足产品负责人的要求。每日站会将如何帮助开发人员？
- A. 敏捷管理专业人士可以为网络开发人员提供指导。
- B. 网络开发人员可以与团队讨论可能的解决方案。
- C. 网络开发人员可以向团队提出问题，以创建可视化。
- D. 会议可用于讨论该需求是否属于优先事项。
82. Team members on an agile project face several issues that need to be communicated to, and resolved with, stakeholders. What should the team do to most effectively communicate and resolve the issues?
- A. Phone the stakeholders
- B. Email the stakeholders.
- C. Meet face-to-face with the stakeholders.
- D. Hold a video conference with the stakeholders.
82. 一个敏捷项目的团队成员遇到需要与干系人沟通并一起解决的若干问题。若要最有效地沟通并解决这些问题，团队应该怎么做？
- A. 致电给干系人。
- B. 给干系人发送电子邮件。
- C. 与干系人面对面会面。
- D. 与干系人召开视频会议。
83. An agile team has been incrementally delivering features for the past year. However, team velocity for the last four iterations has decreased. During the latest team retrospective team members raised concerns that the product owner is impacting their productivity by frequently reaching out to them individually. What should the agile team lead do?
- A. Increase the frequency of backlog grooming and iteration planning sessions with the product owner.
- B. Ask the product owner to address the whole team to avoid redundancies.
- C. Meet and product owner to determine the root cause.

D. Hold a meeting and tell the team to obtain permission before responding to the product owner.

83. 一年中一直在逐步交付功能，然而，最近四次迭代的团队速度已经下降。在最近成员担心产品负责人会通过频繁地与他们单独接触来影响他们的生产力。敏捷团队领导该怎么做？

- A. 负责人进行待办列表梳理和迭代计划会议的频率。
- B. 面向整个团队来陈述问题，以避免重复。
- C. 负责人开会，确定根本原因。
- D. 开会，并告知团队在回应产品负责人之前先获得许可。

84. During a planning meeting, an agile practitioner asks a stakeholder to clarify requirements. The agile practitioner notices differing opinions between the team and the stakeholder. What should the agile practitioner do?

- A. Work with the stakeholder and the team to gain alignment.
- B. Remind the team of previously established agreements.
- C. Ask the project sponsor to remind the stakeholder about their role in the planning meeting.
- D. Take control of the meeting by asking team members to provide their opinions and make decisions.

84. 在规划会议上，敏捷管理专业人士要求一名干系人澄清需求。敏捷管理专业人士注意到团队和该干系人之间的意见不一致。敏捷管理专业人士应该怎么做？

- A. 与该干系人和团队一起合作，取得一致。
- B. 提醒团队之前订立的协议。
- C. 请项目发起人提醒项目干系人他们在规划会议中的角色。
- D. 通过要求团队成员提出各自的意见和做出决策，控制会议。

85. A team member located outside of the country recommends a new, web-based conferencing application that will improve communication at no extra cost. The local team objects to the application and prefers to meet face-to-face. What should the agile practitioner do?

- A. Encourage the team to experiment with the new application and then re-evaluate it.
- B. Explain that the new application is not approved by all team members and discuss alternative solutions.
- C. Determine what application is best for the team.
- D. Ask the product owner to decide what application is best for the team.

85. 一名位于国外的团队成员推荐一种新的、基于网络的会议应用程序，将在不生产额外成本的情况下改善通信。但本地团队反对应用程序，并倾向于面对面会议。敏捷管理专业人士应该怎么做？

- A. 鼓励团队尝试新的应用程序，然后重新评估该应用程序。
- B. 解释新的应用程序未被所有团队成员批准并讨论替代解决方案。
- C. 确定什么应用程序最适合团队。
- D. 要求产品负责人决定哪个应用程序最合适团队。

86. An agile project team requires a new, custom tool for integration as a project component. The team hires a contractor to create the tool. How should the project team plan and monitor the contractor's work?

-
- A. By ensuring the contractor submits a project plan and status reports
 - B. By using a sprint backlog and retrospective meetings
 - C. By using the product backlog and daily stand up meetings
 - D. By ensuring daily task plans are created and status updates are communicated clearly
86. 敏捷项目团队需要一个新项目组件的集成工具。项目团队应如何计划和监督分包商工作？
- A. 通过确保分包商提交项目计划和状态报告。
 - B. 通过使用 sprint 待办事项和回顾会议。
 - C. 通过使用产品待办事项和每日站会。
 - D. 通过确保创建每日任务计划并明确沟通状态更新。
87. An agile team needs to identify the possible causes of an issue they are experiencing in a current project. What should the agile team do?
- A. Develop a spike.
 - B. Create an ishikawa diagram.
 - C. Perform a prior analysis.
 - D. Complete a variance and trend analysis.
87. 敏捷团队需要识别当前项目中遇到问题的可能原因。敏捷团队应该怎么做？
- A. 开发一个探测。
 - B. 创建石川图。
 - C. 执行事前分析。
 - D. 完成偏差和趋势分析。
88. During which meeting should an agile practitioner work with the team to share information about tasks, and commitments?
- A. Stakeholder priority
 - B. Project status
 - C. Sprint retrospective
 - D. Stand up
88. 在哪次会议期间，敏捷管理专业人士应与团队合作，分享任务、故事和承诺相关的信息？
- A. 干系人优先级会议
 - B. 项目状态会议
 - C. Sprint 回顾会议
 - D. 站会
89. A product owner states that a pending release' s identified goals are unmet. What should the agile practitioner do to ensure that future releases meet the goals?
- A. Have the product owner prioritize the product backlog before the next sprint planning session.
 - B. Inform the product owner of the sprint' s cost.
 - C. Ensure that the product owner works with stakeholders to envision the product.
 - D. Obtain an approved ROI from the product owner.
89. 产品负责人指出，一个未决发布的已识别目标无法得到满足，若要确保未来发布满足目标，敏捷管理专业人士应该怎么做？
- A. 在下次 sprint 计划会议之前，让产品负责人对产品待办列表排列优先顺序。
 - B. 通知产品负责人 sprint 的成本。

-
- C. 确保产品负责人与干系人一起设想产品。
 - D. 从产品负责人获得批准的 ROI。

90. While working on a user story in a sprint, a team member comes up with an idea for adjusting an organizational process in order to maximize value delivery. What is the best time to propose this idea to the team?

- A. During the next sprint planning session.
- B. During the next daily scrum.
- C. During the project status meeting.
- D. During the sprint retrospective.

90. 在处理一个 sprint 的用户故事时，团队成员提出了调整组织过程实现价值交付最大化的想法。向团队提出这个想法的最佳时机是什么？

- A. 在下一次 sprint 规划会议上。
- B. 在下一次每日 scrum 期间。
- C. 在项目状态会上。
- D. 在 sprint 回顾会议上。

91. After the first sprint, an agile practitioner notices that some team members are unclear about an agile environment's highest priority. On what should the agile practitioner advise those team members to focus?


- A. Delivering valuable solutions
- B. Balancing flexibility and stability
- C. Managing chaos
- D. Detailing business requirements

91. 在第一次 sprint 之后，敏捷管理专业人士注意到一些团队成员尚不清楚敏捷环境的最高优先级。敏捷管理专业人士应建议这些团队成员关注哪一点？

- A. 交付有价值的解决方案。
- B. 平衡灵活性和稳定性。
- C. 管理混乱。
- D. 详细的业务需求。

92. At the end of a sprint, the scrum master sees that some story points remain. Based on the burn down chart, and according to agile principles, what should the scrum master do?

- A. Extend the sprint by two days to allow completion of the stories.
- B. Place the incomplete stories back in the product backlog for reprioritization by the product owner.
- C. Authorize overtime to complete the stories.
- D. Place the incomplete stories in the sprint backlog for the following sprint so that they receive top priority.

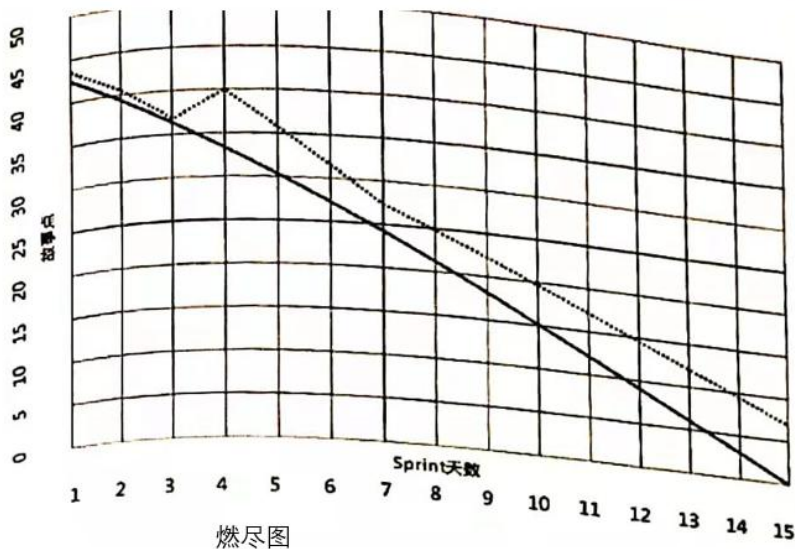

92. 在一个 sprint 结束时，scrum 主管看到还存在一些故事点，根据燃尽图，并按照敏捷原则，scrum 主管应该怎么做？

- A. 将 sprint 延长两天完成这些故事。
- B. 将不完整的故事放回产品待办列表中，以便产品负责人重新排列优先顺序。
- C. 批准加班完成这些故事。
- D. 将不完整的故事放在下一个 sprint 的 sprint 待办列表中，以便获得最高优先级。

93. A project team petitions the team lead to extend an iteration by one day so they can complete a feature by the next sprint review. What should the team lead do?

- A. Maintain the current and future iteration lengths.
- B. Extend all iterations by one day.
- C. Extend the current iteration by one day.
- D. Extend the current iteration by one day, and shorten the next iteration by one day.

93. 项目团队请团队领导将一个迭代延长一天时间，让他们可以在下一次 sprint 评审会前完成一个功能，团队领导应该怎么做？

- A. 保持当前和未来的迭代时间长度。
- B. 将所有迭代延长一天。
- C. 将当前迭代延长一天。
- D. 将当前迭代延长一天，并将下一个迭代缩短一天。

94. A team needs to evaluate stories for a critical-to-satisfy end user. What method should the team amplify?

- A. Impact mapping
- B. Story mapping
- C. Personas
- D. Assign priority to stories

94. 在团队需要评估一个最终用户的用户故事，其满意度至关重要。团队应该使用什么方法？

- A. 影像图
- B. 故事图
- C. 人物
- D. 为故事分配优先级

95. An experienced agile team is working on a new project. The project manager expects that the team will make few mistakes and finish ahead of schedule. The team feels that the project manager's expectations are too high, since every project is different. What should the agile team do?

- A. Advise the project manager that the team may make mistakes in the beginning, but improve with each iteration.
- B. Inform senior management of the project manager's expectations at the daily stand up.
- C. Ask the product owner to speak to the project manager about agile principles.
- D. Ask the sponsor to assign another project manager who is familiar with agile.

95. 一个经验丰富的敏捷团队正在开展一个新项目。项目经理期望团队几乎不犯错误，比进度计划提前完成项目。团队认为项目经理的期望太高，因为每个项目都不一样。敏捷团队应该怎么做？

- A. 告诉项目经理团队在开始时可能会犯错。但每次迭代都会有所改善。
- B. 在每日站会上向高级管理层通报项目经理的期望。
- C. 请产品负责人向项目经理讲述敏捷原则。
- D. 请项目发起人任命一名熟悉敏捷管理的项目经理。

96. Regulatory requirements mandate that a project's implemented functionality be documented. What should the team do to comply with this requirement?

- A. Ask the product owner to create a story about the documentation.
- B. Wait for a hardening iteration.
- C. Collect the documentation in the iteration that follows the development iteration.
- D. Add this requirement to the definition of done.

96. 监管要求将某个项目已实施的功能记录在文件中。若要满足这个要求，团队该怎么做？

- A. 请产品负责人创建关于该文件的故事。
- B. 等待迭代固化。
- C. 在开发迭代之后的迭代中收集文件。
- D. 将此要求添加到已完成的定义中。

97. What should an agile practitioner do if a team's velocity decreases due to lack of engagement?

- A. Investigate the cause and address the issue in the next retrospective.
- B. Inform the product owner.
- C. Talk to the team and facilitate a stand up to address the issue.
- D. Decrease the number of stories

97. 如果由于缺乏参与，团队的速度下降，敏捷管理专业人士应该怎么做？

- A. 调查原因，并在下一次回顾会议上陈述该问题。
- B. 通知产品负责人。
- C. 与团队讨论，并促成一次站会，陈述该问题。
- D. 减少故事数量。

98. What should a development team do when they identify significant technical debt during a sprint?

-
- A. Dedicate the next iteration entirely to technical debt cleanup.
 - B. Ask the customer to include incremental technical debt cleanup in future iterations.
 - C. Discuss the technical debt in the next retrospective meeting.
 - D. Capture the technical debt in the product backlog.
98. 开发团队在一个 sprint 期间识别到重大技术债务时应该怎么做?
- A. 在下一个迭代专注与技术债务清理。
 - B. 要求客户在未来的迭代中包含增量技术债务清理。
 - C. 在下次回顾会议中讨论技术债务。
 - D. 在产品待办事项中收集技术债务。
99. What should an agile practitioner do if the team questions the value of contributing during daily Stand-ups?
- A. Describe how stand ups increase the likelihood of detecting obstacles.
 - B. Demonstrate how stand ups justify management goals.
 - C. Explain how stand ups remove the need for multiple burn down charts.
 - D. Show how stand ups eliminate the need for detailed status reports for the sponsor.
99. 如果团队质疑每日站会的意义。敏捷管理专业人士应该怎么做?
- A. 说明每日站会如何提高检测障碍的可能性。
 - B. 演示每日站会如何证明管理目标的合理性。
 - C. 说明每日站会如何去除多个燃尽图的需求。
 - D. 展示每日站会如何消除发起人对详细状态报告的需要。
100. Trend analysis shows that velocity is significantly lower than predicted and the release will be completed a month behind schedule. The team recommends changing the end date to reflect this. What should the agile practitioner do?
- A. Announce that the team has not exceeded the predicted velocity, but that the end date will remain the same.
 - B. Ask the scrum master to reduce additional features in the product backlog. Then re-plan subsequent iterations.
 - C. Meet with the business owner to determine whether to reduce scope or add time.
 - D. Ask the team to increase velocity to meet contractual obligations, and document this decision.
100. 趋势分析显示，速度显著低于预期，版本完成日期降落后与进度计划一个月。团队建议更改结束日期以反映这一点。敏捷管理专业人士应该怎么做?
- A. 宣布团队没有超过预测速度，但结束日期将保持不变。
 - B. 要求 scrum 主管减少产品待办事项中的额外特性，然后重新计划后续迭代。
 - C. 与业务负责人联系以确定是减少范围还是增加时间。
 - D. 要求团队提高速度以满足合同中的义务，并记录此决定。
101. A company's chief technology officer (CTO) asks the agile team lead to map out the portfolio of projects to facilitate decision-making for project prioritization and selection. What should the team lead use to help the CTO?
- A. Bottom-up estimating
 - B. Affinity estimating
 - C. Delphi technique

D. Backlog grooming

101. 一家公司的首席技术官（CTO）需要敏捷团队主管筹划项目组合，以促进项目优化和选择的决策。为了帮助首席技术官。团队主管应该使用什么？

- A. 自下而上估算
- B. 亲和估算
- C. 德尔菲技术
- D. 待办列表梳理

102. An organization that currently uses traditional methods wants to transition to agile. An initial assessment reveals that the organization's culture is unready to adopt agile practices. The agile practitioner spends the next three months influencing, Educating, and training people in the organization. What should the agile practitioner do next?

- A. Perform another assessment, and analyze the results.
- B. Opt to maintain the existing methodologies.
- C. Implement stand ups, reviews, and retrospectives on non-agile projects.
- D. Force pilot projects to use agile methodologies.

102. 一家组织目前使用传统方法，希望转型到敏捷方法。一项初步评估显示，该组织的文化还未做好采用敏捷实践的准备。敏捷管理专业人士在接下来的三个月里影响、教育和培训组织中的人员。敏捷管理专业人士下一步应该怎么做？

- A. 执行另一项评估并分析结果。
- B. 选择保持现有方法。
- C. 在非敏捷项目实施站会，评审会议和回顾会议。
- D. 强制执行试点项目，使用敏捷方法。

103. A traditional project manager assumes an agile project in an organization trying to adapt agile practices. What should the project manager do to achieve success?

- A. Assist team members with their assigned work.
- B. Help tackle issues facing the customer.
- C. Ensure that all team members have the appropriate resources.
- D. Evenly delegate work assignments to maintain team balance.

103. 一个传统项目经理在一个尝试采用敏捷实践的组织中负责管理一个敏捷项目，若要获得成功，项目经理应该怎么做？

- A. 协助团队成员完成分配给他们的工作。
- B. 帮助解决客户面对的问题。
- C. 确保所有团队成员都有适当的资源。
- D. 平均分配工作任务来维持团队平衡。

104. A customer is frustrated because they do not know when the product will be available for market. What should the agile practitioner do to resolve this?

- A. Collaborate with stakeholders to complete a release plan.
- B. Ask the product owner to complete the user stories and iterations.
- C. Create a product vision statement.
- D. Complete a product strategy document.

104. 客户由于不知道产品什么时候可以上市而感动沮丧。若要解决这个问题，敏捷管理专业人士应该怎么做？

- A. 与干系人一起完成发布计划。
- B. 要求产品负责人完成用户故事和迭代。
- C. 创建一份产品愿景说明书。
- D. 完成一份产品战略文件。

105. An agile team is developing some functionality as part of work scoped into the current iteration. One team member is facing an issue that is impeding progress on a story. What should the agile manager do to help the team move forward?

- A. Use technical skills and experience to identify a solution and direct the team to follow it.
- B. Brainstorm the issue with the team and facilitate the identification of solution.
- C. Assign a team member to resolve the issue by a set deadline at any cost.
- D. Replace the story with a new one.

105. 敏捷团队正在开发一些功能，作为纳入当前迭代范围内工作的一部分。一名团队成员正遇到一个妨碍故事进展的问题。若要帮助团队继续向前发展，敏捷经理应该怎么做？

- A. 使用技术技能和经验来找出解决方案，并指示团队遵循该解决方案。
- B. 与团队一起对该问题进行头脑风暴，促进找到解决方案。
- C. 分配一名团队成员，以任何代价在规定期限之前解决该问题。
- D. 使用一个新故事替换该故事。

106. A project owner states that the added, non-functional work identified as required in the initial planning session is not valuable, and asks to exclude it from the product backlog. What should the agile team do?

- A. Ensure that the added, non-functional work is factored into the acceptance criteria.
- B. Determine the time needed to complete the added, non-functional work and increase the time estimates for individual tasks.
- C. Propose that the added, non-functional work be included and prioritized in the product backlog.
- D. Support the product owner and postpone the added, non-functional work until project completion.

106. 产品负责人指出，根据初始规划会议的要求识别添加的非功能性工作没有价值，并要求将其从产品待办列表中。敏捷团队应该怎么做？

- A. 确保将添加的非功能性工作纳入验收标准。
- B. 确定完成添加的非功能性工作所需要的时间，并增加个别任务的时间估算。
- C. 建议包含添加的非功能性工作，并对产品待办列表排列优先顺序。
- D. 支持产品负责人。并推迟添加的非功能性工作，直到项目完成。

107. An agile team is about to start the fifth iteration cycle. The team is concerned that urgent maintenance tasks for an older artifact has taken excessive time. This has made it difficult to keep other commitments. During the retrospective, the team jointly decides against putting maintenance tasks into the backlog. Instead, they plan to lower capacity and add slack time to the next cycle.

What will happen in the next iteration cycle?

-
- A. The velocity will decrease.
B. The velocity will increase.
C. The velocity will remain stable.
D. The cumulative flow diagram will show a downward dent for that iteration cycle.
107. 敏捷团队即将开始第五个迭代周期。团队担心，一个较旧工件的紧急维护任务花费太多时间。这已经导致其很难遵守其它承诺。在回顾会议上，团队共同决定不将维护任务纳入待办列表，相反的，他们计划降低产量，并增加下个周期的浮动时间。下个迭代会发生什么？
- A. 速度将会降低。
B. 速度将会提高。
C. 速度将会保持稳定。
D. 累积流图将显示该迭代周期将向下凹陷。

108. An agile team identifies a set of tasks as administrative. What should the agile team lead do?
- A. Have a team member handle these tasks.
B. Flag it as an obstacle.
C. Assume the tasks to allow team members to focus on delivery.
D. Escalate the tasks to management.
108. 敏捷团队将一组任务识别为行政任务。敏捷团队主管应该怎么做？
- A. 让一名团队成员处理这些问题。
B. 将其标记为障碍。
C. 承担这些任务，让团队成员专注于交付。
D. 将这些任务升级上报给管理层。

109. A team has discovered a breakthrough product for which early market delivery is critical. The work is broken down to first build a framework, and then to add functionality. The team decides to use three-week sprints until the framework is built, and the switch to two-week sprints for functional additions. What should the team and management do?
- A. Tune sprint cycles to the correct work size.
B. Create sprints of equal duration, break down work even if it fails to meet completion criteria, and grant exceptions since the associated risk is known and contained.
C. Work on the framework and functionality simultaneously so that sprints have the same duration.
D. Revisit the product vision and roadmap, break work down into nearly equal-sized pieces, and deliver functionality as early as possible.
109. 团队发现了一个突破性产品，而尽早的市场交付对于该产品至关重要。这项工作被分解为首先构建框架，然后添加功能。团队决定使用为期三周的 sprint 构建框架，然后切换到为期两周的 sprint 添加功能。团队和管理层应该怎么做？
- A. 将 sprint 周期调整到正确的工作大小。
B. 创建持续时间相同的 sprint，分解工作。即使未能达到完成标准，并且由于已知且已包含相关风险而给予例外。
C. 同时对框架和功能开展工作，让 sprint 具有相同的持续时间。
D. 重新审视产品愿景和路线图，将工作分解成几乎相同大小的部分，尽可能早地交付功能。

110. User stories have been assigned for development in the next iteration, and offline and online information radiators show the status information. The marketing team, planning on making a launch announcement at a global event being held in six months ask the product owner for go-live date. What should the product owner do?

- A. Provide an updated roadmap with a set target launch date.
- B. Provide a roadmap and detailed iteration plans for the next six months.
- C. Create a new plan from the target launch date.
- D. Provide an estimated go-live date based on current iteration velocity.

110. 用户故事已经分配在下一次迭代中开发，而离线和在线信息发射源显示状态信息。营销团队计划在六个月内举行的全球性活动中进行发布公告，要求产品负责人提供上线日期。产品负责人应该怎么做？

- A. 提供更更新的路线图，并设定目标发布日期。
- B. 提供未来六个月的路线图和详细的迭代计划。
- C. 从目标发布日期创建一份新的计划。
- D. 根据当前迭代速度提供估算的上线日期。

111. An agile practitioner is concerned about a high-risk portion of a project. The agile practitioner wants to ensure that risk and value are both given priority in the solution. What should the agile practitioner do?

- A. Create four quadrants that show the risk-to-value relationship, and do the high-risk, high-value task first.
- B. Create four quadrants that show the risk-to-value relationship, and do the high-risk, low-value task second.
- C. Use an information radiator, and have the development team focus on the highest risk development matter.
- D. Use a fishbone diagram to see the relationship between schedule, cost, and functionality risks.

111. 敏捷管理专业人士对项目中的高风险部分感到担忧，敏捷管理专业人士希望确保风险和价值都在解决方案中设立优先级。敏捷管理专业人士应该怎么做？

- A. 创建四个象限，显示风险与价值的关系，首先执行高风险、高价值的任务。
- B. 创建四个象限，显示风险与价值的关系，首先执行高风险、低价值的任务。
- C. 使用信息发射源，并让开发团队专注于具有最高风险的开发事项。
- D. 使用鱼骨图查看进度计划、成本和功能性风险之间的关系。

112. The development team expressed concerns regarding the number of emails and calls they are receiving from company executives about the recent launch of a product. What should the scrum master do?

- A. Inform the development team that they should ignore the phone calls and emails.
- B. Work with the product owner to re-direct the executives' inquiries.
- C. Ask the product owner to enter the requests into the product backlog as high priority.
- D. Ask the scrum master to enter the requests into product backlog as high priority.

112. 最近，开发团队对从公司主管处收到有关产品发布的电子邮件和电话数量表示担忧。Scrum 主管应该怎么做？

- A. 通知开发团队忽略电话和电子邮件。

-
- B. 与产品负责人一起，转达主管的问询。
 - C. 让产品负责人将这些请求作为高优先级录入产品待办事项中。
 - D. 让 scrum 主管将这些请求作为高优先级录入产品待办事项中。

113. During planning for an agile project, a new stakeholder is engaged who proposes changes to the original requirements. What should the agile project manager do to ensure successful project completion?

- A. Have the team analyze the impact of the changes and update the stakeholders.
- B. Provide stakeholders with updated reports and conduct daily stand ups.
- C. Post information radiators in prominent places and regularly send risk burn down charts to the stakeholders.
- D. Compel stakeholders to attend risk response meetings and conduct daily stand ups to discuss changing priorities and risks.

113. 在规划一个敏捷项目期间，一个新的干系人参与，提出变更原始需求。为确保项目成功完成。敏捷项目经理应该怎么做？

- A. 让团队分析这些变更的影响并让该干系人更新该信息。
- B. 向干系人提供更新的报告，并召开每日站会。
- C. 在显眼的地方发布信息发射源，并定期向该干系人发送风险燃尽图。
- D. 强迫干系人参加风险应对会议，并召开每日站会，讨论变更优先级和风险。

114. During a project retrospective, an agile team provided feedback that the learning curve was high. The team spent extra effort learning new technologies, troubleshooting and resolving issues related to the new technologies. Since the organization anticipates similar projects in the future, what should the team suggest to management?

- A. Assigning the same team to similar projects since the team has acquired the required skill sets.
- B. Arranging knowledge-sharing sessions with other teams.
- C. Using pair programming to assist with learning new technologies.
- D. Encouraging new team members to learn new technologies and adding it to the project schedule.

114. 在项目回顾会议上，敏捷团队提供了学习曲线很高的反馈。团队花费额外的精力学习新技术。排除故障并解决与新技术相关的问题。组织预期今后有类似项目，团队应该向管理层提出什么建议？

- A. 将同一团队分配到类似项目，因为团队已经获得所需的技能。
- B. 安排与其他团队的知识交流会。
- C. 使用结对编程来协助学习新技术。
- D. 鼓励新团队成员学习新技术，并将其添加到项目进度计划中。

115. A company's CEO and CFO received contradictory information regarding a project's status. What should the agile practitioner do to resolve this?

- A. Ensure that the status is up to date and available.
- B. Add a recurring stakeholder status meeting.
- C. Email both parties a copy of the project burn down chart.
- D. Include a task to generate a weekly executive summary.

115. 一家公司的首席执行官和首席财务官收到关于项目状态的相对矛盾信息。若要解决这个问题，敏捷管理专业人士应该怎么做？

- A. 确保状态更新到最新并可用。
- B. 添加一个定期干系人状态会议。
- C. 向双方发送一份项目燃尽图。
- D. 包含一项任务，生成一份每周执行摘要。

116. Who should remove and document the impediments that emerge during a current sprint?

- A. Project manager
- B. Product owner
- C. Agile team
- D. Scrum master

116. 在当前 sprint 中，谁应该删除和记录出现的障碍？

- A. 项目经理
- B. 产品负责人
- C. 敏捷团队
- D. Scrum 主管

117. An agile team is tasked with external projects that use a waterfall approach with fixed milestones. The team recognizes a misalignment between the misalignment and Their owner on-demand requests for external data information. Multiple dependencies make it impossible to postpone milestones for these waterfall projects. What should the agile team do to resolve this?

- A. Create a visual chart of the external dependencies and keep stakeholders informed the risks.
- B. Maintain an impediments backlog that is visible to all stakeholders and team members.
- C. Collaboratively review the project roadmap with affected stakeholders and adjust it to include external milestones.
- D. Find a solution to mitigate the risk during the upcoming retrospective.

117. 敏捷团队分配有外部项目任务。该项目使用的是具有固定里程碑的瀑布法，团队认识里程碑与他们自己对外部数据信息的按需请求存在偏差。多个依赖关系使得推迟这些瀑布项目的里程碑变得不可能。若要解决这个问题，敏捷团队应该怎么做？

- A. 创建外部依赖关系的可视图表，并让项目干系人了解风险。
- B. 维护一份让所有干系人和团队成员可见的障碍待办列表。
- C. 与受影响的干系人合作审查项目路线图，并对其加以调整，包含外部里程碑。
- D. 在即将召开的回顾会议上找到解决方案以减轻风险。

118. An agile team wants to use a cumulative flow diagram to communicate predictable delivery to stakeholders. What data do they need to effectively use this diagram?

- A. Number of work items in the development feature
- B. Annual number of steps used on the Kanban board
- C. Number of sprints required for development
- D. Work in progress (WIP) limit from the team's Kanban board

118. 敏捷团队希望使用累计流表与干系人沟通可预测的交付。若要有效地利用这个图标，他们需要什么数据？

- A. 开发功能中的工作项数量。
- B. 在 Kanban 板上使用的年度步骤数。
- C. 开发所需的 sprints 数量。
- D. 团队 Kanban 板上正在进行的在制品（WIP）限制。

119. An agile team requires specific, customer-supplied materials to test a functionality. Implementation is complete and ready for deployment, but the customer failed to supply the necessary materials. What should the agile team do?

- A. Deploy the product without testing.
- B. Escalate the issue to the sponsor.
- C. Procure the materials elsewhere to complete testing.
- D. Note the issue in the backlog and communicate the deadline impact to the customer.

119. 敏捷团队需要客户提供的特定材料来测试某个功能。实施已完成并准备好部署，但客户却未能提供必要的材料。敏捷团队应该怎么做？

- A. 在不进行测试的情况下部署产品。
- B. 将该问题上报给项目发起人。
- C. 在其他地方采购材料来完成测试。
- D. 将该问题记录在待办列表中，并向客户沟通对截至日期的影响。

120. A business owner asks an agile practitioner to provide a central place where stakeholders can find information about a project's progress. What should the agile practitioner recommend?

- A. Regular circulation of updated, detailed versions of the project plan
- B. Maintain an online team collaboration site and redirect the business owner to the same
- C. Regular one-on-one meetings with stakeholders
- D. Daily scrum meetings with stakeholders

120. 业务负责人要求敏捷管理专业人士提供一个中心位置，让项目干系人可以查找项目进展的相关信息。敏捷管理专业人士应提供什么建议？

- A. 定期循环更新项目计划的详细版本。
- B. 维护在线团队协作网站，并将业务负责人重新定向到相同的网站。
- C. 与项目干系人定期举行一对一会议。
- D. 与项目干系人举行每日 scrum 会议。

121. How should an agile team use a kanban board?

- A. To escalate issues to the project owner
- B. To work with the team to increase velocity
- C. To share risks with the project manager
- D. To reduce confusion about task ownership

121. 敏捷团队应该如何使用 Kanban 板？

- A. 将问题上报给项目负责人
- B. 与团队合作，提高速度
- C. 与项目经理分享风险

D. 减少有关任务所有权的困惑

122. A project is to be started with a team of nine existing and nine new members. The scrum master feels that the team is too large and wants break it into three teams. The scrum master sets a constraint that each team have an equal number of existing team members for knowledge sharing and experience. What should the scrum master do to accomplish this?

- A. Ask the team members' functional managers for guidance on how to group the team members.
- B. Observe which team members are comfortable working together, then assign accordingly.
- C. Ensure that members begin to self organize as small teams with efficiently distributed skills.
- D Assign team members to their respective teams based on the skills known to the scrum master.

122. 一个项目将由九名现有成员以及九名新成员组成的团队开始。scrum 主管觉得团队太大了,想将其分解成三个团队。scrum 主管设定了一个制约因素,每个团队都拥有相同数量的现有团队成员进行知识和经验分享。若要完成这项工作,scrum 主管应该怎么做?

- A. 向团队成员的职能经理寻求如何给团队成员分组方面的指导。
- B. 观察哪些团队成员在一起感觉比较舒服,然后进行相应的分配。
- C. 保证成员开始自我组织为具有有效技能分布的小团队。
- D. 根据 scrum 主管所了解的技能,将团队成员分配给各自的团队。

123. An agile team is doing increment planning. What should the team do to help align stakeholder expectations and build trust?

- A. Develop and share a lightweight vision statement with the stakeholders.
- B. Create a ranked work list of user stories to implement the solution and add tasks under the user stones.
- C. Create a high-level increment plan and risk bum down chart to show stakeholders that the team is working on the right priorities and risks.
- D. Obtain sign-off on the increment plan by the agile coach to demonstrate that agile practices are being followed.

123. 敏捷团队正在进行增量规划。团队应该做些什么来帮助协调干系人的期望和建立信任?

- A. 制定并与干系人分享轻量级愿景说明书。
- B. 创建用户故事的排序工作列表,实施解决方案,并在用户故事下方添加任务。
- C. 创建粗略的增量计划和风险燃尽图,向干系人展示团队正在处理正确的优先事项和风险。
- D. 获得敏捷教练对增量计划的签署同意,以证明敏捷实践得到遵循。

124. An agile team responsible for maintaining power distribution networks is working application to capture faults and maintenance requests directly from the public in the event of a calamity. The CIO wants regular updates on the projects progress distributed to the entire organization. What should the team use to accomplish this?

- A. Information management meeting
- B. Information radiator
- C. Shared information platform application

D. Project management information system (PMIS)

124. 负责维护电网的敏捷团队正在开发一个应用程序，该应用程序能在灾难发生时直接从公众捕获故障和维护请求。首席信息官希望定期更新分发给整个组织的项目进度。若要完成这项工作，团队应该使用哪一项？

- A. 信息管理会议
- B. 信息发射源
- C. 共享信息平台应用程序
- D. 管理信息系统 (PMIS)

125. A senior team member with siloed knowledge resigns, providing very little notice. As a result, the team experiences bottlenecks. What should the team lead have done to ensure that development was maintained in this scenario?


- A. Merged similar development teams to enhance information sharing
- B. Had the senior team member document their daily processes
- C. cross-trained the team in supplemental skills
- D. Hired temporary staff with the required skill set

125. 一名拥有封闭知识的高级团队成员辞职，提供极少信息。结果，团队经历瓶颈。若要确保在该情景中继续保持开发，团队领导应该事先做什么？

- A. 合并类似的开发团队以加强信息共享
- B. 让高级团队成员记录他们的日常流程
- C. 交叉培训团队的补充技能
- D. 聘请具有所需技能的临时工作人员

126. At the beginning of a project, an agile team should defer which quadrant's features?

- A. 1
- B. 2
- C. 3
- D. 4

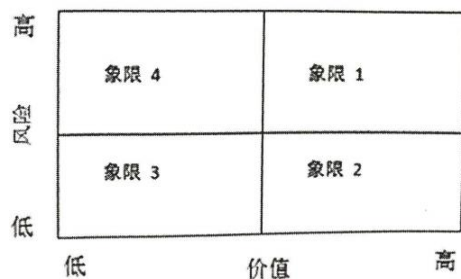

126. 在项目开始时，敏捷团队应该推迟哪个象限的功能？

- A. 1
- B. 2
- C. 3
- D. 4

127. An agile team must hand over the results of each iteration to an external team for testing. The latest results report an increased number of defects. What should the agile team do?

-
- A. Begin testing the product internally to avoid any miscommunication and to identify any lack of resources that the external test team has.
 - B. Ensure that the external test team has the appropriate materials to test the product.
 - C. Investigate the root causes of the reported defects and invite a representative of the external test team to the iteration review and planning meetings.
 - D. Determine if this quality issue is caused by technical debt.

127. 敏捷团队必须将每次迭代的结果移交给外部团队进行测试。最新的结果显示缺陷数量增加。敏捷团队应该怎么做？

- A. 开始在内部测试产品，以避免任何错误沟通，并确定外部测试团队是否缺乏资源。
- B. 确保外部测试团队拥有适当的材料来测试产品。
- C. 调查所报告缺陷的根本原因，并邀请外部测试团队的代表参加迭代审查和规划会议。
- D. 确定这个质量问题是否由技术债务引起的。

128. During a retrospective, an agile team indicates that the iteration velocity forecast was unmet. While 19 points were planned, only 9 were completed. The team believes that 19 points are reasonable for the next iteration, but the practitioner disagrees. The team shares that departmental meetings were a factor at should the agile practitioner do?

- A. Tell the team that the next iteration's velocity estimate should be lowered.
- B. Ask the team to track non-project hours.
- C. Ask the team to work overtime to ensure that estimates are met.
- D. Determine roadblocks that prevented the sprint success and mitigate them.

128. 在回顾会议上，一个敏捷团队表示无法满足迭代速度预测。虽然计划了 19 个点，但仅完成 9 个点。团队认为 19 个点对于下一个迭代是合理的，但是敏捷管理专业人士不同意。团队分享说部门会议是一个影响因素。敏捷管理专业人士应该怎么做？

- A. 告诉团队应降低下一次迭代的速度估算。
- B. 要求团队跟踪非项目时间。
- C. 要求团队加班工作，确保满足估算。
- D. 确定阻止 sprint 成功的障碍，并减轻这些障碍。

129. What describes an agile team that is achieving its highest performance?

- A. Team members understand each other without the need for supervision.
- B. Team members adjust to each other and work as a single unit without the need for supervision.
- C. The team functions as a single unit but needs supervision.
- D. The team is self-managing and focuses its full attention on performance challenges.

129. 下列哪一项描述了一个实现其最高绩效的敏捷团队？

- A. 团队成员在不需要监督的情况下相互理解。
- B. 团队成员相互适应，作为一个独立单元工作，不需要监督。
- C. 团队作为一个独立的单元运转，但需要监督。
- D. 团队自我管理，并将其全部注意力都放在绩效挑战方面。

130. What can an agile team do to avoid shortsightedness in a project?

- A. Expand its practices to include both planning and looking ahead to quickly identify the unknowns.

-
- B. Plan the project with one- or two-week iterations.
 - C. Plan the project and adhere to project timelines.
 - D. Perform long experiments on multiple options to determine if one or more work to its satisfaction.

130. 若要避免项目中的短视问题，敏捷团队能够怎么做？

- A. 扩大其实践，包括规划和展望，快速识别未知事项。
- B. 用一周或两周的迭代规划项目。
- C. 规划项目，并遵守项目时间表。
- D. 对多个方案进行长时间的实验，以确定一个或多个工作是否达到其满意程度。

131. An experienced team member notices that a new team member consistently misses iteration commitments. What should the experienced team member do?

- A. Ask the team member to assign the commitment to the agile practitioner.
- B. Ask the team member's manager to speak with them.
- C. Ask the scrum master to apply pressure on the team member.
- D. During the retrospective, coach the team on how to better estimate.

131. 一名经验丰富的团队成员注意到，一名新团队成员总是不能兑现迭代承诺。该经验丰富的团队成员应该怎么做？

- A. 要求该团队成员将该承诺分配给敏捷管理专业人士。
- B. 要求该团队成员的经理与其谈话。
- C. 要求 scrum 主管对该团队成员施加压力。
- D. 在回顾会议上，教导团队如何更好地估算。

132. For what is the MoSCoW method used?

- A. Tracking progress
- B. Validating a product
- C. Prioritizing stories
- D. Estimating story size

132. MoSCoW 方法的用途是什么？

- A. 跟踪进度
- B. 核实产品
- C. 确定故事的优先级
- D. 估算故事规模

133. During the advanced stages of implementing a complex design, an agile practitioner realizes that the architecture is not scalable for user requirements. The architect suggests a workaround that is minimally adequate, but may cause some performance issues. What should the agile practitioner do?

- A. Calculate the cost of redoing the architecture and seek management approval.
- B. Implement the workaround since performance issues can be addressed in the next iteration.
- C. Brainstorm with the team to identify a solution.
- D. Tell the team that this is unacceptable for the upcoming project.

133. 在实施一个复杂设计的后期阶段，敏捷管理专业人士意识到架构不能满足用户需求。架构师建议一种最小限度的权变措施，但可能会导致一些性能问题。敏捷管理专业人士应该？

-
- A. 计算重建架构的成本，并寻求管理层的批准。
 - B. 实施该权变措施，因为性能问题可以在下一次迭代中解决。
 - C. 与团队头脑风暴确定解决方案。
 - D. 告诉团队，这对于未来的项目是不可接受的。

134. Retrospectives have failed to result in the efficiency improvements anticipated by an agile team lead. What should the team lead do to ensure that retrospectives bring value to the team and project?

- A. Impose tighter retrospective timelines.
- B. Identify the issue that is preventing retrospective findings from being implemented and immediately resolve it.
- C. Coach and remind the team to address retrospective action items.
- D. Ensure that the product owner prioritizes improvements in the next planning session.

134. 回顾会议未能按敏捷团队领导的预期改进效率。若要确保回顾会议为团队和项目带来价值，该团队领导应该怎么做？

- A. 实行更紧凑的回顾会议时间表。
- B. 确定妨碍回顾会议结果得到实施的问题，并立即解决。
- C. 辅导并提醒团队聚焦回顾会议行动项。
- D. 确保产品负责人在下次规划会上对改进进行优先级排序。

135. What should a development team do when they identify significant technical debt during a sprint?

- A. Dedicate the next iteration entirely to technical debt cleanup.
- B. Ask the customer to include incremental technical debt cleanup in future iterations.
- C. Discuss the technical debt in the next retrospective meeting.
- D. Capture the technical debt in the product backlog.

135. 开发团队在一个 sprint 期间识别到重大技术债务时应该怎么做？

- A. 在下次迭代专注于技术债务清理。
- B. 要求客户在未来的迭代中包含增量技术债务清理。
- C. 在下次回顾会议中讨论技术债务。
- D. 在产品待办事项中收集技术债务。

136. An agile coach working with a group of teams observes a dysfunction in the way management measures the teams' productivity. What dysfunction did the agile coach observe?

- A. Management is looking at the teams' burndown charts for all teams displayed on the wall.
- B. Management is looking at the teams' sprint boards to manage the flow of tasks and expose the work in progress (WIP).
- C. Management is insisting that teams add WIP limits so that additional work is not pulled into the WIP State.
- D. Management is comparing velocity across teams and rewarding the team with the highest velocity.

136. 敏捷教练正在与多个团队一起工作，注意到管理层衡量团队生产力的方式存在功能障碍。敏捷教练观察到的功能障碍是什么？

-
- A. 管理展正在查看墙上展示的所有团队的燃尽图。
 - B. 管理层查看的是团队的 sprint 板，来管理任务流以及显示在制品（WIP）。
 - C. 管理层一直让团队添加 WIP 限制，以便额外的工作不会被拉进 WIP 状态中。
 - D. 管理层正在比较团队间的速度，并奖励速度最高的团队。

137. What's the purpose of a Scrum-of-Scrums meeting?

- A. Inform management of project progress.
- B. Bring together all members of all Scrum teams.
- C. Coordinate the work of multiple Scrum teams.
- D. Launch an international Scrum project.

137. Scrum-of-Scrums 会议的目标是什么？

- A. 通知管理层项目进度。
- B. 将所有 Scrum 团队的所有成员集合在一起。
- C. 协调多个 Scrum 团队的工作。
- D. 启动一个国际 Scrum 项目。

138. A project team planned on building a user interface in 10 iterations. The interface was to include five features and have a response time of less than one second for each click. By the end of the tenth sprint, the team developed all five features but failed to meet the response time. What should the team have done to avoid this?

- A. Put measures in place from the first iteration to ensure compliance with the completion criteria
- B. Created a mandate that the product owner be involved in closely managing the team
- C. Conducted a performance review team to remove less-competent team members
- D. Adopted cross-functional development techniques for critical activities

138. 项目团队计划在 10 次迭代中构建用户界面。该界面包括五个功能，每次点击响应时间少于一秒。在第十次 sprint 结束时，团队开发出所有五个功能，但未能满足响应时间。若要避免这种情况，团队事先应该怎么做？

- A. 从第一次迭代就采取措施，确保符合完成标准
- B. 创建产品负责人应密切参与团队管理的委托书(授权书)
- C. 对团队进行绩效审查，开除能力不足的团队成员
- D. 对关键活动采用跨职能开发技术

139. An agile coach is working with a team that serves clients making product requests by phone. During a daily commitment and planning meeting, a team member states that they were unable to resolve a client request because they lacked sufficient product knowledge. What should the agile coach do?

- A. Facilitate a team discussion to identify knowledge gaps and determine the best way to address them.
- B. Provide the team member with training in any lacking areas.
- C. Meet with the team member's line manager to discuss their development plan.
- D. Ask the line manager to assign the team member with the required technical knowledge.

139. 敏捷教练正在与一个团队合作，为通过电话请求产品的客户提供服务。在日常承诺和重新规划会议期间，团队成员表示，由于他们缺乏足够的产品知识，无法解决客户请求。敏捷教练应该怎么做？

-
- A. 促进团队讨论，识别知识差距，并确定解决这些差距的最佳方式。
 - B. 在任何缺乏知识的领域，为团队成员提供培训。
 - C. 与这些团队成员的直线经理开会，讨论他们的培养计划。
 - D. 要求直线经理分配具备所需技术知识的团队成员。

140. During a project meeting, a team is faced with a difficult decision. After discussion and deliberation, the team lead makes the final decision and ends the discussion. This causes a team member to withdraw from future collaboration. What should the team lead have done to prevent this?

- A. Iterated the need for agile teams to make quick decisions, then followed up with that team member
- B. Empowered a team member to facilitate the decision-making process, then made a final decision on behalf of the team
- C. Refrained from participating in the team's decision-making process
- D. Established agile-based ground rules prior to team meetings

140. 在项目会议期间，团队面临一个困难的决策。经过讨论和审议，团队领导作出最终决策，并结束讨论。这导致一名团队成员退出未来的合作。若要避免这种情况，团队领导事先应该怎么做？

- A. 重申敏捷团队需要做出快速决策，然后与该团队成员跟进
- B. 授权一名团队成员推进决策过程，然后代表团队做出最终决策
- C. 不参与团队的决策过程
- D. 在团队会议之前制定基于敏捷的基本规则

141. A project has several features that will deliver immediate customer value. The product owner needs to determine which features to include in the upcoming iteration. What should the product owner have the customer review and approve?

- A. Comprehensive schedule of immediate deliverables
- B. Description of all features' functions and an estimate of their cost
- C. Priority list of desired features and functions
- D. Work breakdown structure (WBS)

141. 一个项目有几个功能可以立即为客户提供价值。产品负责人需要确定要在即将到来的迭代中包含哪些功能。产品负责人需要客户审查和批准什么内容？

- A. 立即可交付成果的综合进度计划
- B. 所有特征的功能描述和成本估算
- C. 所需特征和功能的优先级列表
- D. 工作分解结构（WBS）

142. A company begins practicing agile to enable better access to global customers and the marketplace. During the transition, many teams straggle with the changes, which affects morale. What should an agile coach do to cultivate the best use of agile practices and enable high performance?

- A. Meet individually with team members to provide them with a big picture of the project and its benefits to the organization.
- B. Work closely with teams and their managers to identify and resolve issues through coaching, mentoring, teaching, and facilitation.

C. Coach only at the team level, providing information on expectations, and helping individuals through upskilling.

D. Obtain stakeholder feedback on team effectiveness and share it with the team.

142. 一家公司开始实行敏捷实践，以便更好地接触全球客户和市场。在过渡期间，很多团队都在与这个变化做斗争，因此影响士气。敏捷教练应该怎样做才能最好地利用敏捷实践并实现高绩效？

A. 与团队成员单独开会，为他们提供项目及其对组织带来好处的一个大蓝图。

B. 与团队及其经理紧密合作，通过辅导、指导、教学和推进来识别和解决问题。

C. 仅在团队层面教导，提供有关期望的信息，并帮助个人提升技能。

D. 获得干系人对团队有效性的反馈，并与团队分享。

143. The team's only testing environment is unavailable and development work cannot be tested. The only expert who can fix it is out sick for at least a week. What should the agile team do?

A. Seek an exception to the definition of done, communicate that work will be tested during the next sprint, and move on.

B. Escalate the issue to management for a resolution.

C. Immediately collaborate to get the test environment working again and communicate the status to the stakeholders.

D. Call the expert who is out sick to see if they can resolve the issue.

143. 团队唯一的测试环境不可用，开发工作无法进行测试。唯一可以解决这个问题的专家至少要请一周病假。敏捷团队应该怎么做？

A. 寻找“已完成”定义的例外情况，沟通在下一次 sprint 期间将测试工作，并继续推进。

B. 将问题上报给管理层解决。

C. 立即合作，令测试环境恢复工作，并向干系人沟通状态。

D. 打电话给生病的专家，看看他能否解决问题。

144. An agile team is behind schedule on the current iteration. What should the team do?

A. Agree to work extended hours and weekends to make up the lag in the current iteration.

B. Complete whatever scope is possible, and hold a retrospective to obtain lessons learned.

C. Request additional resources to make up the lag.

D. Reduce the current iteration's scope.

144. 敏捷团队在当前迭代中落后于进度计划。团队应该怎么做？

A. 同意延长工作时间和周末工作，弥补当前迭代中的时间滞后量。

B. 完成任何可能的范围，并召开回顾会议，获得经验教训。

C. 请求额外的资源来弥补时间滞后量。

D. 减少当前迭代的范围。

145. A senior developer on an agile team is only motivated by learning new technologies and processes. However, the current project does not require any new skills. The agile team lead notices that the senior developer is demotivated and spending excessive time complaining about the project, the client, and other team members. What should the agile team lead do?

-
- A. Recommend that the senior developer be assigned to a more challenging project.
 - B. Ask the senior developer to start working toward a new certification.
 - C. Ask the senior developer to utilize a complex tool to develop code more efficiently.
 - D. Suggest that the senior developer mentor junior developers on the team.

145. 敏捷团队的高级开发人员只能通过学习新技术和新流程的方式激励。但是，目前的项目需要任何新技能。敏捷团队领导注意到，高级开发人员变得很消极，花大量时间抱怨项目、客户和其他团队成员。敏捷团队领导应该怎么做？

- A. 建议将高级开发人员分配到一个更具挑战性的项目。
- B. 要求高级开发人员开始为新的认证工作。
- C. 要求高级开发人员利用复杂的工具来更有效地开发代码。
- D. 建议高级开发人员指导团队的初级开发人员。

146. Due to business demands, a project's goals and requirements change. How can new stakeholders become engaged with these changes?

- A. Ask the product owner to lead frequent meetings about the product's vision with the new stakeholders.
- B. Continuously refine the stakeholder register to incorporate new stakeholders and engage them frequently.
- C. Invite new stakeholders to iteration planning meetings.
- D. Invite new stakeholders to stand up meetings.

146. 由于业务需求，项目的目标和需求发生变化。新的干系人如何能够参与到这些变化中？

- A. 要求产品负责人与新的干系人频繁地召开与产品愿景相关的会议。
- B. 持续更新干系人登记册，包含新的干系人并让他们经常参与。
- C. 邀请新的干系人参加迭代规划会议。
- D. 邀请新的干系人参加每日站会。

147. An agile team must develop an innovative mobile customer app for a company that wants to beat competitors to the marketplace. The agile team lead needs to create a plan and communicate it to stakeholders. What should the agile team lead do?

- A. Create a low-level outline that includes feature itemization, task development, task estimates, and project milestones.
- B. Ask the development team to perform a one-sprint technical spike to determine the project's feasibility.
- C. Ask the business owner to add or remove features based on business value.
- D. Develop a high-level outline for features that can be added in future releases.

147. 敏捷团队必须为公司开发一个创新的移动客户应用程序以击败市场竞争对手。敏捷团队领导需要制定一份计划并将其传达给项目干系人。敏捷团队领导应该怎么做？

- A. 创建一个详细大纲，包含功能项目化、任务开发、任务估算和项目里程碑。
- B. 要求开发团队执行一次 sprint 的技术“刺探”，以确定项目的可行性。
- C. 要求业务负责人根据业务价值添加或删除功能。
- D. 为未来版本中可以添加的功能制定概要大纲。

148. A new agile team lead habitually becomes involved in the work from a support perspective, and uses information radiators to ensure that all actions to remove impediments are visible to the go team. What is the agile team lead doing?

-
- A. Adopting the practice of receiving feedback that will facilitate team improvement
 - B. Practicing the servant leadership style of working with an agile team
 - C. Building a collaborative team work culture
 - D. Following a participatory decision-making model

148. 一名新的敏捷团队领导从支持角度习惯性地参与工作，并使用信息发射源来确保所有行动，消除对团队可见的障碍。敏捷团队领导正在做什么？

- A. 采用接收反馈的做法，促进团队改进
- B. 实行与敏捷团队合作的仆人式领导风格
- C. 建立协作式团队工作文化
- D. 遵循参与性决策模型

149. An agile team has a pre-developed plan to work on three-week sprints on a regular cadence. The stakeholders are invited to review progress after every two sprints. How should the product owner ensure that the team is delivering value to the customer?

- A. Have the team continue to work according to the pre-developed plan
- B. Ensure that artifacts produced to deliver features remain valuable for the next iteration.
- C. Ask the customer to continuously prioritize and validate the backlog.
- D. Ask the customer to regularly create and validate backlog items.

149. 敏捷团队有一个预先制定的计划，以固定节奏为为期三周的 sprint 工作。每两次 sprint 后，邀请干系人审查进展情况。产品负责人应如何确保团队为客户提供价值？

- A. 让团队继续按照预先制定的计划工作。
- B. 确保为交付功能而生产的工件对下一次迭代仍有价值。
- C. 要求客户继续确定优先级并确认待办列表。
- D. 要求客户定期创建并确认待办列表事项。

150. A project's product owner asks the scrum master to facilitate the estimation activity. The scrum master then meets with the team and the product owner to clarify the user stories. Following the meeting, the team assembles and provides individual user-story estimates. What technique did the team use?

- A. Planning poker
- B. Wideband Delphi
- C. Formal point counting
- D. Lessons learned

150. 项目的产品负责人要求 scrum 主管推进估算活动。然后，scrum 主管与团队和产品负责人开会，澄清用户故事。会后，团队收集并提供个人用户故事估算。团队采用的是什么方法？

- A. 计划扑克
- B. 宽带德尔菲法
- C. 正式点计数法
- D. 经验教训

151. What should a scrum master do when an agile team member is behind on their tasks?

- A. Move the tasks to another team member who has spare capacity in the sprint.
- B. Ask the team for suggestions.
- C. Hold a one-on-one meeting to encourage the team member to meet task commitments.

D. Inform key stakeholders.

151. 一名敏捷团队成员的任务落后时，Scrum 主管应该怎么做？

- A. 将任务移交给在 sprint 中有余力的另一名团队成员。
- B. 让团队提供建议。
- C. 召开一对一会议，鼓励该团队成员履行任务承诺。
- D. 通知关键项目干系人。

152. A team member located outside of the country recommends a new, web-based conferencing application that will improve communication at no extra cost. The local team objects to the application and prefers to meet face-to-face. What should the agile practitioner do?

- A. Encourage the team to experiment with the new application and then re-evaluate it.
- B. Explain that the new application is not approved by all team members and discuss alternative solutions.
- C. Determine what application is best for the team.
- D. Ask the product owner to decide what application is best for the team.

152. 一名位于国外的团队成员推荐一种新的、基于网络的会议应用程序，将在不产生额外成本的情况下改善通信。但本地团队反对应用程序，并倾向于面对面会议。敏捷管理专业人士应该怎么做？

- A. 鼓励团队尝试新的应用程序，然后重新评估该应用程序。
- B. 解释新的应用程序未被所有团队成员批准并讨论替代解决方案。
- C. 确定什么应用程序最适合团队。
- D. 要求产品负责人决定哪个应用程序最适合团队。

153. What can agile teams use to assure customers that they are progressing toward achieving the goals of a product release?

- A. Burn up and burn down charts
- B. General progress status report
- C. Requirements analysis report
- D. Retrospective chart

153. 敏捷团队可以使用什么向客户保证，他们正朝着实现产品发布目标前进？

- A. 燃起图和燃尽图
- B. 一般进度状态报告
- C. 需求分析报告
- D. 回顾图表

154. What should an agile project manager provide to motivate a team?

- A. An environment that gives members the freedom to focus on work in which they are personally interested
- B. An environment in which team members can find their own motivation
- C. Rewards and appraisals
- D. More vacation time and stock options

154. 敏捷项目经理应该提供什么来激励团队？

- A. 让团队成员能自由专注于他们个人感兴趣的工作环境
- B. 团队成员可以找到自身动力的环境

-
- C. 奖励和评估
 - D. 更多休假时间和股票期权

155. An agile project team is creating a project's release plan. What information should the release plan include?

- A. A sequence of detailed activities that will be carried out to complete each task or story.
- B. Developers' high-level tasks that indicate on which user stories they need to work.
- C. A detailed view and estimates and acceptance criteria for stories that are to be developed in a particular release.
- D. A high-level view and expectations about what is likely to be developed and in what timeframe.

155. 敏捷项目团队正在创建一个项目的发布计划。发布计划应包含哪些信息？

- A. 为完成每个任务或故事而将执行的一系列详细活动。
- B. 开发人员的概要任务，指出他们需要工作的用户故事。
- C. 需要在特定版本中开发的故事详细视图、估算和验收标准。
- D. 对可能开发什么以及在什么时间范围开发的粗略视图和期望。

156. An agile team, using scrum methodology, finds new risks. When should these risks have been identified?

- A. During any planning meeting
- B. In the retrospective meeting
- C. During the daily stand up meeting
- D. In the sprint planning meeting

156. 敏捷团队使用 scrum 方法发现了一些新风险。应在何时识别这些风险？

- A. 在任何规划会议上
- B. 在回顾会议上
- C. 在每日站会上
- D. 在 sprint 规划会议上

157. During the iteration to deliver a product's features, a stakeholder asks for a new feature that was not included in the planned scope of work. The stakeholder threatens to escalate the issue to senior management if this new feature is not included in the current iteration. What should the agile practitioner do to resolve this?

- A. Meet with the stakeholder to discuss implementing only part of the new feature now.
- B. Collaborate with the team and product owner to reprioritize the new feature.
- C. Ask the stakeholder to obtain approval from senior management.
- D. Request guidance from senior management.

157. 在交付某个产品功能的迭代过程中，干系人要求提供不包含在计划工作范围内的一项新功能。该干系人威胁说，如果该新功能未包含在当前迭代中，将会把问题升级上报给高级管理层。若要解决这个问题，敏捷管理专业人士应该怎么做？

- A. 与该项目干系人开会，讨论现在仅实施部分新功能。
- B. 与团队和产品负责人合作，重新确定此新功能的优先级。
- C. 要求该项目干系人获得高级管理层的批准。
- D. 向高级管理层请求指导。

158. An engineering organization is changing its project management approach to agile. what's the best method to win that transition?

- A. Team managers monitor their team's progress on a daily basis.
- B. A senior executive in charge of leading the transition.
- C. A quick transition and start using Agile across all projects.
- D. Documents issued by the CEO to shift to Agile in all projects.

158. 一个工程机构将其项目管理方法改为敏捷。那么实现这种转变的最佳方式是？

- A. 让团队经理每天监控其团队进度。
- B. 让一个高级主管负责领导这次转变。
- C. 快速过渡，开始在所有项目中使用敏捷。
- D. 由 CEO 颁布在所有项目中转向敏捷的文件。

159. An agile team wants to collectively determine a project's likely size. What will the team be doing if they use the planning poker technique to accomplish this?

- A. Estimating the relative size of stories by using story points
- B. Estimating stories by placing them in buckets
- C. Estimating story points by comparing them to similar, past features
- D. Using the number of dots for votes to estimate story points

159. 敏捷团队希望集体决定项目的可能规模。如果他们使用计划扑克技术来完成这项工作，那么团队将会做什么？

- A. 通过使用故事点估算故事的相对规模
- B. 通过将其粗略归类来估算故事
- C. 通过将其与过去类似功能进行对比来估算故事点
- D. 使用点数来估算故事点

160. During which meeting should an agile practitioner work with the team to share information about tasks, stories, and commitments?

- A. Stakeholder priority
- B. Project status
- C. Sprint retrospective
- D. Stand up

160. 哪次会议期间，敏捷管理专业人士应与团队合作，分享任务、故事和承诺相关的信息？

- A. 干系人优先级会议
- B. 项目状态会议
- C. Sprint 回顾会议
- D. 站会

161. An executive wants to know a project's progress at the end of every sprint. The scrum master agrees to the request, and shares the appropriate agile metric to cover the project's progress and scope. What is the best artifact to be shared?

- A. Product backlog
- B. Velocity chart
- C. Sprint burndown chart
- D. Release burndown chart

161. 每次 sprint 结束时，一名高管想知道项目的进展情况。Scrum 主管同意该请求，并分享适当的敏捷测量指标来涵盖项目的进展情况和范围。需要分享的最佳产物是什么？

- A. 产品待办事项
- B. 速度图
- C. Sprint 燃尽图
- D. 发布燃起图

162. The product owner is creating a product roadmap for the next 5 years and includes one product release per year. The product owner wants detailed estimates for the first year so that better external commitments can be made. What should the product owner do?

- A. Ask the team to break down the backlog and estimate for the next 3 releases.
- B. Work with the team to create a high level estimate beyond the first release.
- C. Ask the team for a detailed breakdown of the next iteration and high level estimates for the remaining duration.
- D. Ask the team to break down the first 3 releases and remove or add estimates as time progresses.

162. 产品负责人正在为未来 5 年制定产品路线图，包括每年发布一个产品。产品负责人希望详细估算第一年，以便能够做出更好的外部承诺。产品负责人应该怎么做？

- A. 要求团队分解待办列表并估算后面 3 次发布。
- B. 与团队合作，创建第一次发布之外的粗略估算。
- C. 要求团队详细分解下一次迭代和剩余持续实践的粗略估算。
- D. 要求团队分解前 3 次发布，并随着时间的推移删除或添加估算。

163. What should a manager do to facilitate successful communication among members of a virtual, cross-functional team located in multiple geographic areas?

- A. Break down deliverables based on geographic locations to avoid communication difficulties.
- B. Encourage team members to adjust working hours agilely due to time-zone differences.
- C. Ask each team member to send out daily emails with updated work plans.
- D. Ask the team to use a Kanban board for transparency of development features.

163. 一个虚拟的跨职能团队成员位于多个地理区域，管理者应如何促进他们间的成功沟通？

- A. 根据地理位置拆分可交付成果，避免沟通困难。
- B. 由于时差不同，鼓励团队成员敏捷地调整工作时间。
- C. 要求每名团队成员发送每日电子邮件，并附上更新的工作计划。
- D. 要求团队使用 Kanban 板来实现开发功能的透明度。

164. The development team expressed concerns regarding the number of emails and calls they are receiving from company executives about the recent launch of a product. What should the scrum master do?

- A. Inform the development team that they should ignore the phone calls and emails.
- B. Work with the product owner to re-direct the executives' inquiries.
- C. Ask the product owner to enter the requests into the product backlog as high priority.
- D. Ask the scrum master to enter the requests into the product backlog as high priority.

164. 最近, 开发团队对从公司主管处收到有关产品发布的电子邮件和电话数量表示担忧。scrum 主管应该怎么做?

- A. 通知开发团队忽略电话和电子邮件。
- B. 与产品负责人一起, 转达主管的问询。
- C. 让产品负责人将这些请求作为高优先级录入产品待办事项中。
- D. 让 scrum 主管将这些请求作为高优先级录入产品待办事项中。

165. Based on the chart, if team velocity is 15, how many iterations will be needed to complete all stories?

- A. 3
- B. 4
- C. 5
- D. 7

165. 根据图表, 如果团队的速度为 15, 需要多少次迭代来完成所有故事?

故事	故事点
A	12
B	10
C	10
D	9
E	11
F	9
G	12

- A. 3
- B. 4
- C. 5
- D. 7

166. An agile practitioner is concerned about a high-risk portion of a project. The agile practitioner wants to ensure that risk and value are both given priority in the solution. What should the agile practitioner do?

- A. Create four quadrants that show the risk-to-value relationship, and do the high-risk, high-value task first.
- B. Create four quadrants that show the risk-to-value relationship, and do the high-risk, low-value task second.
- C. Use an information radiator, and have the development team focus on the highest risk development items.
- D. Use a fishbone diagram to see the relationship between schedule, cost, and functionality risks.

166. 敏捷管理专业人士对项目中的高风险部分感到担忧。敏捷管理专业人士希望确保风险和价值都在解决方案中设立优先级。敏捷管理专业人士应该怎么做?

- A. 创建四个象限, 显示风险与价值的关系, 首先执行高风险、高价值的任务。
- B. 创建四个象限, 显示不风险与价值的关系, 其次执行高风险、低价值的任务。
- C. 使用信息发射源, 并让开发团队专注于具有最高风险的开发事项。
- D. 使用鱼骨图查看进度计划、成本和功能性风险之间的关系。

167. An agile team needs to identify the possible causes of an issue they are experiencing in a current project. What should the agile team do?

- A. Develop a spike
- B. Create an ishikawa diagram.
- C. Perform a pre-mortem analysis.
- D. Complete a variance and trend analysis.

167. 敏捷团队需要识别当前项目中遇到问题的可能原因。敏捷团队应该怎么做？

- A. 开发一个探测
- B. 创建石川图
- C. 执行事前分析
- D. 完成偏差和趋势分析

168. A company has recently adopted agile practices and team members are feeling the transition effect. What should an agile coach do to ensure stakeholders and managers accept agile?

- A. Let upcoming sprints illustrate agile concepts.
- B. Establish close working relationships and identify opportunities for training.
- C. Conduct a meeting to describe the agile process.
- D. Let the first project release serve as an example of increased productivity.

168. 一家公司最近采用敏捷实践，团队成员感受了转型影响。若要确保项目干系人 and 管理人员接受敏捷实践，敏捷教练应该怎么做？

- A. 用即将到来的 sprint 说明敏捷概念。
- B. 建立密切的工作关系并确定培训机会。
- C. 召开会议来描述敏捷过程。
- D. 让第一次项目发布作为提高生产力的一个例子。

169. An agile team is estimating an upcoming sprint. For a two-hour pair programming activity, what are the ideal hours that should be planned?

- A. Two hours -two hours for a developer and zero hours for a reviewer.
- B. Three hours-two hours for a developer and one hour for a reviewer.
- C. Four hours-two hours each for a developer and a reviewer.
- D. Five hours-two hours for a developer, two hours for a reviewer, and one hour for integration.

169. 敏捷团队正在估算一个即将进行的 sprint。为了进行两小时的结对编程活动，应该计划多长的理想时间？

- A. 两小时-开发人员两小时，审查员零小时。
- B. 三小时-开发人员两小时，审查员一小时。
- C. 四小时-开发人员和审查员各两小时。
- D. 五小时-开发人员两小时，审查员两小时，还有一小时用于集成。

170. Following a sprint review, the product owner expresses dissatisfaction with a feature and asks that several new requirements be considered. What should the team do when conducting a detailed analysis in subsequent sprints?

- A. Complete a root cause analysis.
- B. Define “done” by detailing acceptance criteria.

-
- C. Improve triangulation when estimating user stories.
 - D. Perform a kano analysis.

170. 在 sprint 评审会后，产品负责人对某项功能表示不满，并要求考虑几项新需求。在对后续 sprint 执行详细分析时，团队应该怎么做？

- A. 完成根本原因分析。
- B. 通过细化验收标准来定义“已完成”。
- C. 估算用户故事时，改善三角测量。
- D. 执行卡诺分析。

171. When considering impact on a project, to whom should an agile project manager give top priority on the stakeholder list?

- A. The stakeholder who can prevent the project from achieving its goals
- B. The stakeholder who can delay the project
- C. The stakeholder who can prevent the project from delivering within budget
- D. The stakeholder who can work as a friend and help prepare the stakeholder list

171. 在考虑对项目的影响时，在干系人名单中敏捷项目经理应给予哪位最高优先级？

- A. 能够妨碍项目实现目标的干系人
- B. 能够延迟项目的干系人
- C. 能够妨碍项目按预算交付的干系人
- D. 能够像朋友一样工作并帮助准备干系人名单的干系人

172. A product owner approves five stories presented during a sprint review. The team knows that one story is functionally complete but technically incomplete. What should the team do?

- A. Refrain from mentioning it in the sprint review and continue technical work during the next sprint to maintain velocity.
- B. Raise the issue during the sprint review.
- C. Ignore any incomplete technical work since the story is functionally complete.
- D. During the retrospective, reprimand the developer who worked on this story.

172. 产品负责人批准在 sprint 评审会上提交的五个故事。团队知道其中一个故事功能性完整，但技术上不完整。团队应该怎么做？

- A. 在 sprint 评审会上不提及此事，并在下一次 sprint 期间继续技术工作以保持速度。
- B. 在 sprint 评审会提出该问题。
- C. 由于故事的功能性完整，忽视任何不完整的技术工作。
- D. 在回顾会议上，谴责为这个故事工作的开发人员。

173. An agile team must upgrade a technology which will require at least one sprint to complete. This upgrade is on the impediment list, and all stakeholders are aware of the risk. However, the customer is unwilling to spare one sprint on non-functional development. What should the product owner do?

- A. List the upgrade as high risk and defer it until the end of the project.
- B. Prioritize the upgrade, as accruing technical debt contributes to higher risk in the future.
- C. Schedule the upgrade to occur during a sprint that contains few development tasks.
- D. Cancel the upgrade.

173. 敏捷团队必须升级一项技术，但该技术至少需要一次 sprint 的完成。这项升级出现在障碍清单上，且所有干系人都意识到该风险。但是，客户不愿意在非功能性开发方面进行一次 sprint。产品负责人应该怎么做？

- A. 将这项升级列为高风险，并将其推迟到项目结束。
- B. 确定这项升级的优先级，因为技术债务的积累将导致未来出现更高的风险。
- C. 在包含少量开发任务的 sprint 期间安排执行这项升级。
- D. 取消这项升级。

174. An agile team is midway through planning the development of a new system with an evolving requirement. Team members are experienced in the domain from a similar, past project. What should the agile team do?

- A. Use bottom-up estimating to aggregate lower-level tasks into higher-level tasks.
- B. Follow the extreme programming estimate method by averaging the schedules of the most and least-experienced team members.
- C. Use historical velocity for existing team members, and estimate 50% velocity for new members.
- D. Estimate based on historical data, and improve continuously based on team learning, delivery experience, and stakeholder feedback.

174. 敏捷团队正处于规划一个新系统开发项目中途，该系统的需求不断发生变化。团队成员从过去的一个类似项目中获得该领域的经验。敏捷团队应该怎么做？

- A. 使用自下而上的估算，将较低层级的任务汇集到更高层级的任务中。
- B. 通过将经验最丰富和经验最不丰富团队成员的进度计划平均化，遵循极限编程估算法。
- C. 使用现有团队成员的历史速度，并为新团队成员估算 50% 的速度。
- D. 根据历史数据估算，并根据团队学习、交付经验和项目干系人的反馈不断改进。

175. After submitting a list of project requirements, their expected functionalities, and their value added, the product owner schedules a workshop to develop stories for the next few iterations. What should be the objective for this workshop?

- A. Obtain all requirement specifications before the team begins work.
- B. Define clear acceptance criteria for all requirements.
- C. Complete story point estimation and prioritize it in the backlog.
- D. Create small stories that can be completed in less than one week.

175. 在提交项目需求清单、其预期功能及其附加值后，产品负责人将安排一次研讨会，为下几次迭代开发故事。这个研讨会的目标应是什么？

- A. 在团队开始工作之前获得所有需求规范。
- B. 为所有需求定义明确的验收标准。
- C. 完成故事点估算，并在待办列表中确定其优先级。
- D. 创建可以在一周内完成的小故事。

176. During a review meeting, some agile team members complain that refactoring is needed to more quickly and reliably implement future features. What should the agile team lead do?

- A. Encourage the team to continue the critical analysis of the product's quality in upcoming iterations, and ask the product owner to prioritize a technical user story for refactoring.

-
- B. Ask the team to estimate how long refactoring will take, then ask the product owner to prioritize the stories that will take the least amount of time to refactor.
 - C. Focus on refactoring during the next iteration
 - D. Add refactoring as technical debt to the risk register.

176. 在评审会议期间，一些敏捷团队成员抱怨说，需要重构才能更快速、更可靠地实施未来功能。敏捷团队领导应该怎么做？

- A. 鼓励团队继续对即将到来的迭代中的产品质量执行批判性分析，并要求产品负责人优先考虑重构技术用户故事。
- B. 要求团队估算重构需要多长时间，然后要求产品负责人优先考虑需要最少重构时间的用户故事。
- C. 在下一迭代过程中关注重构。
- D. 将重构作为技术债务添加进风险登记册。

177. Team members complain that the same issues continue to resurface in retrospectives, yet remain unresolved. The team now wants to discontinue retrospectives because they are ineffective. What should the team do?

- A. Conduct retrospectives in alternating sprints.
- B. Generate more insights and use the Fibonacci series to prioritize actions.
- C. Prioritize action items and agree to close a specific number of those items during a sprint.
- D. Make the most experienced team member responsible for ensuring that action items are closed.

177. 团队成员抱怨同样的问题在回顾中继续重现，但仍未得到解决，团队现在希望停止回顾，因为没有效果。团队应该怎么做？

- A. 在交替的 sprint 中进行回顾。
- B. 产生更多见解，并使用斐波纳契数列来确定行动的优先级。
- C. 确定行动项的优先级，并同意在 sprint 期间关闭这些特定数量的事项。
- D. 让最有经验的团队成员负责确保行动项关闭。

178. An agile team is struggling with an issue. A team member mentions that another team had a similar issue that was resolved, but lessons learned documents are unavailable. What should the agile practitioner do?

- A. Encourage the team to independently find a solution.
- B. Work with the team to create a solution for disseminating team knowledge throughout the company.
- C. Suggest that all agile teams share weekly reports on their projects.
- D. Recommend hiring an external expert to advise on the best methods for sharing knowledge among teams.

178. 敏捷团队正在努力解决一个问题。一名团队成员提到另一个团队解决了一个类似问题，但是无法获得经验教训文件。敏捷管理专业人士应该怎么做？

- A. 鼓励团队独立找出解决方案。
- B. 与该团队合作，创建一个在整个公司传播团队知识的解决方案。
- C. 建议所有敏捷团队每周分享他们的项目报告。
- D. 建议聘请外部专家就在团队之间分享知识的最佳方法提供建议。

179. A team member on a feature-driven development team discovers that a missing, fundamental requirement will prevent implementation of the sprint objective. What should the team member do?

- A. Start immediately to execute this requirement.
- B. Postpone the missing requirement until the next sprint.
- C. Create a user story and update the product backlog with the missing requirement.
- D. Modify the current user story to include the missing requirement.

179. 功能驱动型开发团队的一名团队成员发现，缺失的基本需求将妨碍 sprint 目标的实施。该团队成员应该怎么做？

- A. 立即开始此需求的执行。
- B. 将缺失的需求推迟到下一次 sprint。
- C. 创建用户故事并将缺失的需求更新到产品待办列表中。
- D. 修改当前用户故事，包含缺失的需求。

180. A key influence in a company is leading its transformation to agile. What should be developed as part of the shared vision for the new team?

- A. Mission statement
- B. Ground rules and conflict management framework
- C. Detailed process guide, with an organizational structure for issue escalation
- D. Shared values, working rules, and agreements

180. 公司的一名关键者正在领导公司的敏捷转型。应制定哪一项作为新团队共同愿景的组成部分？

- A. 使命宣言
- B. 基本规则和冲突管理框架
- C. 详细的过程指南，以及问题升级上报的组织结构
- D. 共同的价值观、工作规则和协议
